

Anticipatory Action Framework

2024

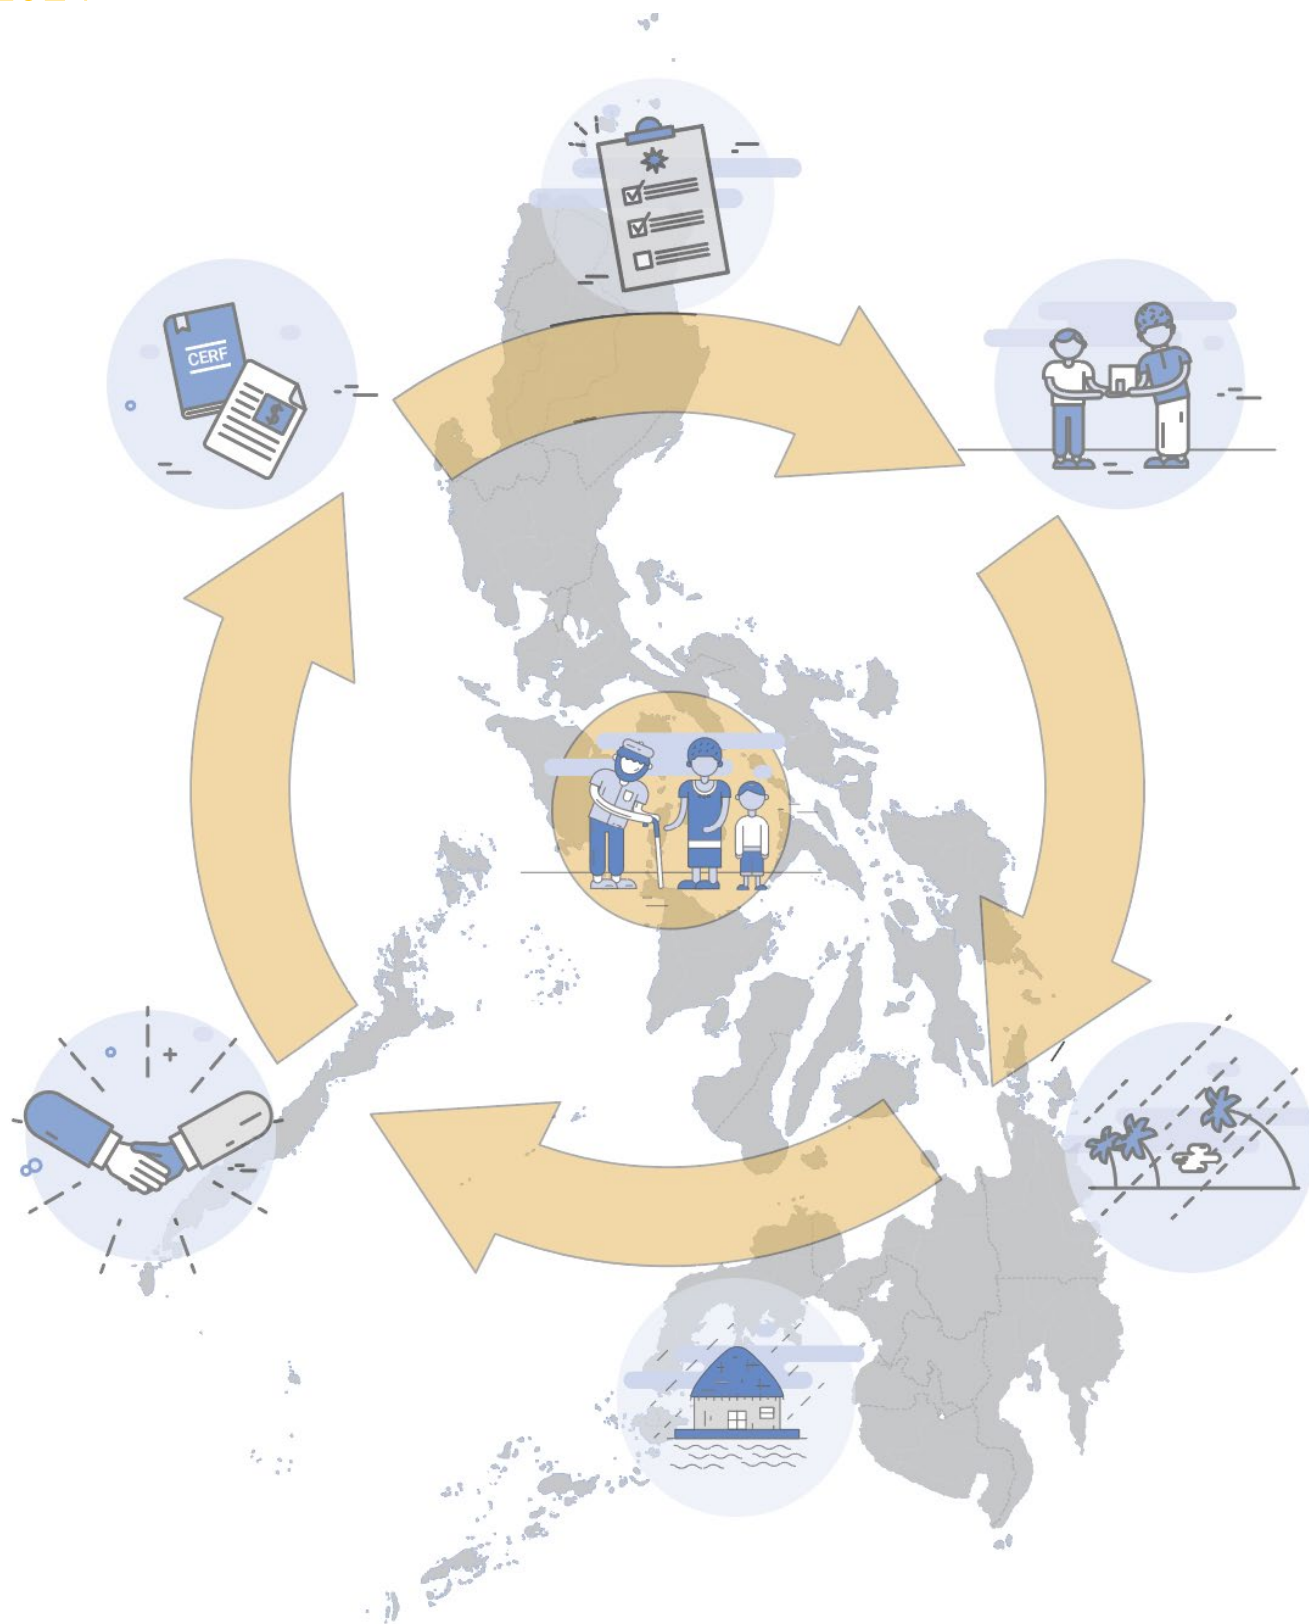


Table of Contents

1. Overview	1
Summary	1
Executive summary	1
2. Introduction	5
Objectives of anticipatory action	5
Core principles	6
Tropical Cyclones in the Philippines	6
Crisis timeline	7
3. Forecast, Scenarios and Triggers	8
Forecasts	8
Scenarios	9
Triggers and thresholds	10
Activation protocol	11
4. Anticipatory Action Plan	15
Overview	15
Approach to targeting at-risk beneficiaries	17
Flagship Initiative Integration	18
Organizational set up of the CERF AA Pilot Framework	20
Partnerships and localization of anticipatory action	21
Operational coordination with local authorities	23
Mandatory pre-emptive evacuation procedure	23
Consultation with communities	23
Ensuring readiness for timely implementation	25
Pre-emptive cash interventions	25
Priority interventions	27
5. Pre-agreed Financing	32
CERF	32
Anticipatory Action Partnership and Funding framework	33
6. Learning	33
Agency-specific M&E	33
Independent Impact Evaluation	Error! Bookmark not defined.
Advocacy and Public Communication	35
7. Annexes	37
Annex 1 - Anticipatory Action: Summary table	37
Annex 2 – DRAFT trigger messages	42
Annex 3 - Evaluation of forecasts for anticipatory actions - April 2021	43
Annex 4: Contact Information	49
Annex 5: Post Distribution Monitoring Indicators	50

1. Overview

Summary

The purpose of this document is to present the framework for anticipatory action (AA) in the Philippines, including the forecasting trigger (the model), the pre-agreed action plans (the delivery) and the pre-arranged financing (the money).

Executive summary

The Framework outlines an approach to a collective anticipatory action delivered at scale as an innovative attempt to pilot typhoon response in the Philippines. The document includes details about the forecasting trigger (the Model), the pre-agreed action plans (the Delivery) and the pre-arranged financing (the Money). As this is a learning pilot an investment will be made in documenting evidence and learning (the Learning). Central Emergency Response Fund (CERF) has allocated \$7.5 million for this pilot in typhoon season 2024.

The objective of the pilot is to mitigate, and to a certain extent prevent, the severe impact of typhoons on people's homes and livelihoods, while building on government's mandatory pre-emptive evacuation procedures that saves lives. With this intervention, the most at-risk communities will have better financial resources to prepare prior to landfall. Multi-sectoral assistance will be delivered by the UN agencies, NGOs and the Red Cross/Red Crescent in close collaboration with local authorities. For example, IOM will provide cash assistance and support vulnerable families in strengthening their houses; FAO's intervention will promote preservation of livelihoods and income by supporting poor farmers and fisherfolks to rent a secure and safe place for their farming and fishing tools and livestock while FAO's multi-purpose cash will support other needs; and WFP's multi-purpose cash will support food and other relevant needs while in evacuation. Anticipatory action interventions will mount a collective humanitarian action at scale to mitigate the impact of a severe typhoon hitting Region 5 (Bicol), Region 8 (Eastern Visayas) and/or Region 13 (Caraga). In March 2022, the AA Core Group conducted an after-action review and recommended a few improvements to the pilot. To extend the geographic coverage of the pilot, two scenarios were developed for the 2022 AA under CERF to cover most vulnerable areas in Region 5, 8 and 13 (Caraga). Scenario 1 covers pilot areas in Region 5 and Samar Island Provinces (Northern Samar/Eastern Samar/Western Samar) in Region 8. Scenario 2 covers Region 13 (Caraga) and Leyte Island provinces in Region 8 (Leyte/Southern Leyte)

The segment-based approach ensures that community perspectives are met and ensures tailored actions for children, adults, elderly, LGBTQIA+, persons with disabilities, and other intersecting factors. The pilot aims to reach about 372,700 people under Scenario 1 and 203,300 people under Scenario 2 with assistance ahead of a typhoon's landfall.

The Model includes a trigger mechanism based on the ECMWF forecast and IFRC/ Netherlands Red Cross 510 probabilistic typhoon impact prediction model developed for the Philippines that is using the ensemble of forecasted tracks and wind speed from high resolution model to predict the impact. The Humanitarian Data Centre will support OCHA and the Triggers group in monitoring the development of tropical cyclones and running a parallel program based on the model developed by NLRC 510.

Each CERF AA Scenario follows a 2-stage trigger activation:

- 1. Readiness trigger (pre-activation): 3-7 days prior to forecast landfall**
 - a. Tropical Cyclone with potential to reach category level 2 or higher (greater than 154 km/h maximum 1-minute sustained wind speed/ 136 km/h maximum 10-minute sustained wind speed).
 - b. Projected to directly impact areas within Region 5, 8 and 13 (Caraga).
- 2. Activation trigger: on or before 72 hrs (3 days) prior to forecast landfall**

- a. As soon as ECMWF forecasts are available for a certain TC, OCHA Philippines together with HDX will calculate the predicted total number of totally damaged buildings using the 510 model, produce an impact map, and update every 6-12 hours.
- b. **Threshold is reached and CERF anticipatory action activated if 72 hours (3 days) before landfall (or sooner)** the predicted number of houses to be totally damaged fall within the range of 50% probability that 50,000 houses will be totally damaged to 85% probability that at least 8,000 houses will be totally damaged.

3. Readiness activation with action activation

- a. The readiness and action activation can be triggered at the same time with a cut-off of 72 hours prior to the tropical cyclones forecast landfall.
- b. Activation trigger can be reached and activated if the estimates on the total number of destroyed houses reaches the thresholds even without readiness trigger activation on or before 72 hours before the tropical cyclones forecast landfall.

The Delivery. In case of sudden-onset disasters such as typhoon response, the delivery of anticipatory action is time critical. For this pilot, anticipatory interventions have been selected to be rooted in the current operating environment and government mandatory evacuation and safety protocols. Consideration is given to the compounding effects of COVID-19, the agency's operational capacity to deliver within the limited time window, the ability to mitigate the impact of typhoon damage, CERF funding priorities addressing protection, lessons learned from the 2021 near activation of the Framework, the 2022 Simulation Exercise, the no regrets approach, and the Enhancing Resilient Communities Flagship Initiative for which the Philippines is one of the four pilot countries¹.

Above all, proposed anticipatory action interventions that save shelter and livelihoods, should not interfere or disincentivize government's pre-emptive interventions that save lives. The contingency of operating in the continued COVID-19 context requires stricter adherence to health protocols in the evacuation centers (ECs), meaning that preparations for mandatory evacuations would commence even earlier.

Given the very short lead times, the following interventions are being proposed under this pilot:

About 55% (scenario 1) or 68% (scenario 2) of the overall CERF anticipatory action pilot budget will be used through cash assistance, both multi-purpose as well as sectoral top-ups. A harmonised, pre-emptive multi-purpose cash (MPC) transfer of US\$60 (PhP 3,300, which includes a 7% forex buffer), or 1/3 of the Minimum Expenditure Basket (MEB) plus transportation costs, to support basic needs for 10 days (3 days prior to and 7 days after landfall) will be delivered by FAO, IOM, UNFPA, and WFP. Partners will reach 74,900 of the most vulnerable households (372,700 beneficiaries) living in prioritized provinces of Region 5 and Region 8 under scenario 1 and 35,300 of the most vulnerable households (203,300 beneficiaries) in Region 8 and Region 13 (Caraga) under scenario 2. The pilot is designed around a two-staged approach to cash distribution. WFP and FAO will trigger cash distributions collected at over-the-counter remittance shops 72 hours before landfall, and IOM and UNFPA will distribute in or close to evacuation centres.

FAO, together with OXFAM and CARE, will work with local communities to rent schools, local community halls, and places of worship to store critical livelihood items, such as boats and nets for fisherfolk or tools and seeds for farmers. By providing safe-storage sites, the intervention will preserve hard-won development gains and key livelihoods for 600 households and most vulnerable farmers and fisherfolks. FAO's MPC will target 15,150 agriculture dependent families, and a further 17,000 agri-households will benefit from messaging and agro-climate advisories. IOM will ensure that evacuees have access to safe and dignified living conditions at the onset of their pre-emptive evacuation by providing modular tents in government-recognized ECs. IOM will also deliver cash for shelter grants totaling PhP 4,400 (\$80), which will facilitate immediate access to appropriate materials and tools for evacuees to repair their shelters right after typhoon's landfall. These interventions will alleviate grave stress from sudden displacement and promote early recovery, thereby contributing to prevention of prolonged displacement and mitigate socio-economic loss from disasters.

UNFPA will ensure that those who are at the highest risk (pregnant and vulnerable women) will be reached with MPC and with sexual and reproductive health and rights (SRHR) and gender-based violence (GBV) / protection commodities and information. The focus will be on ensuring linkage to continuous lifesaving SRHR and GBV services and ensuring the right

¹ For more information on the Flagship initiative in the Philippines, see <https://response.reliefweb.int/philippines/flagship-initiative>.

to dignity guided by the survivor centered approach and protection from sexual exploitation and abuse (PSEA) before, during and after a significant typhoon event.

Promoting shock-responsive social protection, UNICEF will provide unconditional and unrestricted cash transfers as a top-up to beneficiaries of the government's flagship social protection program' (Pantawid Pamilya Pilipino Program, or 4Ps). These top ups are designed to cover the costs of the specific child-centered needs of vulnerable families, across for health, nutrition, WASH, education, and protection; and continued access to time-sensitive services before disruption by the typhoon. The top ups total PhP 1,200 (\$22) per household and will be delivered through Landbank, used for other 4Ps benefits.

FAO, WFP and UNFPA integrated several Flagship initiative approaches in their 2024 anticipatory action projects, building on community-suggested solutions during community consultations. These FI approaches center on the protection of community and household assets via the distribution of community microgrants, also termed Group Cash Transfers (GCT), and the provision of physical safe storage sites

Anticipatory action interventions were developed also in consultation with the ICCG and each cluster, as per the revised HCT Minimum Operations Protocol that incorporates anticipatory action as its standard way of responding to significant typhoons during the 2024 typhoon season.

CERF Anticipatory Action Funding Requirements

Agency	Scenario 1	Scenario 2
IOM	1,717,091	2,722,279
WFP	2,270,954	1,668,876
FAO	1,586,881	323,096
UNICEF	832,319	
UNFPA	675,919	643,327
Total	7,083,164	5,357,578

The Learning.

Independent impact evaluation

Independent evaluation and learning are central to all OCHA-facilitated Anticipatory Action Framework. Evidence on the impact of anticipatory action is essential to mobilize global political and financial support for AA and to further scale up the efforts. Without this, the humanitarian system will struggle to secure investments to protect more people against shocks in more places, as well as crowd in development agencies, International Financial Institutions (IFIs) and governments. In that regard, the learning and evidence generated from Philippines will greatly benefit anticipatory action efforts across the globe.

To maximize the learning from the Philippines pilot in the event of activation, OCHA has partnered with Kobo (an international humanitarian non-profit organization) and researchers at the Harvard Humanitarian Initiative, to design an evaluation of the framework for Tropical Cyclones. The evaluation will measure the impact of AA interventions on households and communities and facilitate the learning from innovative pilots such as community cash grants and safe storage interventions.

Methodological approach

The central objective of the evaluation will be to assess the impact of OCHA-supported anticipatory action programs on the well-being of registered beneficiaries. The evaluation will use a mixed-methods, community-centered approach that primarily focuses on community experiences and perceptions.

The evaluation will focus on four central evaluation questions (EQ) and a number of topics or themes for each:

EQ1: People & community: How do anticipatory actions engage and affect the community members in terms of awareness, preparedness, and overall well-being?

EQ2: Resources & tools: How effective are the resources and tools provided for anticipatory action in preparing the community for, and recovering from, cyclones?

EQ3: Processes & mechanisms: How well do the processes and mechanisms in place support the timely implementation and effectiveness of anticipatory actions?

EQ4: Governance & accountability: How appropriate and effective are the governance and accountability structures in enabling and supporting anticipatory actions?

To get a complete picture of the impact of anticipatory actions by the UN agencies and other partners, survey instruments will be designed to gather the experience of various stakeholders and groups.

An ad hoc M&E group, i.e. the Learning Team, was also established as part of the CERF Philippines Core Group to assess how collective and coordinated early action can work at scale for typhoon response in the Philippines as well as capture and share learning about how to improve the approach to planning and implementation of anticipatory interventions. The group will meet on a needs basis.

Communication activities. The RC/HC and UN agencies and partners agreed to put strong emphasis on communication activities also to ensure communicating as “One UN” and communicating the story before, during, and after the AA response. OCHA prepared an updated operational communications plan for the project in 2024, including key messages, communication activities and approach to communicating impact. The communication plan is being finalized with the 5 UN agencies and will be released separately.

2. Introduction

Objectives of anticipatory action

The possibilities of predicting the occurrence of shocks as well as its humanitarian impact have substantially increased in the last decade, particularly in the case of extreme climate events. By taking this anticipatory approach – using “evidence of risk”, instead of “suffering” – we can today protect better and save more lives, optimize resources and preserve hard-won development gains. This resilience-building thinking has also impacted on the way we plan and organize humanitarian action.

Today, we can predict with increasing confidence the occurrence and humanitarian impact of tropical cyclones. Anticipatory action is envisioned to contribute to building community resilience especially if done alongside climate-smart disaster risk reduction and response efforts. By combining different analytical approaches, out-of-the-ordinary weather events could to an extent be predicted, which would enable their projected impact to be proactively mitigated based on pre-identified anticipatory actions. Building on growing evidence that acting prior to the onset of a predictable hazard is more (cost-)effective than traditional humanitarian response, OCHA has facilitated the setup of an Anticipatory Action Framework for the Philippines with FAO, IOM, UNFPA, UNICEF and WFP being the key UN agencies implementing early action interventions, working closely with Red Cross/Red Crescent, NGO partners as well as local authorities.

An essential aspect of these anticipatory action initiatives is the inclusion of intersectional considerations recognizing that community segments – women, children, youth, elderly, LGBTQIA+, persons with disability, and other vulnerable groups often face disproportionate impacts during a crisis. Building on growing evidence that acting prior to the onset of a predictable hazard is more effective, collective Anticipatory Action Frameworks are being established by CERF and facilitated by OCHA, that also aims to address these disparities by ensuring that early interventions are inclusive and equitable. Each Framework comprises of 3 core elements, all of which are underpinned by a clear learning, monitoring and evaluation plan:

- A robust forecasting embedded in a clear decision-making process (**the model**).
- Pre-agreed action plans that can fundamentally alter the trajectory of the crisis (**the delivery**).
- Pre-arranged finance (**the money**).

Anticipatory action is still an innovative space, requiring “proof of concept”. Thus, in addition to the 3 core elements, an investment in documenting evidence, learning from each framework, ensuring that the approach is improved to meet the needs of all community members effectively, is necessary (**the learning**).



Objectives for the 2024 typhoon season

The objective of the anticipatory action is to mount at scale a collective humanitarian action to mitigate the impact of a severe typhoon hitting Region 5 (Bicol), Region 8 (Eastern Visayas) and Region 13 (Caraga). The pilot will cover most vulnerable communities living in prioritized provinces, with the aim to reach about 372,700 (scenario 1) or 203,300 (scenario 2) people with relief assistance ahead of typhoon landfall. Multi-sectoral assistance will be delivered by the UN agencies, NGOs in close collaboration with local authorities.

Key changes in 2024, compared to the 2023 Framework, are slight decrease of the geographic reach of the pilot area especially with IOM in scenario 1, and the incorporation of lessons learned from the Enhancing Resilient Communities Flagship Initiative.

Core principles

The anticipatory action pilot Framework in the Philippines has been tailored to the local context as well as the RC/HC priorities, which are guiding its design and implementation:

1. The Philippines is not new to anticipatory action and there have been several small-scale activations for typhoons in the past seven years. The pilot needs to learn from the wealth of this experience and good practice while remaining adaptive, focused, practical and pragmatic to be able to activate at scale. It should be activated with 'No regrets' principle in mind.
2. Catalytic funding. As with any CERF project, the pilot should be catalytic in funding and develop complementary projects to leverage additional resources and engage wider humanitarian community in piloting early action approaches.
3. Leverage existing know-how on forecasting and data analytics. The pilot should leverage existing expertise, including local knowledge, in forecast modelling and shock analysis for typhoons in the Philippines.
4. Cost efficiency. The pilot should remain nimble and prove cost-effectiveness of the model ensuring investment go in the hands of the most affected people.
5. Supporting localization. Built on the principle of aid localization, the pilot ensures close collaboration with the government and ownership of national and local authorities. At least 30 per cent of the total allocated amount should go to local NGOs and strategic partners.
6. Integration with the Flagship initiative and promoting accountability to affected population. The pilot embraces community-building approaches, consulting communities throughout the process to understand their preparedness, challenges and coping strategies in times of disasters. Keeping in mind CERF four funding priorities, empowering the most vulnerable and strengthening their resilience, prioritizing intervention that empower women and other marginalized groups.
7. COVID-19 contingency. The pilot will continue to integrate the impact of COVID-19 and other compounding effects.
8. Striving for integration. The pilot design will prevent duplication of coordination mechanisms, ensure utilization of the HCT, ICCG and working groups, and foster linkages with long term programming, including resilience and development initiatives.

Tropical Cyclones in the Philippines

According to the [World Risk Report 2023](#), the Philippines, ranked first among all countries for disaster risks, with index value of 46.8. In 2021, disasters triggered 5.7 million internal displacements, of which storms accounted for 91%. Typhoon Rai, known locally as Odette, led to the largest number of disaster displacements of the year worldwide. Without action, climate change will impose substantial economic and human costs, affecting the poorest households the most. The World Bank estimates that the economic damages due to climate change in the Philippines could reach up to 7.6 percent of GDP by 2030 and 13.6 percent of GDP by 2040, clearly outpacing its growth.


The areas of the Philippines most frequently impacted by tropical cyclones are the provinces along the eastern seaboard, with cyclones frequently make landfall on the islands of Eastern Visayas, Bicol region, northern Luzon and eastern Mindanao. Approximately twenty tropical cyclones enter the Philippine Area of Responsibility (PAR) each year, an average of five of these are potentially destructive. Tropical cyclones with 118 to 220 km/h wind strength or higher have significant impact to lives and properties, including livelihoods and shelter. Tropical cyclones can hit the Philippines any time of the

year, but the months of June to November are the most active and May the least active. Tropical cyclones normally move east to west across the country, heading north or northwest as they exit the PAR. Due to warm coastal waters of the Philippine Sea, exacerbated by climate change warming, rapid intensification ahead of landfall is common. Cyclones usually account for at least 30 per cent of annual rainfall in northern Philippines.

In December 2021, Typhoon Rai swept through southern and central Philippines, bringing torrential rains, violent winds, floods, landslides and storm surges in the Visayas and Mindanao regions. It was characterized as a rapid intensification tropical cyclone as it strengthened from category 2 to category 5 within hours, leaving less time for response preparedness measures to be put in place. While the AA Core Group was initially considering potential activation of the pilot, the forecasting model by 510 was unable to pick up the rapid intensification in the last hours before landfall. Besides, the typhoon hit outside of the 2021 pilot areas. The scale and magnitude of the impact of Typhoon Rai created overwhelming needs, with 12 million people affected and 2.4 million in need of assistance. About 2.1 million houses were either damaged or destroyed and 10.2 million hectares of agricultural crops were destroyed. This was the costliest typhoon that hit the Philippines since Typhoon Haiyan. The HCT mounted a humanitarian response, requesting \$169 million of assistance to support the government response efforts.

Crisis timeline

While the rainy season usually starts in June, the more destructive tropical cyclones tend to hit the landmass later in the year, from September to December.

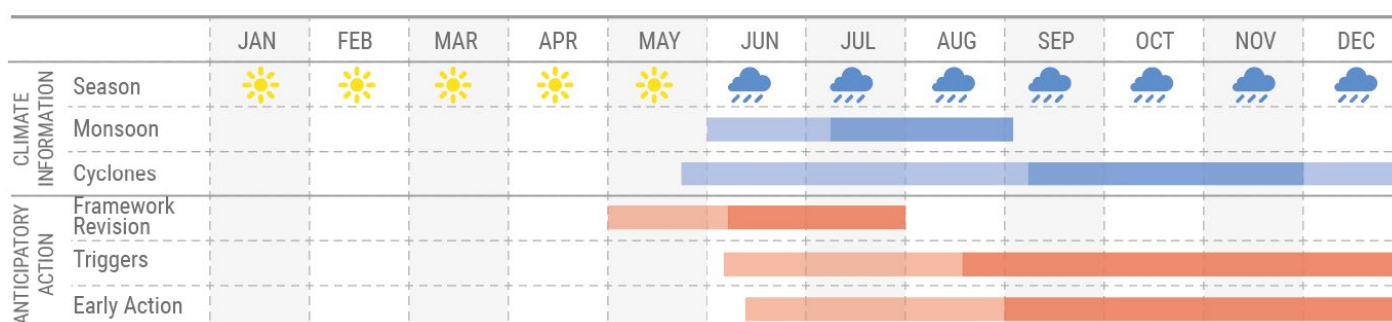

Destructive tropical cyclones cause significant losses to agriculture and damages to infrastructure, particularly, health, schools, houses, markets, water facilities, communication, and have serious humanitarian consequences including loss of livelihoods, reduced income, disruption to continuing education and exacerbation of pre-crisis protection issues, such as GBV.

Embedding anticipatory action in the existing humanitarian coordination mechanisms

To prevent duplication of coordination platforms, the HCT, based on ICCG recommendation, endorsed in May 2021 [a review of the existing HCT Minimum Operations Protocol for Typhoon Response](#) to account for anticipatory action interventions, which will be used at least for the 2021-2022 typhoon season.

Consequently, clusters adjusted their cluster-specific contingency plans and identified the most suitable early action interventions, relying on their technical expertise as well as by consulting with communities and considering various intersectional factors to ensure that anticipatory action are tailored to address the diverse needs of different community segments.

In 2023, the AA Technical Working Group with National Government agencies initiated the creation of a bill to institutionalize AA in the government preparedness and response structure. Through the work and advocacy of the AA TWG, a bill has been passed in the Philippine Congress in February 2024. House bill 9935 and Senate bill 2643 – “*An act institutionalizing a mechanism on the declaration of state of imminent disaster; Providing the criteria for such declaration and lifting; Enabling anticipatory measures and providing funds therefor.*” The bill aims to institutionalize AA into the Philippines preparedness and response framework that would allow government agencies to access funds prior to an imminent disaster.




PHILIPPINES

Humanitarian Country Team Minimum Operations Protocol for Tropical Cyclone

As of 18 July 2024

Immediate actions undertaken by the Humanitarian Country Team (HCT) and Inter-cluster Coordination Group (ICCG) during a tropical cyclone event identified to have a potential significant humanitarian impact on any part of the country. Anticipatory Actions (AA) are considered as part of the Pilot Anticipatory Action implementation in the Philippines focusing on Bicol, Eastern Visayas and Caraga for 2024 typhoon season.

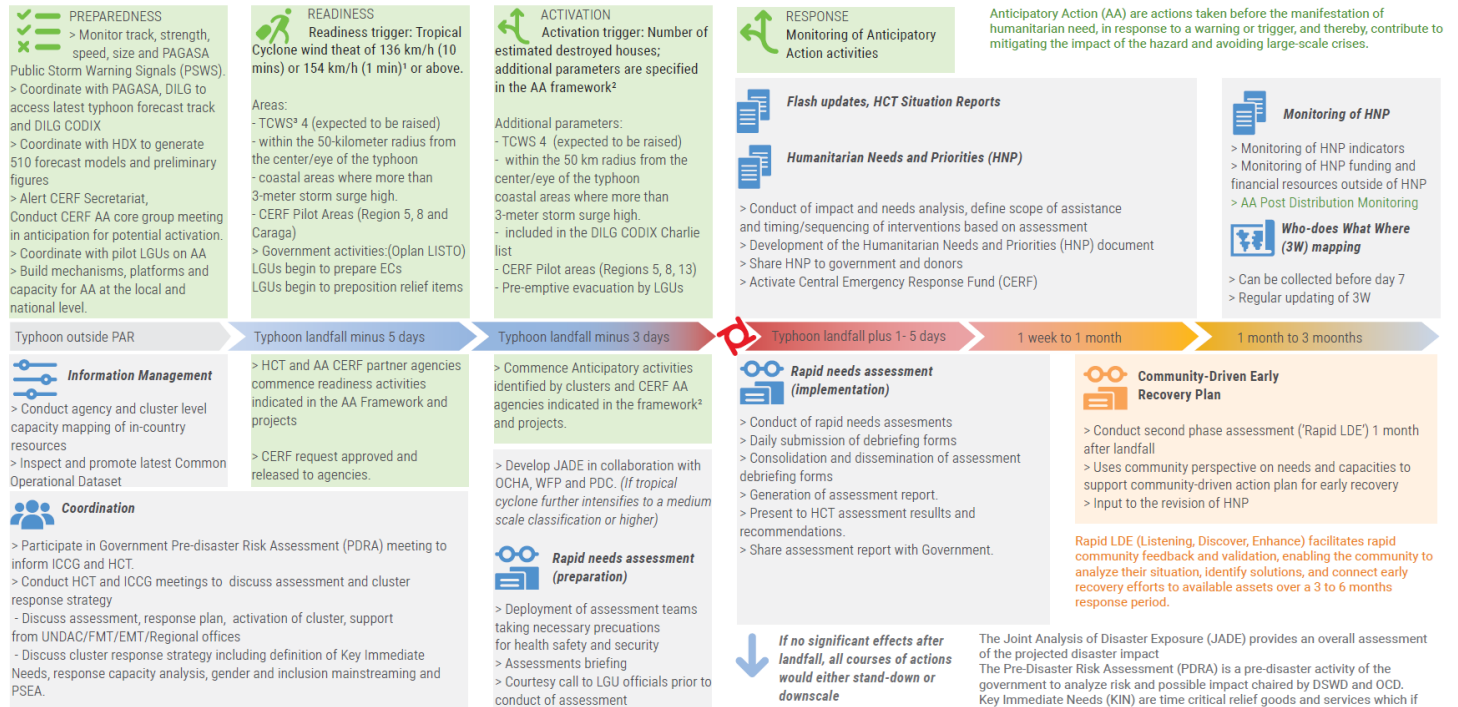

¹<https://www.nhc.noaa.gov/aboutshws.php>

²Anticipatory Action Framework

³PAGASA Tropical Cyclone Warning System


Creation date: 18 July 2024 Sources: OCHA, HCT, ICCG, FI Feedback: addrawe@un.org www.unocha.org/philippines www.reliefweb.int

3. Forecast, Scenarios and Triggers

Forecasts

Several organizations have implemented forecast-based financing (FbF) activities in the Philippines for small-scale typhoon response where they developed and used forecast and trigger mechanisms, while 3 key actors (WFP, IFRC/510, Global Parametrics) have developed their own models. OCHA and the Humanitarian Data Centre facilitated discussion among these organizations to understand various forecasting models developed for tropical cyclone and to determine the most appropriate methodology to use for the CERF AA Pilot in the Philippines. After a thorough analysis, it was decided to use the IFRC/510 model. The [summary and report link](#).


The Netherlands Red Cross 510 Initiative model was further revamped from a deterministic to a probabilistic impact forecast using ECMWF data. It is based on historical data that captures the relationship between impact (the houses totally damaged) and several explanatory variables (hazard, vulnerability and exposure). It uses typhoon forecast tracks, rainfall and wind speed to predict impact. There is an ongoing discussion and drafting of a Data Sharing Agreement (DSA) between OCHA/HDX, FAO, PRC, StartNetwork and PAGASA to use PAGASA data as one input in the 510 model.

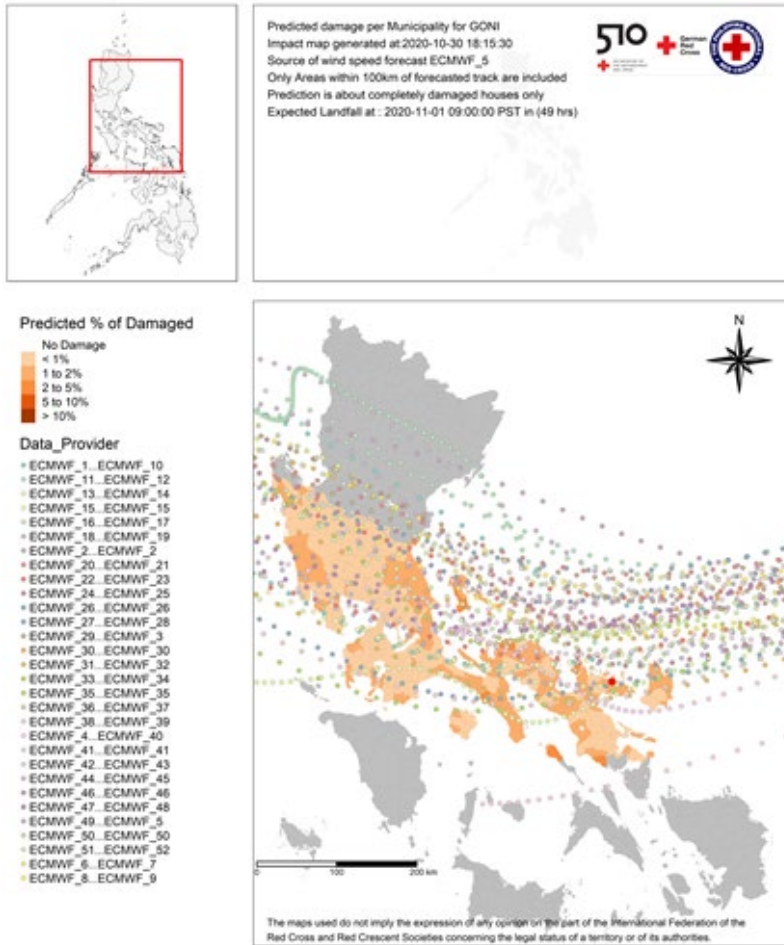


Scenarios

The 2024 Framework preserves the two scenarios approach put forward in 2022, to cover Regions 5, 8 and/or 13 (Caraga). Scenario 1 covers pilot areas in Region 5 and Samar Island Provinces in Region 8. Scenario 1 is based on a typhoon forecast track with a general direction and cone of uncertainty towards region 5 and Samar Island Provinces:

Northern Samar/Eastern Samar/Western Samar. Scenario 2 covers Region 13 (Caraga) and Region 8, Leyte Island Provinces, namely Leyte and Southern Leyte.

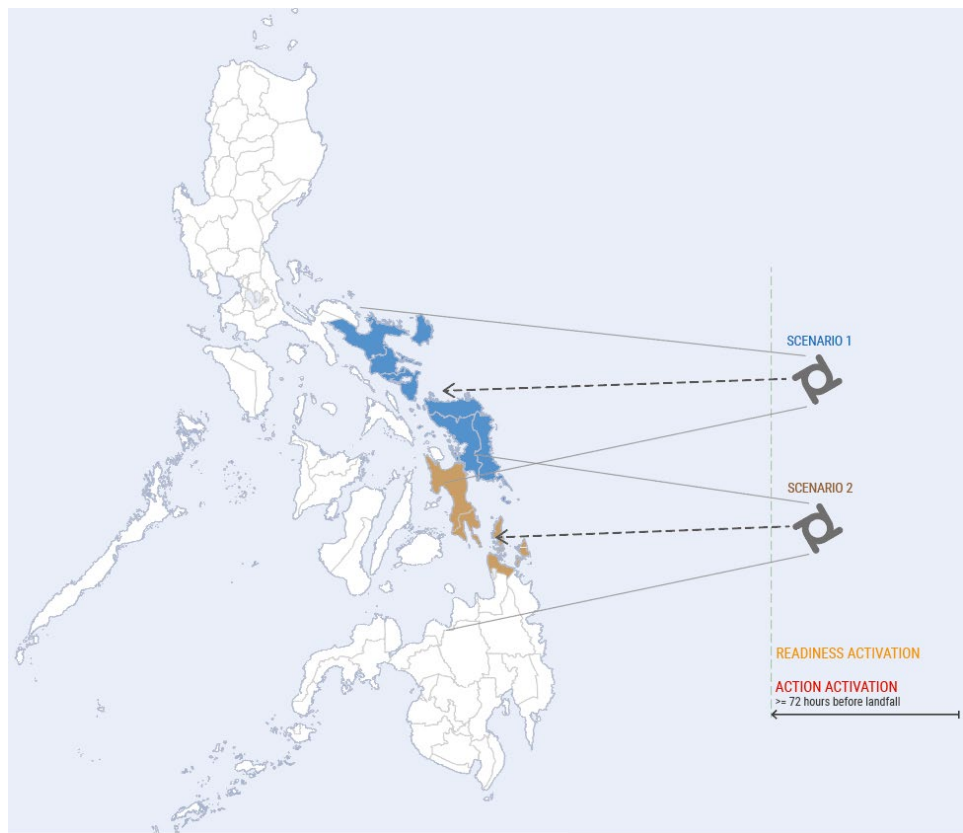

Triggers and thresholds

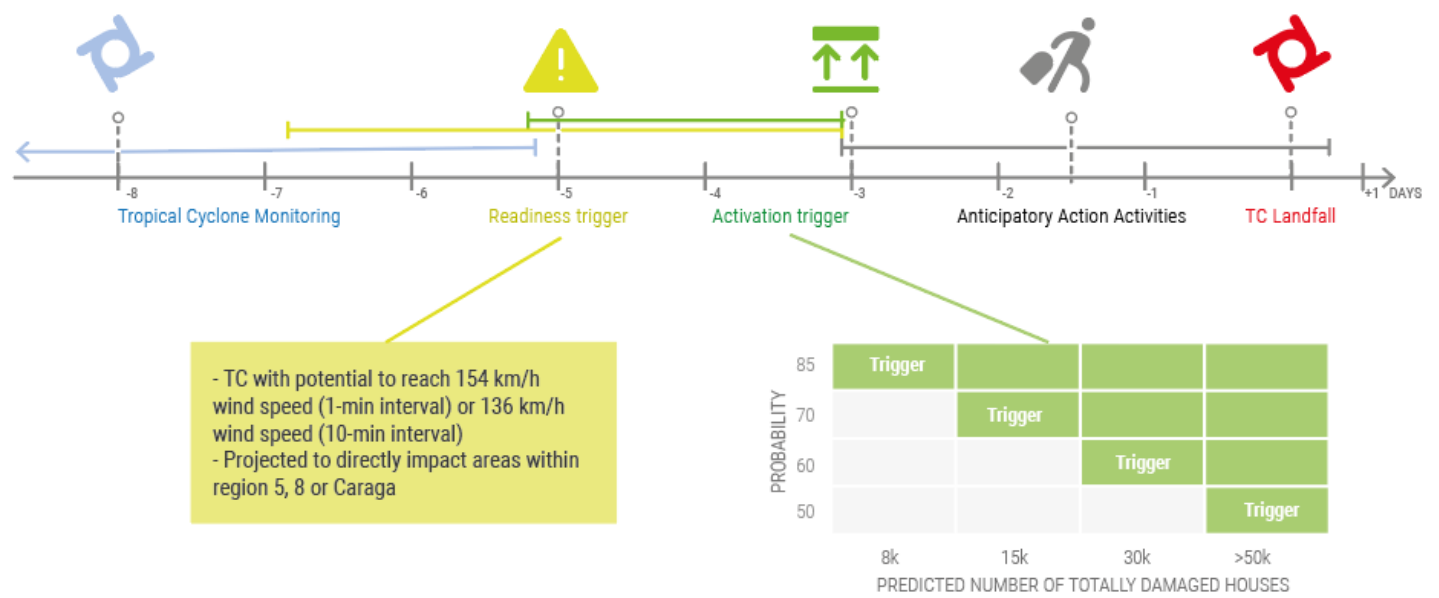

The CERF AA follows a 2-stage trigger activation:
1. Pre-activation triggers (readiness): 3-6 days prior to forecast landfall

a. Tropical Cyclone with potential to reach wind speed greater than 154 km/h maximum 1-minute sustained wind speed or 136 km/h wind speed at 10-minute sustained wind speed.

The weather bureaus/international organizations are listed in monitoring forecasts and using it for AA.

1. [Philippine Atmospheric, Geophysical and Astronomical Services Administration \(PAGASA\)](#)
2. [European Centre for Medium-Range Weather Forecasts \(ECMWF\)](#)
3. [Global Ensemble Forecast System \(GEFS\)](#)
4. [Weather Nerds \(Private Initiative\)](#)

b. Projected to directly impact areas within region 5, 8 and/or 13 (Caraga).

c. Readiness activation is either scenario 1 or scenario 2.

d. Only the scenario activated for readiness will be activated for anticipatory action.

e. Activation for readiness cut-off is 72 hours (3 days) prior to forecasted landfall.

f. If the forecasted tropical cyclone track is unclear on which scenario it will follow, the Triggers group will closely monitor the development and wait until a more definitive track is observed or until 3 days prior to forecast landfall. *Triggers group in discussion with Core group will provide a recommendation to the RC/HC on which scenario to potentially activate based on all available information.*

g. *Readiness activation can be activated with activation trigger at the same time on or before 72 hours before forecast landfall for scenario 1 or 2.*

2. Activation trigger: on or before 72 hrs (3 days) prior to forecast landfall

- a. As soon as ECMWF forecasts are available for a certain TC, OCHA Philippines with HDX will calculate the predicted total number of totally damaged buildings using the 510 model, produce impact map, and update it every 6-12 hours.
- b. If the readiness trigger has been reached earlier, activation for AA will only be for scenario where readiness was activated. Otherwise, we refer to #1.g above
- c. Threshold is reached and CERF AA is activated if 72 hours (3 days) before landfall, the predicted numbers fall within this range: 50% probability that 50,000 houses or more will be totally damaged, or 85% probability that 8,000 will be totally damaged.
- d. AA activation cutoff is 72 hours prior to forecast landfall.
- e. AA activation can be triggered if the number of predicted number of destroyed houses fall within the threshold even if the readiness trigger was not reached on/or before 72 hours before forecast landfall.

Activation protocol


The table and graphic below describe the activation protocol, including key roles and responsibilities in monitoring and activation of the Framework.

Organization	Activity	Timeline	Medium	Output
Triggers group, OCHA, HDX and NLRC 510	Monitoring of Tropical Cyclone (TC) formation; Join Government PDRA meetings	6-10 days prior to forecast landfall	Communication via the triggers group; regular email update from OCHA to core group	Forecast track and category of a typhoon; Generate TC timeline indicating the dates and days until forecast landfall.
HDX and OCHA	Generation of impact estimates	3-7 days prior to forecast landfall; every 6-12 hours based on PAGASA, ECMWF and other data (if available)	Sent via the Triggers group; regular email update from OCHA to core group	Forecast category and track of a typhoon; Impact and probability estimates, impact maps and landfall map (if possible)
Triggers Group and OCHA	If the readiness trigger is reached: ✓ A tropical cyclone forecast with potential to reach wind speed (greater than 154 km/h (1-min) or 136 km/h (10-min)) and projected to directly impact areas within Regions 5, 8 and/or 13 (Caraga). ✓ forecast track is clear and follows a general direction	3-7 days prior to landfall; <i>Limit for the activation for readiness trigger is 3 days prior to landfall.</i>	Email from RC/HC via OCHA to Core Group with attached 510 products as well as other meteorological agency (i.e. PAGASA) reports	Readiness trigger notice (indicating which scenario is activated) is sent to AA partners. <i>* Activation for AA will only be for scenario where readiness was activated. Readiness and activation thresholds are reached</i>

	to impact either scenario 1 or 2. ✓ TC forecast track and wind strength will be based on information available primarily from PAGASA, and compared with ECMWF, GFS, JMA and other weather bureaus in the region. ✓ If TC generally follows a track within scenario 1, activate readiness trigger for scenario 1. ✓ If TC generally follows a track within scenario 2, activate readiness trigger for scenario 2. ✓ Can be triggered with AA activation at the same time for either scenario 1 or 2 before 72 hrs before landfall. A Readiness activation notice indicating the scenario is sent to AA partners.			<i>at same time for either scenario 1 or 2.</i>
	✓ If the TC forecast track is not clear on which scenario it will impact, Triggers Group with Core Group will recommend to the RC/HC which scenario to activate based on all available information.	4-6 days prior to forecast landfall.	Email and meeting (if needed)	Triggers group and Core group to agree on which scenario to recommend to activate for readiness.
RC/HC Or OCHA on behalf of RC/HC	Notify CERF on the readiness trigger and potential activation of AA	3-7 days prior to landfall	RC/HC or OCHA PHL to send email to CERF	Email to the CERF secretariat on readiness activation
CERF	CERF notice to AA partners on release of funds	Upon activation of readiness trigger	CERF email to RC/HC and AA Core group	Email from CERF to UN agencies
HDX/OCHA	Generation of impact estimates (number of damage houses with probability)	3-5 days prior to forecast landfall; every 6-12 hours based on 510 modelling process	Sent via the Triggers group and email to Core Group	Impact and probability estimates, impact maps and landfall map
AA Core group	Inform local partners, FSPs and partner government agencies on the potential activation of AA in target areas	3-5 days prior to landfall	Meeting and email; Provincial lead to inform all local partners including LGUs	Early warning messages
Triggers Group, OCHA	If activation triggers are met for a particular scenario on or before 72 hrs (3 days) prior to landfall, recommend to RC/HC for AA Activation ✓ Activation for AA will only be for scenario where readiness was activated ✓ Activation will be based on threshold matrix. ✓ Activation can be triggered even if readiness trigger is not reached	On or before 72 hrs (3 days) prior to expected landfall. <i>AA activation cutoff is 72 hours (3 days) prior to forecast landfall.</i>	Meeting and email	Recommendation submitted to the RC/HC for activation
RC/HC/ or OCHA on his behalf	Notice to AA partners on activation action.	On or before 72 hrs (3 days) prior to forecast landfall	Email	Activation notice sent to AA partners and to CERF
Triggers Group, OCHA, HDX	If activation triggers are not met for a scenario that was activated for readiness 72 hrs prior to landfall, an activation trigger stand down notice.	70 hrs prior to landfall	Meeting and email	Stand down notice sent to partners and to CERF

OCHA, Triggers Group, HDX	Continue monitoring of TC development after stand-down notice	1-2 days prior to landfall	viber/whatsapp group and email	Impact maps ; TC track
---------------------------	---	----------------------------	--------------------------------	------------------------

The communication flow between partners involved in the AA CERF pilot in the Philippines.

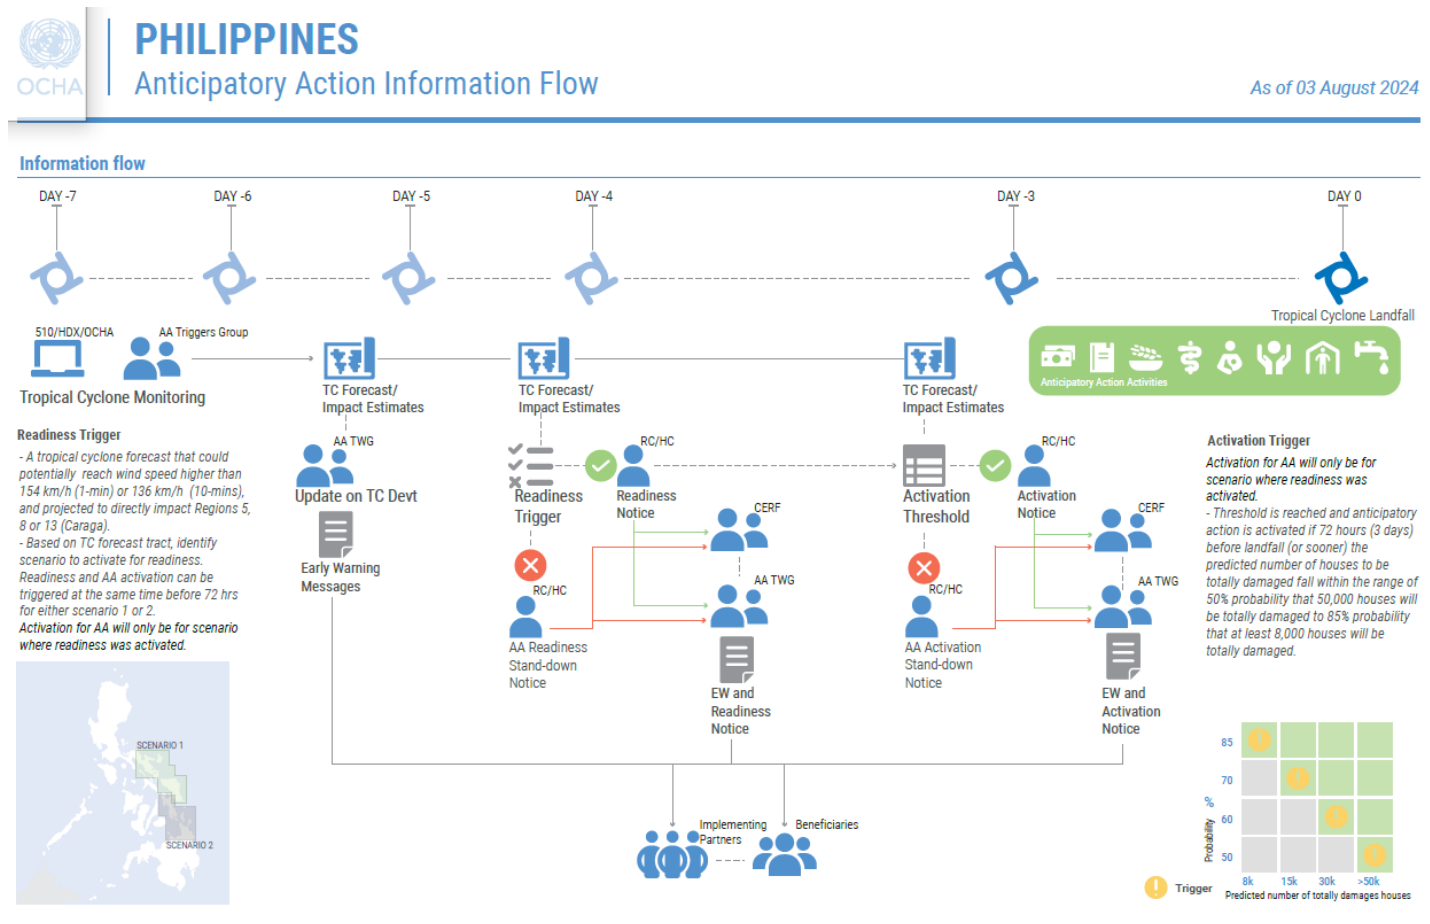

Known challenges, limitations and how to overcome these in the future

Key challenge in anticipating tropical cyclone path is the wide cone of uncertainty where the TC could change its track in a matter of hours. For example, there was a 150 km error in track position 72h ahead landfall for Super Typhoon Goni, which in an archipelago country poses significant operational challenges. A possible way to mitigate this uncertainty is to have assistance pre-positioned in several provinces and several partners on stand-by at the same time.

In the hours before landfall, TCs can also undergo rapid intensification that could effectively shorten the lead time from trigger activation. Tropical Cyclone Rai (Odette) was closely monitored by AA teams in December 2021, 7 days prior to forecast landfall and no numerical estimates were meeting AA thresholds. It was decided at 4 and 3 days prior to landfall that readiness and activation were stood down. But 24 hours prior to landfall, TC Rai underwent rapid intensification from typhoon category 2 to category 5. Due to the experience on TC Rai on near activation, an [after-action review by partners](#) was conducted by the Core Group in March 2022 to reflect on lessons learned and provide inputs to the revision and update of the AA Framework for 2022. NLRC/510 conducted a study to incorporate into their model the effect of rapid intensification in predicting the damage figures. The result of the study was not conclusive to incorporate into the model. Further study on rapid intensification was recommended.

Due to a fairly wide cone of uncertainty within the TC track, all seven provinces in scenario 1 or four provinces in scenario 2 will be activated under the proposed Framework. Some pilot areas might not be highly impacted but since these are highly

vulnerable areas, losses and damages will still be incurred and the AA activities will provide assistance and help build capacity. With sudden-onset events, there is a chance of a false alarm, i.e. that the readiness trigger is reached but not the activation trigger.

To further lessen the potential of false alarm, it was decided that the readiness trigger can be activated at the same time with AA activation at 72 hours before landfall while AA can be activated even if the readiness trigger is not reached. To give a better perspective on the potential false activation, the characteristics and development of past strong tropical cyclones were considered. Using the day the TC developed into a typhoon category for readiness trigger activation (at least 4 days prior to forecast landfall). 11 past tropical cyclones that had significant impact on regions 5, 8 or 13 were considered. Out of the 11, only 8 would have been considered for AA activation due to their strength and their chance to forecast significant damage to houses. Out of the 8 significant typhoons, 7 can be considered to have reached readiness trigger activation by day -4 or -3. This is because the TC has reached a typhoon category and the potential to intensify is reported.

Local name	International name	Landfall day	Should have activated		Readiness reached		Notes
			Scenario 1	Scenario 2	Scenario 1	Scenario 2	
Sendong	Washi	12/16/2011		N		N	Tropical Storm category
Pablo	Bopha	12/3/2012		Y		Y	Typhoon category at day -4
Yolanda	Haiyan	11/7/2013	Y		Y		Intensification on day -4
Ruby	Hagupit	12/6/2014	Y		Y		Typhoon category at day -4
Nina	Nock Ten	12/25/2016	Y		N		Severe Tropical Storm at day -3
Tisoy	Kammuri	12/2/2019	Y		Y		Typhoon category at day -4
Ursula	Phanfone	12/24/2019		Y		N	Typhoon category at day -2
Ambo	Vongfong	5/14/2020	N			Y	Landfall at 155kph
Quinta	Molave	10/25/2020	N		N		
Rolly	Goni	10/31/2020	Y		Y		Severe Tropical Storm at day -4 but still intensifying
Odette	Rai	12/16/2021		Y		Y	Rapid intensification on day -1

On a previous study, if the 2022-2023 trigger methodology is applied to 10 recent strong typhoons that affected Regions 5, 8 and 13 and would have reached the readiness trigger (see table below), *only three (Haiyan, Kammuri and Rai with Region 13 included) would also reach the activation trigger 72 hours before landfall.* In this case, readiness costs will be kept at a minimum (4% of the cost) to ensure that only very limited funding is used prior activation.

Typhoon	year	Activation trigger
Washi	2011	
Haiyan	2013	Yes
Bopha	2012	
Hagupit	2014	
Nock-ten	2016	
Kammuri	2019	Yes
Phanfone	2019	
Vongfong	2020	
Goni	2020	
Rai	2021	Yes

To understand the performance of the readiness trigger, we turn to [this thesis](#) from 510 on rapid intensification. Table 4 on page 24 summarizes historical typhoons that should have reached the activation trigger for DREF, their maximum landfall

windspeeds, and the maximum windspeed forecast 24 hours in advance. Setting our target windspeed to 200 km/h (since we are really interested in Cat 4 and above), and the readiness windspeed to 178 km/h, we can use this table to roughly estimate the readiness trigger performance:

Metric	Value
TP	3
FP	1
FN	16

The false positive (FP) rate is relatively low, and we conclude that if the readiness trigger is reached, there would be an approximately 25% chance that it is a false activation. However, due to rapid intensification, we encounter a substantial number of false negatives (FN). This means that we only expect to reach the readiness trigger for about 15% of all typhoons for which we should have reached it.

There are several caveats to this simple analysis, including that we are considering typhoons for the full country rather than just our region of interest, and we cannot guarantee the completeness of the sample.

To ensure readiness for eventual activation of the pilot and as a form of simulation, the Triggers Team will monitor each tropical cyclone that enters the Philippine Area of Responsibility in 2024 as per the above-mentioned procedures.

Flagship initiative – towards a people-centered anticipatory action

The Flagship Initiative aims to improve humanitarian aid delivery by focusing on people-centered approaches and supporting government efforts. Led by the UN Resident and Humanitarian Coordinator, it leverages local expertise to transform how aid is provided, emphasizing community resilience. Going beyond mainstream AAP approaches, communities are seen as decision-makers, not merely consulted aid recipients, promoting collaboration and breaking down barriers in the aid system. The initiative enhances community involvement, builds partnerships, and learns from local practices. The Flagship Initiative is currently implemented in four countries: Colombia, Niger, South Sudan, and the Philippines.

In the Philippines, the Flagship Initiative is implemented in the regions covered by CERF-AA. In these regions, the Flagship Initiative team conducted the Listen, Discover, and Enhance (LDE) process by which community perspectives and priorities are being listened through the Resilience-Based Participation Community Appraisal (ReBPCA) Tool from which various aspirations and recommendations highly relevant to the CERF-AA are gathered and collated.

During the CERF-AA Planning workshop held in June 2024, participants engaged in a discussion that resulted in key flagship initiative recommendations based on community-suggested solutions. These recommendations emphasized the importance of focusing on saving and protecting community assets such as livelihoods, safe shelters, and safe spaces. Also, there was an advocacy for enhancing community efforts through providing micro-grants to groups and increasing segment-based participation in the planning process. The workshop highlighted the need to enhance understanding of AA at the municipal and barangay levels, as well as to clarify and strengthen the capacity of Local Government Units (LGUs) to integrate AA into existing response strategies effectively to better prepare in anticipation of potential crises.

4. Anticipatory Action Plan


Overview

Destructive tropical cyclones cause significant losses to agriculture and damages to infrastructure, particularly houses, health, schools, markets, water facilities, communication, and have serious humanitarian consequences, including loss of livelihoods, reduced income, disruption to continuing education and exacerbation of pre-crisis protection issues, such as GBV.


To prevent or reduce the humanitarian impact of severe typhoons, anticipatory actions need to be delivered within the narrow window of opportunity, i.e. between the readiness trigger and the activation trigger, after which the implementation

of anticipatory action interventions could no longer be safely delivered and would interrupt government mandatory evacuation procedures.

Example of activities a Filipino household is advised to undertake before a typhoon and responses of at-risk people on preventive measures and their coping strategies in case of a typhoon:

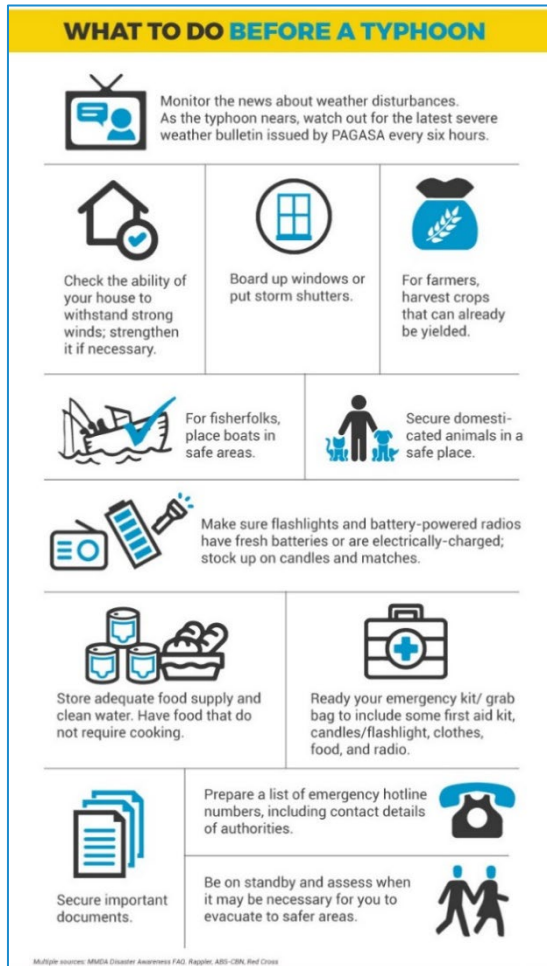


PREVENTATIVE MEASURES

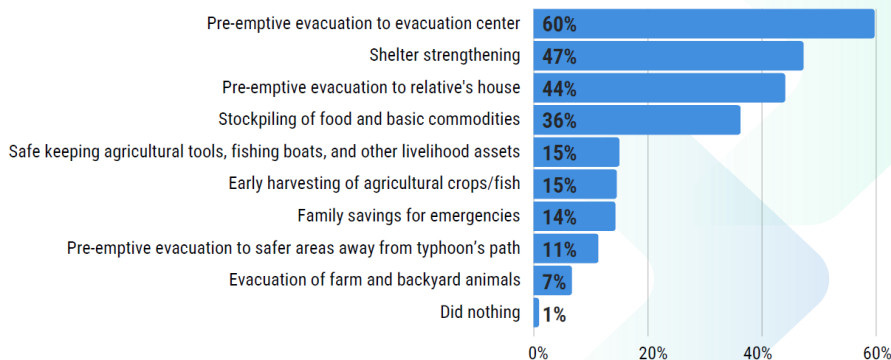

CERF AA pilot Pre-crisis survey 2022: Preventive measures that at-risk people would undertake in case of a major tropical cyclone, source: START Network

COPING STRATEGIES



Measures undertaken	Location Type			
	Coastal	GIDA	Plains	Upland
Borrowed money	68%	51%	67%	63%
Reduced portions of food	43%	32%	42%	25%
Spend savings	36%	22%	23%	21%
Reduced number of meals per day	19%	0%	22%	13%
Seek refuge with relatives and neighbors	20%	24%	25%	39%
Engage in additional work	30%	11%	15%	18%
Sell livestock	10%	5%	7%	4%
Send family member to eat elsewhere (with relatives)	9%	5%	2%	9%
Others	4%	19%	2%	5%
Withdraw children from school	1%	3%	4%	2%
Sell household assets	4%	3%	1%	0%

CERF AA pilot Pre-crisis survey 2022: Coping strategies of at-risk communities in the aftermath of a major tropical cyclone, source: START Network

Agencies need significant operational capacity (sectoral, logistic, administrative, financial, human resources) to implement interventions at scale in a timely and effective manner. It is critical to note that the success of actual implementation in a particular village or municipality relies on a number of factors, such as its geographic location, proximity to major roads, accessibility to evacuation centres and designated financial service providers, early activations of mandatory evacuations, pre-emptive power cuts and interruptions of telecommunication lines, localized wind and rain events as well as landslides, which may be aggravated by previous rainfall events during the rainy season as well as COVID-19-related movement restrictions. All these factors are outside the scope of this Framework. Duty of care of humanitarian responders will be agencies' utmost priority when activating anticipatory action assistance.

For this pilot, interventions have been selected to be rooted in the current operating environment, including COVID-19, agency capacity to deliver, ability to mitigate the impact of typhoons and learning from past experiences.

To better understand how components of the AA framework come together in a coordinated manner based on the operational timeline, the Core Group organized a week-long simulation exercise in September 2022 on both locations of the pilot. A large-scale joint simulation exercise of anticipatory action activation brought together more than 160 participants and some 500 potential beneficiaries. The final report is available [here](#).

The details of UN-led anticipatory action interventions as part of the pilot are in the annexed CERF applications.

Approach to targeting at-risk beneficiaries

Region 5 (Bicol), 8 (Eastern Visayas) and 13 (Caraga) were selected as they are most often where destructive typhoons made their initial landfall, which brings the greatest damage in terms of wind impact and storm surge. Areas severely affected by Typhoon Rai in December 2021 (Southern Leyte, Surigao del Norte and Dinagat Islands) were also considered in the selection of pilot areas for Scenario 2.

As a starting point, the approach to selecting target municipalities used a common dataset disaggregated by geography, age, sex, disability and poverty to jointly plan for direct CERF assistance to those considered most vulnerable in Region 5, 8 and 13. Municipalities were prioritized based on municipal poverty incidence from Philippine Statistics Authority data (2015), exposure to typhoon impact, number of women, and people living in houses made of light material. A composite index was developed that ranked all municipalities in the three regions according to the selected criteria. The selected areas were presented to LGUs for additional input and suggestions. This prioritization was overlaid on a map with existing presence and operational capabilities of UN agencies, Philippine Red Cross and START Network Partners.

The outcome of this inclusive and consultative approach in 2021 led the Core Group to identify in Region 5 a total of 20 municipalities in four provinces (Camarines Sur, Albay, Catanduanes, Sorsogon), Region 8 a total of 35 municipalities in five provinces (Samar, Northern Samar, Eastern Samar, Leyte, Southern Leyte), and Region 13 (Caraga) a total of 20

municipalities in 2 provinces (Surigao del Norte and Dinagat Islands) where 2.9 million are at risk of being exposed to typhoon impacts.

Scenario 1 beneficiaries breakdown

People targeted by sex and age	Men (≥18)	Women (≥18)	Boys (<18)	Girls (<18)	Total
Total (Incl. PwD from below)	107,316	115,788	74,831	74,860	372,795
Persons with disabilities (PwD) (Out of the total targeted)	7,811	7,383	4,812	3,857	23,863

Scenario 2 beneficiaries breakdown

People targeted by sex and age	Men (≥18)	Women (≥18)	Boys (<18)	Girls (<18)	Total
Total (Incl. PwD from below)	58,639	73,917	36,236	34,598	203,390
Persons with disabilities (PwD) (Out of the total targeted)	2,524	2,579	3,311	3,015	11,429

Flagship initiative integration into anticipatory action


The Flagship Initiative used the pilot areas of CERF AA to identify vulnerable communities to be its pilot areas as well. Based on the initial findings of the Flagship Initiative, communities affected by disasters have collective efforts before, during, and after the disaster, and many of these are done for generations in preparation for various hazards. Collective efforts before a disaster aimed to protect lives, properties, and livelihoods with the end in view that if damaged occur, such would be minimal and recovery would be faster and easier. These pre-disaster initiatives are done by self-help groups based on family or clan, neighborhood, faith/religion, livelihood associations, and registered organizations. These community groups have the greatest potential to implement community-led anticipatory actions supported by cash grants that could potentially enhance their traditional response practices and systems. Cash grants could be best done to groups that have experienced either in managing cash or those who have long-standing experience of self-help initiatives with or without cash assistance.

FAO, WFP and UNFPA integrated several Flagship initiative approaches in their 2024 anticipatory action projects, building on community-suggested solutions during community consultations and discussions held during the June 6 AA workshop. These FI approaches center on the protection of community and household assets via the distribution of community microgrants, also termed Group Cash Transfers (GCT), and the provision of physical safe storage sites.

Under Scenario 1, FAO will pilot anticipatory GCT to 6 fisherfolk and/or farmer folk associations for the safe storage or evacuation of livelihoods assets, benefiting at least 600 association members in total. Each association will receive a group transfer ranging from \$1,250 to \$3,000 (PhP 100,000 to PhP 180,000), made to association representatives. Under scenario 2, 2 fisherfolk associations will receive GCT for the safe storage or evacuation of livelihoods assets, benefiting at least 200 association members. Each association will receive a larger \$10,000 transfer.

WFP will similarly pilot anticipatory GCT for 2 fisherfolk associations under scenario 2, to protect or evacuate livelihoods assets. Each association will receive an average GCT of \$5,000 (transfers may vary), transferred via OTC remittance outlets to association representatives. WFP will update its SOPs in collaboration with LGUs to reflect the 2024 CERF AA Framework, including measures to protect critical livelihood assets. UNFPA will pilot anticipatory GCT for 4 women-led organisations (WLO) under both scenarios 1 and 2, with each WLO receiving \$2,000. These group transfers will protect varying community livelihoods assets, ensure food security, and secure potential evacuation before the typhoon makes landfall.

The transfer amounts for all anticipatory GCT pilots are derived through consultations with the associations and reflect the number of association or group members, the types of assets to be protected, as well as the costs of safe storage, transportation, and evacuation in the

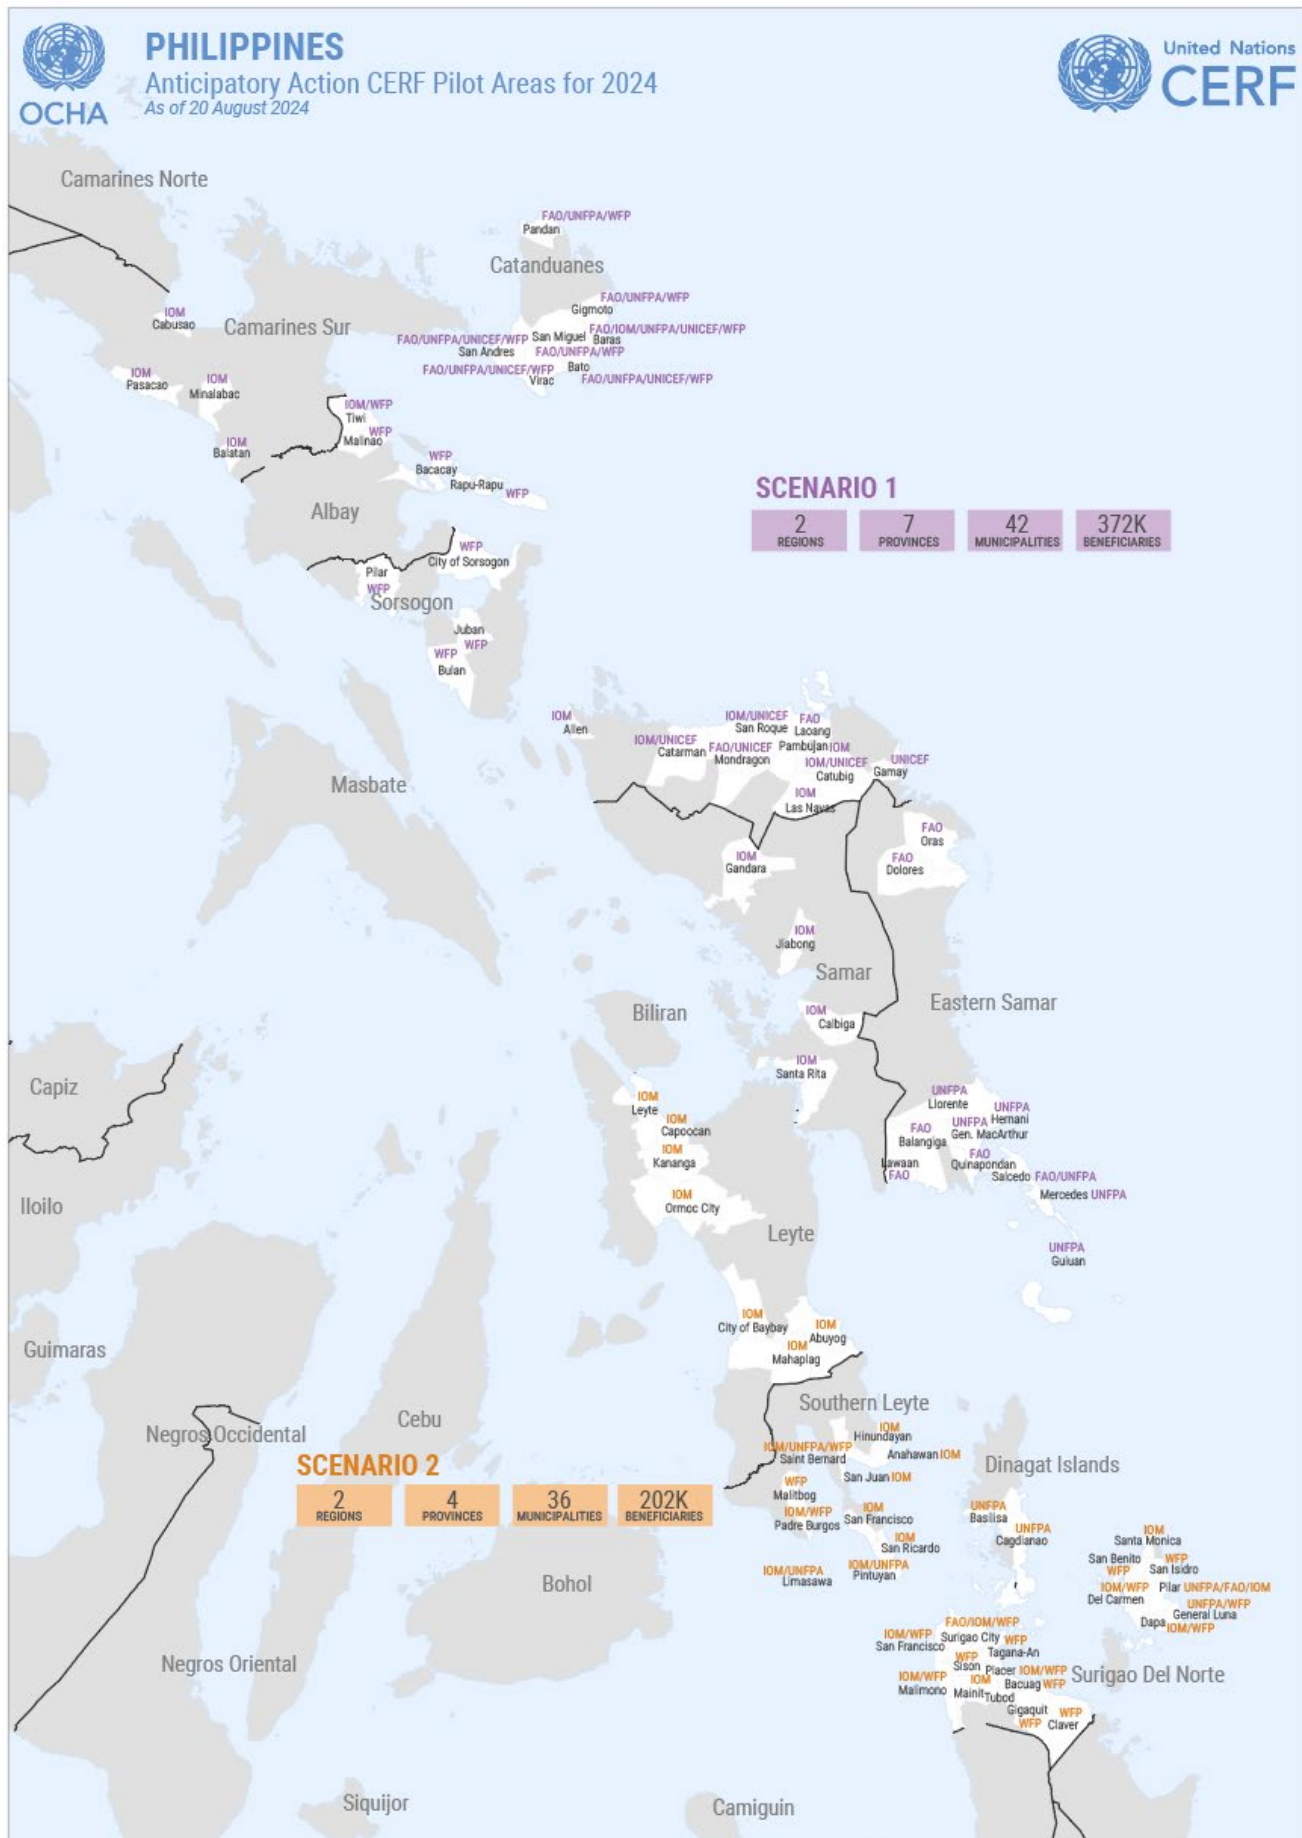

Organizational set up of the CERF AA Pilot Framework


To develop and deliver on the AA Pilot Framework, organizational project structure was set up with reporting lines to the Humanitarian Country Team (HCT) and in close collaboration with the Inter-Cluster Coordination Group (ICCG).

The AA Core Group was established as a principal decision-making body of the pilot; it is convened by OCHA and composed of key UN agencies as well as an NGO representative from the START Network and IFRC. To work on specific technical issues, Team Triggers, Team Cash, Team Cross-cutting issues and Team on Learning were established and are led by respective UN agencies. NGO partners agreed to lead on accountability to affected population and ensuring communities are consulted in development of the Framework.

To ensure regular communication and operational coordination with partners and authorities in prioritized areas, provincial leads were selected. UN agencies were designated as a 'CERF anticipatory action pilot Lead' in each of the eight targeted provinces, with responsibility to ensure the relevant regional, provincial and municipal authorities are well informed of project objectives, are consulted on target beneficiary selection and input in validation, as well as that UN partners are joining key-decision making coordination meetings, such as the Pre-Disaster Risk Assessment (PDRA) meeting organized by the Provincial DRRM office prior to a typhoon landfall. On behalf of the HCT, OCHA would attend national-level PDRA meeting of the National Disaster Risk Reduction and Management Council (NDRRMC).

Region	Province	Coordination Provincial Lead
Region V (Bicol Region)	Albay	WFP
	Camarines Sur	IOM
	Catanduanes	FAO
	Sorsogon	WFP
Region VIII (Eastern Visayas)	Eastern Samar	UNFPA
	Leyte	IOM
	Northern Samar	IOM
	Samar (Western Samar)	IOM
	Southern Leyte	IOM
Region VIII (Caraga)	Surigao Del Norte	WFP
	Dinagat Islands	UNFPA

The AA Core Group collaborates with the AA Technical Working Group, co-chaired by FAO and the national Office of Civil Defense.

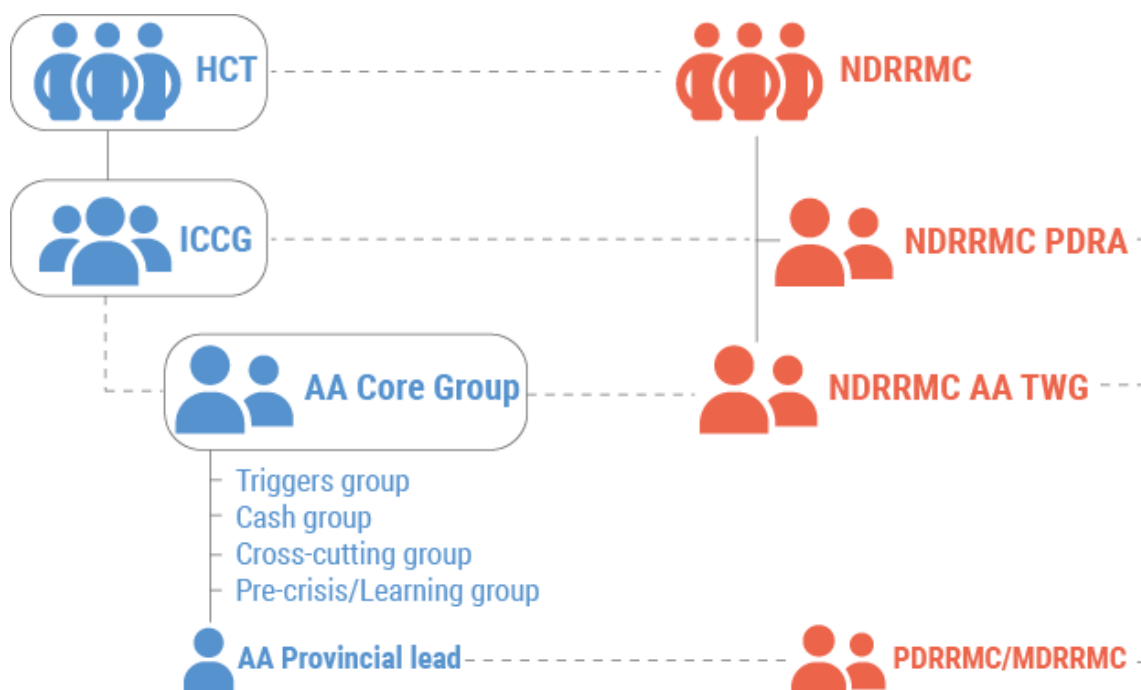

Partnerships and localization of anticipatory action

At the very onset of the pilot design, the RC/HC made a strong call for including local actors in its development and implementation. Both IFRC and START Network have formed part of the Core Group that meets weekly to develop the Framework, working through Team on Triggers, Team on Cash and Team on cross-cutting issues. Agencies with experience in early action interventions significantly contributed to the design of the pilot by sharing their learning with anticipatory action activations in the Philippines.

While the UN agencies are main recipients of CERF funding, each of them works with local partners, with the aim to ensure that at least 30% of allocated CERF budget for the Philippine pilot goes to local NGOs and strategic partners, to the extent interventions allow such partnerships. As per the 2024 Framework, 38% of funding in Scenario 1 and 41% in Scenario 2 will go to NGOs, including local NGOs.

Working with partners and local actors and promoting local buy-in has been mainstreamed throughout the Framework development when preparing its Triggers, the Delivery Model, the Money and the Learning.

Organization	CERF-funded implementing partners
FAO	Oxfam Pilipinas; CARE, PDRRN, AADC
IOM	Catholic Relief Services (CRS); World Vision; CARE, Agri-Aqua Development Coalition Mindanao, Caritas Philippines
UNFPA	ACCORD; ADRA, Good Neighbors International Philippines (GNIP)
UNICEF	Plan Pilipinas, DSWD/Landbank
WFP	National Confederation of Cooperatives

Highlights of how working with local actors will be featured in the pilot:

- UNFPA will utilize the knowledge, resources, and input of local partner and the community in establishing the criteria and methodology for commodity distribution, implementing AA activities and linking to the community and feedback during the monitoring phase of the project. Women and adolescent girls are most of the front-line Barangay Health Workers (BHWs) and Women Friendly Spaces (WFS) facilitators. BHWs will be stationed at the evacuation centers to support coordination of SRH services.
- FAO will work with the following implementing partners: Oxfam, through PDRRNet, will distribute multi-purpose cash and cash for vulnerable livelihoods to beneficiaries in Eastern Samar and Northern Samar; while CARE will conduct the preparedness activities for cash transfers in Catanduanes and Northern Samar and facilitate readiness activities in Catanduanes.
- In addition, local NGOs are particularly engaged in preparedness activities which are not all funded by CERF.
 - For example, FAO is working with CSOs on community preparations, validation of the pre-identified beneficiary lists, mapping of financial service providers and close coordination with local government units and other local actors.
 - Similarly, WFP is engaging with National Confederation of Cooperatives, to carry out community sensitization on the AA project, independent validation of beneficiary lists generated by the local government units, beneficiary registration in WFP's SCOPE platform, pre-crisis mapping, early warning messaging and assist with cash distribution in places where there is no financial service provider. WFP will also use local partners for post-distribution monitoring.
 - Agencies noted that one of the constraints of not engaging with local actors even more is their lack of capacity to work at scale and limited experience with anticipatory action, while at the same time CERF does not fund any capacity building activities that would help local actors develop these skills.
- Local government agencies too are involved in the implementation of some activities. For example, UNICEF is working directly with the Department of Social Welfare and Development (DSWD) and Landbank of the Philippine (LBP) to provide cash top-up to families with children enrolled in the government social protection programme.

CERF Anticipatory Action Localisation

SCENARIO 1						
Agency	Funding	Partners	NGO	NGO %	INGO	INGO %
FAO	1,586,881	PDRRN/Oxfam, CARE	574,850	36%		0%
IOM	1,717,091	CRS (Caritas), World Vision	323,473	19%	149,576	9%
UNICEF*	832,319	DSWD, Landbank, Plan Pilipinas	611,240	73%		0%
UNFPA	675,919	ACCORD, GNIP	150,000	22%	150,000	22%
WFP**	2,270,954	National Confederation of Coop	1,056,043	47%	0	0%
TOTAL	7,083,164		2,715,606	38%	299,576	4%

* UNICEF directly works with government counterparts for distribution

SCENARIO 2						
Agency	Funding	Partners	NGO	NGO %	INGO	INGO %
FAO	323,096	CARE, AADC	97,000	30%		0%
IOM	2,722,279	CARE (Accord, Agri Aqua Devt Coalition)	567,922	21%		0%
UNFPA	643,327	ADRA, GNIP	150,000	23%	150,000	23%
WFP**	1,668,876	National Confederation of Coop	1,363,000	82%		0%
TOTAL	5,357,578		2,177,922	41%	150,000	3%

** WFP costs include transfer value and local third party monitoring costs

Operational coordination with local authorities

The Government of the Philippines has made significant efforts to protect people and infrastructure, leveraging the investment made since Super Typhoon Haiyan of 2013 in improved early warning and reinforcing the important leadership role played by local officials. The Framework is built on existing government Disaster Risk Reduction and Management mechanisms and coordination architecture. The National Disaster Risk Reduction and Management Council through the Office of Civil Defense have been engaged with Forecast-Based- Financing (FbF) partners, FAO, IFRC, WFP and Start Network and is aware of several pilots undertaken in the past four years. OCD co-chaired the FbF Technical Working Group (TWG) with FAO. With the AA CERF Pilot, the Disaster Preparedness Pillar of the NDRRMC adopted the concept of Anticipatory Action and renaming the FbF TWG into AA TWG, with representation from government: DSWD, DoST, DILG and OCD and humanitarian agencies. It is envisioned that with the NDRRMC adopting the AA concept, the AA CERF Pilot can be well implemented at the regional and pilot areas, at the provincial and municipal levels.

As mentioned under the Organizational set up, provincial lead agencies were selected in each of the eight targeted provinces to ensure regular communication and operational coordination with partners and provincial and municipal authorities in prioritized areas. OCHA is leading coordination at a regional level with authorities in region 5 and 8.

Mandatory pre-emptive evacuation procedure

Since Super Typhoon Haiyan, that resulted in over 6,000 casualties, the government strengthened its pre-emptive evacuation procedures. Once a mayor of a municipality triggers pre-emptive evacuations based on a PAGASA Tropical Cyclone Wind Signal and PDRA, it is mandatory for those living in at-risk areas to evacuate. People that actually evacuate to designated evacuation centres are often times those most vulnerable living in houses made of light materials and having no safer alternative, such as staying with relatives or friends living in sturdier shelter.

In line with government's early warning protocols, local authorities are expected to start with pre-emptive evacuations of areas to be most affected 48h before landfall, often times women, children and elderly going ahead, with all evacuations expected to be completed 24h before landfall. People weather the storm in evacuation centers and are allowed to start returning to their homes 12 hours after landfall. Due to COVID-19 pandemic and adherence to stricter health protocols in evacuation centres, mayors are expected to commence preparations for pre-emptive evacuations 72h before landfall.

Pre-emptive evacuations are government's single most successful early action intervention that saves lives. For example, in November 2020 local authorities pre-emptively evacuated over 500,000 people ahead of Super Typhoon Goni and 230,000 people ahead of Typhoon Vamco, effectively saving many lives.

The CERF anticipatory action interventions were designed keeping these mandatory protocols in mind and incentivizing responsible behaviour for vulnerable households to find safer ground in evacuation centres.

Protection from sexual exploitation and abuse (PSEA) in anticipatory action


- Strengthening protection from sexual exploitation and abuse (SEA) is a shared responsibility of the humanitarian and development community. The UN IP Protocol outlines requirements for the UN and its implementing partners to ensure adequate safeguards and appropriate actions related to SEA are in place. With the engagement of International and Local NGOs/CSOs on AA, UN agencies working with them must ensure their partners' organizational capacities on PSEA in line with the minimum PSEA operating standards. The PSEA capacity assessment of NGOs/CSOs is a requirement given that the AA Pilot Project is implementing higher-risk programme activities such as operating in evacuation centers; having direct contact with children; and where sexual and gender-based violence can be prevalent.
- Likewise, government agencies involved in the delivery of humanitarian assistance in partnership and collaboration with UN entities and their implementing partners must pursue all appropriate means to ensure the effective protection of the local populations, particularly women and children, from sexual exploitation and abuse. SEA is unacceptable behavior and is prohibited for UN personnel and implementing partners. A briefing from the

Philippines PSEA Coordinator was organized for the five UN agencies on their commitments and obligations related to SEA risks.

Consultation with communities


The UN agencies and START Network agreed on a collective approach to consultation with communities to ensure diverse and inclusive perspectives and to carry out a pre-crisis survey, based on a similar methodology used by the HCT's Community of Practice Community Engagement for the HCT COVID-19 response consultations as well as for the preparation of the HCT Contingency Plan for the Metro Manila 7.2-magnitude earthquake.

In 2022, the [pre-crisis survey](#) was adjusted to account for anticipatory action interventions and was carried out by the UN agencies with the support of implementing partners reaching 434 respondents from 20 municipalities from four of the provinces in Region 5 and 24 municipalities within four provinces in Region 8. The survey tool has 41 questions divided into five (5) sections: 1. household vulnerability profile; 2. respondent classification; 3. Household (HH) exposure to shocks and risks and coping strategies; 4. at-risk people's priorities and preferences; and 5. access to information platform, communication channel, and accountability mechanism. The survey used five indicators:

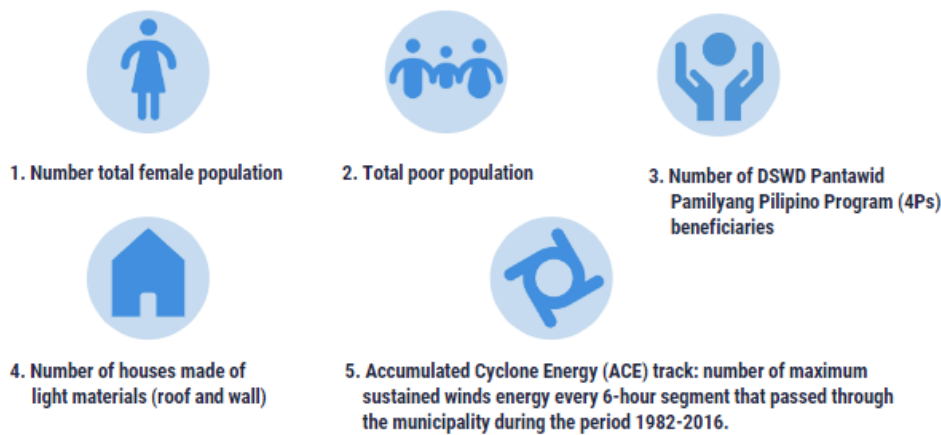

The results of the survey validated and informed the revision of agencies' AA design and implementation plan.


STUDY LOCATION

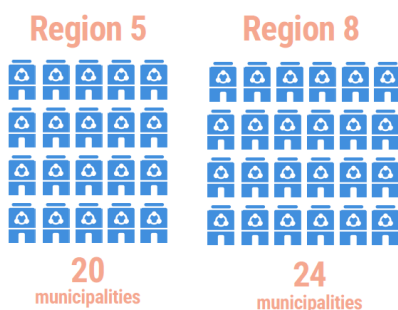

Area Type	Coastal	GIDA	Plains/Flat	Upland	Overall
Region 5					
Albay	63%	0%	20%	18%	26%
Camarines Sur	27%	20%	33%	20%	8%
Catanduanes	32%	0%	36%	33%	39%
Sorsogon	70%	2%	24%	4%	28%
Region 5 Total	50%	2%	28%	20%	100%
Region 8					
Eastern Samar	56%	0%	29%	16%	20%
Leyte	25%	44%	31%	0%	7%
Northern Samar	21%	14%	61%	5%	66%
Samar (Western Samar)	18%	29%	35%	18%	7%
Region 8 Total	28%	14%	50%	7%	100%
Region 5 & 8	38%	9%	40%	13%	100%

Pre-crisis survey 2022 coverage area, source: START Network

Effects of previous typhoons

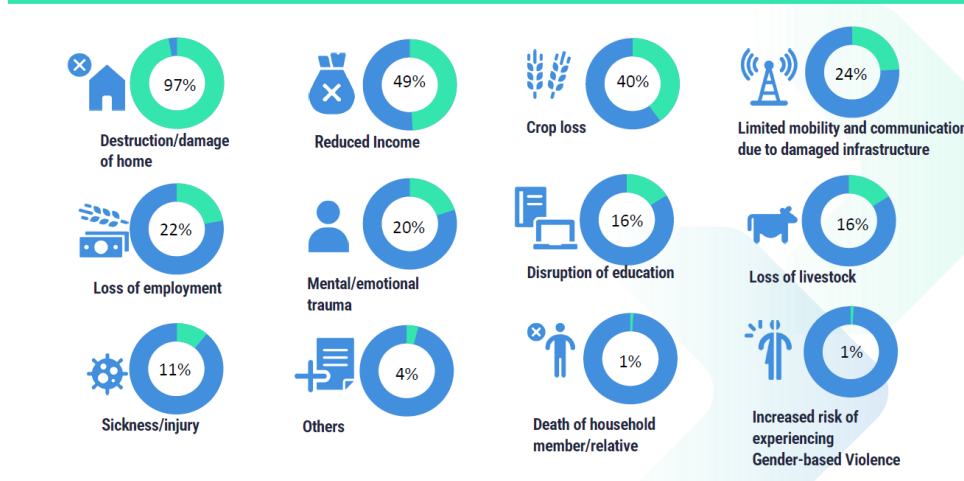

Pre-crisis survey 2022: Feedback from at-risk communities on effects from previous typhoons, source: START Network

Ensuring readiness for timely implementation

In the context of the Philippines only about 48-hours will be available between the Readiness and Activation trigger and very few activities could be implemented in the Readiness phase. Compared to other, more slow-onset pilots, preparedness activities will be critical.

As previous activation attempts indicate, a number of potential operational challenges could hinder implementation of pre-emptive cash interventions, including losing precious hours if the trigger is reached in the hours when the banks are not operating or if telecommunication or power lines are pre-emptively disabled by the authorities. Once Tropical Cyclone Wind Signal 1 is raised, usually 72h ahead of landfall, all ports will be closed, and any island will be out of reach by sea.

Also important will be that agencies put utmost priority to duty of care and safety of staff that will be carrying out anticipatory activities. They require proper equipment, such as raincoats, flashlights if the work is carried out late at night, waterproof bags, as well as IDs and key documents explaining the pilot's early action activities. Evacuation spaces for staff will need to be identified and communicated. Operational agencies will also need to pre-identify suppliers (trucks, vans, etc.) as it is difficult if done a few days before landfall. Segment-based approach in community participation must be considered in these preparedness and response plans to address the diverse needs of affected communities., including women, children, youth, elderly, LGBTQIA+, persons with disabilities and other marginalized groups. Tailored interventions and inclusive communication strategies are essential to ensure that no one is left behind.

To better prepare and plan for these contingencies, the Core Group organized in July 2021 a 1-day simulation exercise that produced a comprehensive Master Plan of the Pilot Operational Timeline (see Annex 1), planning detailed activities of each intervention from preparedness to activation. A joint 2-day simulation exercise was conducted on 19-23 September 2022 both for scenario 1 and scenario 2 to test the framework and assess the effectiveness of the operational components, namely: risk communications/messages; information flow such as alert/warning signals including standby and stand-down messages; coordination with local authorities, community engagement, prepositioning of assistance that includes cash and in-kind, deployment of personnel and other cross-cutting issues such as prevention of sexual exploitation and abuse (PSEA) and Accountability of Affected Population (AAP).

Pre-emptive cash interventions

Given the very short lead times, unconditional pre-emptive multi-purpose cash is a major component of the pilot. Partners agreed to harmonise the MPC transfer value for the 2024 typhoon season, using a Minimum Expenditure Basket methodology to derive the transfer value., instead of Minimum Regional Wage as a proxy to define the transfer value. MEB value as agreed by the Cash Working Group is PHP 9,750, which was endorsed by the HCT in July 2023. The MPC value for

AA is set at PhP 3,330 (US\$58)), equivalent to 1/3 (33%), approximately 1/3 of the monthly MEB Transfer Value, in order to account for the 10-day lead period.²

The partners agreed to budget the transfer cost in the CERF as US\$60 to safeguard 7% buffer against exchange rate fluctuations, using the standard [UN exchange rate](#).

In total, 73,300 vulnerable households in Scenario 1 and 35,300 households in Scenario 2 will receive MPC across Region 5, Region 8, and Region 13 (Caraga). The number of recipient households, delivery mechanisms, and targeting modalities are shown below.

Agency	Modality	Beneficiaries (Households)	Delivery Mechanism	Targeting	Transfer Values
FAO	- MPCA - GCT	Scenario 1: 15,500 (MPC) 6 groups (GCT) Scenario 2: 2,000 (MPC) 2 groups (GCT)	- Metrobank, with payment aggregation (e-wallets, bank transfers / ATM) - Direct Cash (cash in hand)	Vulnerable farmers and fisherfolks in beneficiary list from Registry for Basic Sectors in Agriculture	- MPCA: USD 60 / PHP 3,300 - GCT: USD 1,250-3,000 (S1) and USD 2,600 – USD 3,500 (S2)
IOM	- MPCA - Cash for Shelter	Scenario 1: 6,411 (MPC + CfS) Scenario 2: 15,728 (MPC + CfS)	- OTC FSPs: Palawan - Direct Cash (cash in hand)	Pre-identified families with fragile shelter status in coordination with DSWD and LGUs, with use of Vulnerability Index Tool	- MPCA: USD 60 / PHP 3,300 - CfS: USD 80 / PHP 4,400
WFP	- MPCA - GCT	Scenario 1: 24,908 Scenario 2: 20,000 (MPC) 2 groups (GCT)	- OTC FSPs: Western Union - Direct Cash (cash in hand) - Mobile wallets via MTNC codes - Bank transfers	- Pre-identified families registered in SCOPE, comprised of households in Listahanan and LGU datasets - DSWD 4Ps beneficiaries	- MPCA: USD 60 / PHP 3,300 - GCT: USD 5,000 (average)
UNICEF	SRSP top-up	Scenario 1 & 2: 20,000	Bank transfer: Land Bank	Subset of vulnerable population identified in DSWD 4Ps registry	USD 22 / PHP 1,200
UNFPA	- MPCA - GCT	Scenario 1 & 2: 1,300 (MPC) 4 groups (GCT)	Direct Cash (cash in hand)	- Pregnant women in third trimester - Vulnerable women, including GBV survivors, women with disabilities, solo mothers, female-headed households, persons living with HIV, and women in GIDA	- MPCA: USD 60 / PHP 3,300 - GCT: USD 2,000

FAO's MPC will target small farmers and fisherfolks, with WFP targeting vulnerable 4Ps beneficiaries and UNFPA reaching pregnant women in their third trimester and other vulnerable women including GBV survivors, female-headed families, solo mothers, persons with HIV, and women in GIDA. Considering operational realities and building on government emergency response efforts, the pilot is designed around a two-staged approach to MPC delivery. Whereas WFP, UNFPA, and FAO will trigger cash distribution 72 hours before landfall, IOM will conduct distributions in the vicinity of evacuation centres, which are part of government's mandatory pre-emptive evacuation procedures commencing about 72-48 hours ahead of landfall. In both cases, the pilot aims to demonstrate that acting early will ensure a more dignified, effective and faster approach to delivering humanitarian assistance.

To ensure there will be no duplication between multi-purpose cash approaches of WFP, FAO and IOM, under scenario 1, the agencies agreed to focus on different municipalities, with WFP targeting 16 municipalities in Region 5, while FAO will be targeting 14 municipalities and IOM 19 municipalities in both Region 5 and 8. Also for the purpose of learning, agencies will nevertheless overlap in several municipalities, where multi-purpose cash will be delivered by WFP or FAO, while in such instances IOM will only provide only shelter strengthening top-up in the evacuation centres. Where neither WFP nor FAO will provide blanket multi-purpose cash intervention, IOM will provide both the multi-purpose cash and sectoral top. This model should also allow for learning how different distribution models impact use of cash by beneficiaries.

UNICEF will adopt a different approach to anticipatory cash. Instead of providing MPC to independently targeted households, UNICEF will deliver shock-responsive top-ups of PhP 1,200 (US\$22) to the beneficiaries of the 4Ps, using a typical model of vertical expansion of the national social protection system. The recipients of the top-up – to be budgeted in the CERF at US\$22 to safeguard 7% buffer against exchange rate fluctuations – will receive it in addition to their regular social protection support and will be able to access the money using their existing Landbank ATM cards.

² The Minimum Expenditure Basket transfer value is calculated to last for one month (30days) for a household of five (average household size in the Philippines, outside of BARMM).

UNICEF will deliver the top-ups to support 42,200 children in order to finance their health, nutrition, WASH, education and protection needs and to allow vulnerable households with children to procure basic needs and continue to access time-sensitive services before the landfall and before services may be disrupted.

UNFPA will establish SRH and GBV Surge teams to evacuation centres and distribute MPC via local partners to pregnant and other vulnerable women. UNFPA's An MPC is designed to support the economic stability of vulnerable women and their families by reducing the economic shocks (that escalate interpersonal and household tensions which can catalyze gender-based violence) as well as alleviating adverse health events by providing access to providers and / or medical supplies.

As there will be less than 48h between the Readiness trigger and the Activation trigger, significant preparedness activities for cash distribution have been carried out in advance. Beneficiary registration, validation, as well as possible de-duplication will be implemented ahead of Readiness trigger activation. This is a significant investment in time and money that the agencies are making, as CERF anticipatory action pilot funding will not cover readiness activities if they occur ahead of Readiness trigger. For example, FAO, IOM and UNFPA have raised over \$1.3 million of internal funding to be spent for preparedness activities.

Priority interventions

Interventions by Food and Agricultural Organization (FAO)

Objective: FAO will work with OXFAM, CARE, and the PDRRN to reduce the impact of typhoon on the livelihoods (crops, fishes, and livestock) and increase the financial capacity of the most vulnerable farmers and fisherfolks ahead of pre-emptive evacuations.

Interventions: Upon raising of the readiness trigger, FAO will release the first set of agro-climatic early warning messages to communities. Information disseminated will include location and usage procedures for safe storage sites. FAO will provide multi-purpose cash assistance to 15,150 (Scenario 1) or 2000 (scenario 2) most vulnerable households of farmers and fisherfolks based on the beneficiary list from the government's Cash and Food Subsidy for Marginal Farmers and Fisherfolk (CFSMFF) Program. The target beneficiaries are farmers and fisherfolk registered in the Registry System for Basic Sectors in Agriculture (RSBSA). Cash assistance will help to protect the livelihoods of those anticipated to be affected by the incoming typhoon while supporting and reinvigorating local markets in potential affected areas.

FAO will also work with local fisherfolk organizations and communities to rent schools, local community halls, and places of worship to store critical livelihood items, such as boats and nets for fisherfolks. By providing safe-storage sites, the intervention will preserve hard-won development gains and key livelihoods. FAO will also issue agro-climate messaging to farmers and fisherfolks.

Recognizing the importance of supporting vulnerable agriculture and fisheries' livelihoods in target areas, the FAO-led interventions will adopt market-based approach and assist livelihoods of small holder farmers and fishers to generate income from the pre-emptive food needs as well as small merchants to serve as financial service providers of beneficiary households. This approach will help generate income to support vulnerable livelihoods that are anticipated to be affected by the incoming typhoon. Such interventions include cash for vulnerable livelihoods.

Interventions by International Organization for Migration (IOM)

Objective: The key objective is to mitigate the physical and socioeconomic harm induced by sudden evacuation of the most vulnerable population affected by typhoons, focusing on families living in houses made of light materials less durable to typhoons and in hazard-prone zones. It will supplement the local government's mandatory pre-emptive evacuation, which these vulnerable families will most likely be subjected to at the time of destructive typhoons.

Interventions: IOM together with Catholic Relief Services (CRS)/Caritas, World Vision, CARE, AADC and other local NGOs, will ensure evacuees have immediate access to Shelter Strengthening Kits through multi-purpose cash-based Interventions. The proposed activities seek to reduce the risk of COVID-19 infection and community transmission during the evacuation as well as minimize the socioeconomic strain and psychological distress derived from the displacement.

IOM will ensure that Internally Displaced Persons (IDPs) have access to safe and dignified living conditions at evacuation centres (ECs) at the onset of their pre-emptive evacuation. This will be done specifically by supporting the ECs in upholding

the COVID-19 CCCM Operational Guidelines, which aim to achieve minimum humanitarian standards including preventing COVID-19 transmission and other transmissible diseases at often congested camps and camp-like settings and delivery of modular tents. Through cash-based interventions (CBI), IOM will also facilitate immediate access to appropriate materials and tools for IDPs to repair their shelters right after typhoons' landfall. These interventions will alleviate grave stress from sudden displacement and promote early recovery, thereby contributing to prevention of prolonged displacement and mitigate socioeconomic loss from disasters. Each family will receive PhP 4,400 (USD 80) in cash transfers, which they can use to access nearby local stores and procure materials and tools to repair their damaged shelters based on their priorities. This assistance will be complemented with Multi-Purpose Cash Assistance (MPCA) of PhP 3,300 (USD 60 which includes 7% exchange rate buffer). The MPCA Amount has been harmonized across implementing CERF AA Agencies and transfer value has increased by PhP 50 to help ensure liquidity among FSPs. The MPCA Transfer Value is set at 1/3 of the Minimum Expenditure Basket (MEB) as the transfer is designed to cover critical basic needs for 10 days.

Interventions by United Nations Populations Fund (UNFPA)

Objective: Women, adolescent girls and transgender women especially the vulnerable have safe space, dignified access to protection services and participate in GBV risk prevention and response. Vulnerable women and girls have reduced risks from hazards that threaten their Sexual & Reproductive Health & Rights (SRHR) and are free from Gender-based Violence (GBV) and Sexual Exploitation & Abuse (SEA).

Interventions: Direct financial assistance (60USD /P3300) is provided to 600 pregnant women in their last trimester, and to 700 GBV survivors, women living in geographically isolated and disadvantaged areas (GIDA), persons with disabilities (PWDs), pregnant teens, and LGBTQIA+ headed families. This assistance aims to empower them to prepare for the typhoon and address immediate needs. MPCA transfer value has increased by P50 to ensure sufficient liquidity at Financial Service Providers (FSPs). The transfer value has been harmonized across all implementing agencies and has been set at 1/3 of the Minimum Expenditure Basket (MEB) as to cover critical basic needs for 10 days.

Community Cash Grants: Four Women-led organizations will receive funding (2,000 USD each) to facilitate preparedness activities within their communities before the typhoon makes landfall. This approach leverages local knowledge and leadership to tailor interventions to specific community needs.

UNFPA seeks to protect critical livelihood assets, ensure food security, and potential evacuation through a group/community cash grant modality disbursed to four local women-led organizations or groups. The grant is computed based on the costs of materials, transportation, and other supplies needed by the groups to undertake a range of anticipatory activities. This pilot anticipatory action also aims to address community consultations held as part of the ERC Flagship Initiative, which highlighted that protection of critical livelihood assets, and meeting critical basic needs, are primary concerns among communities in the proposed areas of intervention. These Flagship consultations also affirmed that these actions – protecting critical livelihoods assets and ensuring adequate food security – can be effectively delivered through community cash grant modality. Further aligning with the aims of the Flagship, this modality will work towards ensuring there is a community-led component of the CERF anticipatory action.

By combining these interventions, UNFPA Philippines aims to strengthen the resilience of vulnerable women and their communities, enabling them to better cope with the challenges posed by typhoons. This comprehensive approach addresses both immediate needs and underlying vulnerabilities, promoting a more inclusive and equitable disaster response.

Interventions by United Nations Children's Fund (UNICEF)

Objective: To implement a series of multi-sectoral anticipatory action interventions related to Education, Nutrition, WASH and Child Protection, that will ensure 48,000 children living in 20,000 households have sufficient resources to address their most immediate needs and are better able to mitigate impacts of a significant typhoon. In addition, 110,000 people will be reached through messaging on key lifesaving behaviors and preparedness actions.

Interventions: By using social safety net mechanism of the government, an unconditional cash transfer of \$22 (PhP 1,200) will be provided as a top-up, intended to finance the child-centered needs of vulnerable families that are projected to be impacted by a destructive typhoon. The inclusion of additional cash, representing a portion of the minimum expenditure basket computed for basic needs of children for health, nutrition, WASH, education, and child

protection, will allow the vulnerable households with children to procure basic needs and continue to access time-sensitive services before the typhoon makes landfall, and before services are totally disrupted.

Complementing the cash component will be a number of services and distributions made three days before landfall:

- **Distribution and tracking of nutrition supplies and commodities** (e.g. RUTF, CMV, ReSoMal, MUAC tapes) for health facilities, to ensure that LGUs will have a ready stock of key supplies that may be immediately deployed after a typhoon.
- **Delivery of water quality monitoring and treatment supplies and equipment** to Provincial Health Offices to allow for the immediate testing of water quality and appropriate treatment, thereby maintaining or immediately restoring access to safe water by the disaster-affected population.
- **Deployment of WASH frontline responders** at the provincial and municipal levels to conduct water quality testing and promptly report results.
- **Activation of Child Protection help desks and help lines** to prevent or mitigate abuse, neglect, exploitation, and violence against children by strengthening child protection systems and support families and communities in their protective functions.
- **Distribution of family preparedness checklists and various sectoral messages** on health, nutrition, WASH, protection, and education to equip families with vital information needed to reduce the impacts of the typhoon.

These anticipatory action interventions require inter-cluster coordination to ensure the harmonization in the content and delivery of key messages to target beneficiaries. Coordination will be ensured with the CERF AA Cross-Cutting team, to facilitate delivery of common protection messaging across all sectors.

Interventions by World Food Programme (WFP)

Objective: Provide blanket multi-purpose cash assistance for beneficiaries to initiate preparatory actions to protect their assets, lives, and livelihoods before the arrival of a forecasted destructive typhoon. Through this intervention, WFP's objective is to minimize the negative impact of typhoons on household food security and other essential needs, ensure survival and minimum living standards and enhance overall disaster preparedness.

Beneficiaries will be able to use cash assistance for the procurement of food stocks and other essential needs, as well as for the early harvesting of crops and livestock evacuation, among others.

Intervention: WFP's AA intervention has three key components: distribution of multi-purpose cash assistance to families and community cash grants to selected associations, early warning dissemination and messaging, and generation of robust evidence on the impact of AA. WFP will implement unconditional cash transfer, P3,300 (PHP 62 = USD 1) inclusive of transportation cost, to 25,000 households (HHs) beneficiaries in Albay, Sorsogon and Catanduanes provinces, in Region 5 (Scenario 1); and 20,000 HHs across Southern Leyte (Region 8) and Surigao del Norte (CARAGA) (Scenario 2) 3 days before the landfall of a Category 3 typhoon or higher. Selected associations will receive a community cash grant to protect critical livelihood assets ahead of typhoon landfall. The distribution of cash transfers will be facilitated through WFP's Financial Service Provider (FSP) Western Union. Including registered affiliates or directly to beneficiaries' mobile wallets. In areas with limited mobility or remote locations, WFP will distribute direct cash-in-hand through its Cooperating Partner (CP).

Other anticipatory action projects for tropical cyclones to be aware of

Interventions by OXFAM/ START Network

START Network members will be able to tap into funding from the Anticipation Fund of START Network, pending an alert is submitted by members in the Philippines and subject to the approval and allocation of the START Fund allocation committee, based on pre-agreed criteria and other factors (e.g. perceived capacity of government to respond, other actors responding, value added, etc.).

START Network set up a DRF system for the Philippines, funding that would be automatically released when a trigger is breached. As per current plans, DRF will be able to activate in target pilot areas in Surigao del Norte, Catanduanes and Eastern Samar. Resource mobilization activities are underway for this DRF project both for the Philippines and Bangladesh.

OXFAM will be able to activate its AA interventions for their BREADY project in Salcedo and SHARPER in Catanduanes, subject to the threshold set for activation and in concurrence with LGU partners.

Interventions by Philippine Red Cross (DREF)

The Philippine Red Cross Early Action Protocol is linked to the FbF by the DREF (Forecast based Action by Disaster Relief Emergency Fund) resulting in the automatic flow of funds to the chapters at-risk once the typhoon trigger is reached.

The typhoon Early Actions of the PRC will be triggered if the forecasted impact of the winds on housing, 72h before landfall, is more than 10% of houses predicted to be totally damaged in more than 3 municipalities. In terms of scale, PRC will activate in maximum three provinces (RC Chapters) at the same time with maximum amount of CHF 250,000.

Summary table

Organization	Partners	Cluster/ Sub-cluster	CERF Financing	CERF Financed Reached Population	Activities
FAO	Oxfam/CARE/ PDRRN	FSAC	1,586,881 (scenario 1)	15,150 agriculture- dependent and/or vulnerable families	Multi-purpose cash
FAO		FSAC	323,096 (scenario 2)	76,600 households	Messaging to farmers and fisherfolks
FAO		FSAC		600 households	Safe storage sites
FAO	Oxfam	FSAC		6 partner associations	Community cash grants
IOM	CRS/WV/Carit as		1,717,091 (scenario 1)	47,105 IDPs	CCCM Kits and IEC materials, inclusive of CCCM COVID-19 Operational Guidelines
IOM	CARE, ACCORD, Agri Aqua Development Coalition	CCCM	2,722,279 (scenario 2)	78,640 IDPs	Multi-purpose CBI (Shelter Strengthening Kits) and IEC materials*
UNFPA	ADRA, GNIP, ACCORD	GBV/SRH	675,919 (scenario 1)	14,550 women and girls	Provision of commodities to address SRHR (clean delivery kits) and protection (dignity kits, radios), to vulnerable women and girls,
UNFPA	ADRA, GNIP, ACCORD	SRH	643,327 (scenario 2)	14,550 women, girls	Community-level risk communications messaging for SRHR, GBV, mental health and psychosocial support (MHPSS), and PSEA, using radio stations
UNFPA	ADRA, GNIP, ACCORD	GBV		14,000 people	Distribution of non- conditional cash assistance for protection to families

UNFPA	ADRA, GNIP, ACCORD	GBV		women and adolescents	Monitoring GBV protection in pre-evacuation and distribution of GBV referral pathways
UNICEF	Plan/DSWD	CP/Educ/ Nutrition/ WASH	832,319 (scenario 1)	20,000 households (110,000 boys, girls, men, women)	Cash: Multi-purpose unconditional cash transfer for most vulnerable households to be provided as top-up
UNICEF	Plan, DSWD	CP/Educ/ Nutrition/ WASH		10,000 people	RCCE: Community engagement and dissemination of information and key messages on family preparedness, IPC, health, nutrition, hygiene, protection, and education
UNICEF	CWC, World Vision, DILG, PNP	Child Protection		1,000 women, girls and boys accessing protection, GBV risk mitigation, prevention, or response interventions	Strengthening of child protection systems (including activation of help desks and helplines)
UNICEF	NNC, DOH, LGUs, CSOs	Nutrition		1,000 Children; 1,500 pregnant and lactating women	Distribution of life saving nutrition commodities and supplies to targeted beneficiaries (RUTF, MUAC Tapes)
UNICEF	Plan International Pilipinas,	WASH		At least 10,000 vulnerable households supported by 3 provincial health offices (PHOs)	Prepositioning water quality monitoring & treatment supplies & equipment, basic COVID19 IPC supplies, and materials on WASH and COVID19 IPC
WFP	TBD	FSAC	2,270,954 (scenario 1) 1,668,876 (scenario 2)	24,900 HH for Scenario 1/ 20,000 HH for Scenario 2	Multi-purpose unconditional cash-based transfer

With PSEA as a cross-cutting area of intervention, all UN agencies and their implementing partners under the AA Pilot Project are required to integrate PSEA prevention and response into their priority interventions. A Guidance Note on What Humanitarian Entities Should Be Putting in Place Before, During, and After an Emergency for PSEA is being developed by the Philippine Inter-Agency PSEA Network to support the humanitarian work in the country on operationalizing the PSEA core principles and standards. [A certain percentage of funding is encouraged to be allocated for PSEA programming.](#)

5. Pre-agreed Financing

CERF

The Emergency Relief Coordinator agreed to allocate up to \$140 million from CERF to support a series of anticipatory-action interventions. All funds will be disbursed through CERF's Rapid Response window; CERF has not created a separate "Anticipatory Action" window.

CERF will disburse funds to anticipatory action pilots on a no-regrets basis once three conditions are met:

- Endorsement by the relevant Resident/Humanitarian Coordinator of the Anticipatory Action framework (this document) and the CERF application package comprising an application chapeau, agency-specific project proposals and agency-specific budgets (in annex); and
- Pre-approval by the Emergency Relief Coordinator of the Anticipatory Action framework (this document) and the CERF application package comprising an application chapeau, agency-specific project proposals and agency-specific budgets (in annex);
- Activation of either the readiness trigger or the action trigger within a maximum of two years from the ERC's pre-approval of the framework.

For the 2021/2022 anticipatory action pilot in the Philippines, the ERC has agreed to allocate up to \$7.5 million, which was subsequently extended until the end of 2024. In 2024, Scenario 1 will request USD 7.08 million in funding and Scenario 2 USD 5.36 million. Readiness costs in each scenario are 6% and 5% respectively. The pre-arranged financing agreement with CERF is in place for one severe typhoon event over a two-year pilot period from the moment this framework document is pre-endorsed and pre-agreed. During this timeframe, CERF disbursement is guaranteed once a trigger is reached.

As the CERF funding will be activated and distributed as automatically as possible immediately once the defined triggers are reached, CERF will rely on a streamlined application process to ensure that funds are disbursed to UN agencies quickly. This will involve pre-filling and pre-approving project proposals in advance and maintaining those documents on file until the readiness trigger or action trigger is reached.

CERF will disburse funds on a no-regrets basis as soon as either the readiness trigger or the action trigger is reached. While a portion of the fund can be used immediately upon disbursement for readiness activities, the remaining portion of the funding can only be used if and when an action trigger is reached. The amount of funding for readiness vs action activities will be clearly defined in the pre-approved project proposals and budget. The need to distinguish between these two cost categories in advance is important given the different potential scenarios, though in the context of the Philippines there is indeed only hours available between the two triggers and very few activities could be implemented in the readiness phase. Compared to other, more slow-onset pilots, preparedness activities will be critical.


Of note, readiness and activation triggers can be activated on the same day only if both are reached 4 days before forecast landfall. CERF would disburse 100% of the funds as per the pre-agreed project proposals. Agencies will do their utmost to deliver assistance as quickly as possible, within the 3-day timeframe envisaged by the project proposals. In practice, this means that some actions can no longer be carried out ahead of landfall. This scenario would provide additional learning opportunities to be discussed in the learning committee.

Highlighting challenges and limitations of the current financing model – preparedness costs

While financing is increasingly available to carry out anticipatory actions, collective anticipatory action at scale requires an investment in building the pilots. As with other CERF pilots, these “start-up costs” are incurred by participating agencies prior to the activation of a pilot set up effective anticipatory actions. In 2021, for example DREF revised its financing arrangements for the anticipatory action in the Philippines and allows for about a third of funds to be used for preparedness activities.

Anticipatory Action Partnership and Funding framework

AA Partnership and funding framework

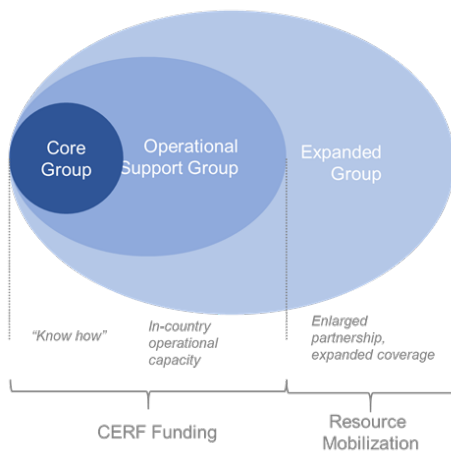

Considering significant interest among all the Philippines Humanitarian Country Team (HCT) partners to join humanitarian anticipatory action activities, the HCT sees the 2023-2024 typhoon season as a year when the humanitarian community in the Philippines is being invited to innovate with early action approaches, using CERF funding as a catalyst for it. Above all, the pilot has been identified as a learning opportunity between anticipatory action actors, humanitarian response community, the government, resource partners, private sector and local academia. While considerable funding has been secured by the CERF, additional funding opportunities are being actively pursued for the Expanded group of partners that will not directly benefit from the CERF funding.

IFRC DREF will activate FbF protocols if their trigger is reached. To be complementary with CERF, they will most likely not target the same municipalities.

6. Learning

OCHA has partnered with Kobo and the Harvard Humanitarian Initiative, to design an evaluation of the framework for Tropical Cyclones. The evaluation will measure the impact of AA interventions on households and communities and facilitate the learning from innovative pilots such as community cash grants and safe storage interventions. The data sharing agreement with implementing agencies is being reviewed by all parties involved to be ready and agreed in time before any potential activation in 2024.

From previous years without the third party organizations to conduct learning and evaluation, the agencies also agreed to a common post- distribution monitoring questionnaire to be rolled-out for cash interventions.

Agency-specific M&E: FAO

Objective

The impact analysis of FAO's AAs in the Philippines aims to assess whether the objectives of the intervention have been achieved. The analysis will focus only on FAO's interventions i.e. (1) multipurpose cash; (2) safe storage sites and (3) early warning messages. It will assess whether this assistance helped protect agricultural assets and food security of vulnerable households from the impact of a typhoon.

Activities

Quantitative Study

The following activities are envisaged to carry out the study:

1. Desk review on previous similar studies conducted in the Philippines and/or similar other contexts.
2. Preparation of the surveys and the data collection plan
3. Programming of questionnaires onto Kobo Toolbox
4. Training of enumerators
5. Pre-testing of the questionnaire

6. Sampling (based on sampling frames of beneficiary and control HH)
7. Data collection, either by phone or in person in the areas targeted by the project.
8. Analysis of survey
9. Presentation of the preliminary findings
10. Drafting of technical report and communication materials.

Qualitative Study – with individuals & donors

1. Preparation of survey questions and data collection plan
2. Programming of questions onto Kobo Toolbox (if required)
3. Training of interviewers
4. Data collection, either by phone or in person
5. Analysis of qualitative data
6. Presentation of preliminary findings (combined with above study)
7. Drafting of technical report and communication materials (linked to above study).

Outcomes

The following outcomes are envisaged from this analysis:

- Improved understanding of the benefits of AAs to protect agricultural livelihoods and food security ahead of sudden onset events such as typhoons.
- Lessons learned and programmatic insights on AA as a means to prevent and mitigate the impact of hazards, strengthening food security and building resilience of vulnerable households in hazard-prone areas.

Learnings on the role of FAO within the OCHA/CERF AA Pilots, and the role of coordination and scale for the success of the AA approach.

Agency-specific M&E: IOM

IOM will develop a monitoring framework that is context sensitive and aligned to COVID-19 protocols. The monitoring framework will define the methodology, frequency, tools and mechanisms for data collection which are most appropriate and effective for measuring activity, output, impact indicators as reflected in the results matrix. In line with the principles of Do No Harm, transparency and accountability to affected populations (AAP) mechanisms will be integrated into the framework.

IOM will use a range of data collection tools and methodologies, ensuring that they meet the requirements to effectively monitor diverse types of activities and outcomes. Given the rapidly changing operational environment in emergencies, IOM has prioritized flexibility and adaptability in the roll-out of data collection methods. Where possible, IOM will use the Kobo Toolbox to improve the speed and quality of data collection across project sites. As the project will cover some remote, isolated and hard to reach areas, as well as to remain adaptable to the changing dynamics of COVID-19 in the country, remote monitoring strategies will be implemented as necessary. In safeguarding the privacy of beneficiary information, IOM's institutional data protection and data security principles will be adhered to.

To ensure data quality and integrity, the project will benefit from three streams of data collection, validation and triangulation. Output-level results monitoring, through regular site visits and post-distribution monitoring make up the first stream. This will be done through site assessments and surveys using a representative sample. A secondary data gathering through focus group discussions, key informant interviews, and learning exercises with local stakeholders make up the second stream and will be used where possible to further verify data received.

At the end of the project, IOM will conduct an After-Action Review (AAR) of project achievements to date, focusing on effectiveness of implementation and strategies undertaken, issues that required corrective action, best practices and lessons learned. The AAR exercise will also result in the formulation of concrete recommendations to further strengthen the AA pilot exercise.

Agency-specific M&E: UNICEF

With the proper conduct of an Evaluation, UNICEF hopes to gain enough learnings on whether its Anticipatory Action interventions have prevented further losses and strengthened security of households in the short run.

Among the areas that can be assessed through the evaluation are:

1. If the AA support has increased prevention activities at the household level
2. If the AA support has reduced asset losses for families

3. If the AA support has reduced other coping strategies
4. If the AA support has sustained or increased child and family food consumption (at time of survey)
5. If the AA support has increased well-being among children and families (at time of survey)
6. If the AA support has an impact on family's ability for quick recovery

Specific to the sectors that will be covered by UNICEF, we also aim to learn the following from this pilot:

Cash	- To understand what mechanisms enable or hinder the use of existing national government social protection systems for anticipatory action or ex-ante disaster financing - To contribute to the policy dialogue on shock responsive social protection in the context of ex-ante interventions
RCCE	- To understand which communication interventions work best as entry points for multi-sectoral RCCE messaging - To understand better how two-way communication interventions can better work in the context of AA, given feedback mechanisms and possible opportunities for dialogue.
Child Protection	- To identify AA entry points for improving and providing more timely Child Protection response initiatives, particularly on preventing and responding to family separation, VAC/ GBV and SEA concerns. - To check feasibility of AA cash-based interventions to improve Child Protection in emergencies programming, particularly on improving help seeking behaviour for protection and MHPSS concerns.
Nutrition	- To determine the viable Nutrition-In-Emergencies (NiE) interventions for anticipatory actions - To establish operational knowledge of the Nutrition Cluster to deliver NiE Minimum Service Package - To identify AA principles and approaches that can be adapted in the strengthening of the NiE planning and implementation of the National and local sub-clusters
WASH	- To get a sense of effectivity of utilising cash transfer programming in the distribution of basic hygiene supplies over in-kind distribution - To determine if anticipatory action could contribute to better promotion of maintaining good health and hygiene during disasters and emergencies and better prevent spread of (water-borne) diseases - To identify further capacity-building needs of responder at the local level, e.g., provincial health offices, to deliver immediate and critical WASH responses, e.g., on water quality monitoring and treatment
Education	- To identify Education items households spend on in the context of anticipatory action - To analyse the communication materials to support the rapid dissemination of messages related to education <u>and how it affects</u> the Education-related expenditures of the households

Independent impact evaluation

Assessments of past anticipatory action interventions have shown several positive outcomes. They show that AA has reduced food insecurity during monsoon floods, improved preparedness and response capabilities, and reduced adverse effects during droughts.

However, several knowledge gaps persist. These include the need for comprehensive assessments that investigate unintended effects as well as long-term impact, the extent to which local knowledge and systems are integrated, the effectiveness of AA governance structures, the efficiency of different modalities and timing of interventions, as well as a robust evaluation framework.

Evaluation and learning are central to all OCHA-facilitated Anticipatory Action Framework. Evidence on the impact of anticipatory action is essential to mobilize global political and financial support for AA and to further scale up the efforts. Without this, the humanitarian system will struggle to secure investments to protect more people against shocks in more

places, as well as crowd in development agencies, IFIs and governments. In that regard, the learning and evidence generated from Philippines will greatly benefit anticipatory action efforts across the globe.

To maximize the learning from the Philippines pilot in the event of activation, OCHA has partnered with Kobo (an international humanitarian non-profit organization) and researchers at the Harvard Humanitarian Initiative, to design an evaluation of the framework for Tropical Cyclone. The evaluation will measure the impact of AA interventions on households and communities and facilitate the learning from innovative pilots such as community cash grants and safe storage interventions.

Methodological approach

The central objective of the evaluation will be to assess the impact of OCHA-supported anticipatory action programs on the well-being of registered beneficiaries. The evaluation will use a mixed-methods community-centered approach that primarily focuses on community experiences and perceptions.

The evaluation will focus on four central evaluation questions (EQ) and a number of topics or themes for each:

EQ1: People & community: How do anticipatory actions engage and affect the community members in terms of awareness, preparedness, and overall well-being?

EQ2: Resources & tools: How effective are the resources and tools provided for anticipatory action in preparing the community for, and recovering from, cyclones?

EQ3: Processes & mechanisms: How well do the processes and mechanisms in place support the timely implementation and effectiveness of anticipatory actions?

EQ4: Governance & accountability: How appropriate and effective are the governance and accountability structures in enabling and supporting anticipatory actions?

To ensure that research findings are timely and connected to a specific activation in the 2024/2025 period, Kobo will undertake, within 1-2 months of activation, a post-activation data collection, sampling from agencies' registered beneficiaries in areas where activation occurred, as well as comparable groups not targeted by the activation, and local authorities.

Survey respondent groups and data collection instruments

To get a complete picture of the impact of anticipatory actions by UN agencies and other partners, survey instruments will be designed to gather the experience of various stakeholders and groups. For this evaluation, three survey instruments will be created and used:

Instrument 1 – Population affected by the disaster: This instrument will gather the experiences of a selected sample of households from the wider affected population.

Instrument 2 - Control group: This instrument will focus on households in vulnerable areas within the same municipalities that are not participants of agencies' AA programs and activities. The instrument for the control group will be very similar to Instrument 1, barring any questions that are specific to actual assistance received.

Instrument 3 – Local authorities: This instrument will gather feedback and experiences of local authorities at different administrative levels regarding agencies' AA programs and activities.

Study design and sampling data requirements

The study design and sampling plan will be confirmed and established in more detail once details about participating agencies and locations have been confirmed. This will include:

- **Pre-activation qualitative interviews with local** leaders in potential areas of activation (pending confirmation from OCHA).
- **A post-activation survey among individuals (n=500) who received support** within the framework of anticipatory action.

- **A post-activation survey among individuals** (n=500) in the area of activation but **not included in programmatic support**.
- Qualitative interviews with local leaders in areas of activation.

For this plan to succeed, the evaluation team needs to access data about households that are part of AA programs. For sampling purposes, participating UN Agencies in activation areas will be asked to provide the evaluation team with the basic beneficiary data to assist with sampling.

Specific indicators for cross-cutting issues

PSEA: A PSEA indicator is proposed to ensure a system-wide approach across the AA Pilot Project wherein all UN agencies and their implementing partners will contribute to the implementation and monitoring of a common indicator, that is, “Number of children and adults who have access to a safe and accessible channel to report sexual exploitation and abuse by personnel who provide assistance to affected populations” (IASC PSEA Indicator 2.1.C). Further details can be found in the IASC PSEA Core Indicators – Guidance Note – Second Edition 2024 [IASC PSEA Core Indicators Guidance Note 2nd Edition 2024.pdf \(interagencystandingcommittee.org\)](#)). Segmental Disaggregated Data: report data disaggregated by gender, age, disability status and other intersecting factors (e.g. ethnic minorities, LGBTQIA+ individuals) alongside with PSEA guidelines.

Advocacy and public communication

At the request of the RC/HC, the UN agencies and partners agreed to put strong emphasis on communication activities also to ensure communicating as “One UN” and communicating the story before, during, and after the AA response. OCHA prepared an **operational communications plan** for the project, including key messages, communication activities, available resources and approach to communicating impact as well as commitment on accountability and transparency.

The focus of communications efforts will be on demonstrating that Anticipatory Action is not only possible from an operational and practical point of view, but that acting prior to the onset of a predictable shock is significantly faster, more dignified, and more effective than traditional humanitarian response.

The targeted audiences for this communication plan are humanitarian donors (including CERF donors, but not exclusively), the Government of the Philippines and other stakeholders in the humanitarian community.

Detailed and audience-tailored key messages will be developed by the communications working group in order to guide the messaging of all products, talking points, and activities.

This communication plan will focus on delivering activities and products that are guided by the following principles:

- Communications as “One UN” and “One Humanitarian Country Team.” While it is expected that individual agencies will won’t to produce their own specific communications, this plan will ensure complementary messaging and the delivery of joint products and materials that can be adapted as needed.
- Focus on affected people. The content and story gathering will focus on how Anticipatory Action can have a real human impact on people caught in humanitarian crises. This will include the stories of affected people whose story we will tell before and after the cyclone.

7. Annexes

Annex 1 - Anticipatory Action: Summary table

AGENCY	IMPLEMENTING PARTNERS	INTERVENTION	PREPAREDNESS ACTIVITIES D- 7/6 days	READINESS ACTIVITIES D -5/3 days	AA ACTIVITIES D -3/0 day
FAO	OXFAM/PDRRN/CARE	Cash (multi-purpose)	Validation of pre-registered beneficiary lists	Beneficiary lists are finalized and communicated to the Bank	FAOR approval for bank transfer given to the Bank (assumes AA)

			Validation of mapped financial service providers (FSPs)	Participate in national/local PDRA meetings	funding is pre-positioned in FAO account) - Bank executes fund transfer to beneficiary accounts - Beneficiaries receive their cash in account or receive their transaction number in payout centers or in digital wallets
	OXFAM/PDRRN/CARE	Cash for vulnerable livelihoods	Standby / Monitor	Beneficiary lists are finalized	Beneficiaries receive their cash in account
		Messaging to farmers and fisherfolks	Finalize messaging specific to areas and sectors based on forecast track and impact	Issue Advisory # 1	Issue Advisory # 2
	Fisherfolk Organizations 400 households	Conditional cash transfer of fishing boats to safe-storage sites	Prepare the pre-identified safe storage sites, ensure availability and safety (else identify alternative options)	- Disseminate locations of safe storage sites and opening schedule Again - Review SOPs on the operation of the safe-storage site	- Beneficiaries start to evacuate livelihood assets into safe sites - Ensure livelihood assets are properly tagged with owners' names - Ensure safe storage sites are secured by a guard
AGENCY	IMPLEMENTING PARTNERS	INTERVENTION	PREPAREDNESS ACTIVITIES D- 7/6 days	READINESS ACTIVITIES D -5/3 days	AA ACTIVITIES D -3/0 day
UNICEF		RCCE: Community engagement and dissemination of information and key messages on family preparedness, IPC, health, nutrition, hygiene, protection, and education	inter-cluster coordination to ensure the harmonization in the content and delivery of key messages to target beneficiaries.	- Printing and delivery of rapid assessment forms, anticipated communication materials (life-saving information) - Deployment of communication equipment - Discussion with LGUs on the establishment/use of feedback mechanisms	- Dissemination of key communication/information materials through various communication channels - Dissemination of information on hotlines and information centers - Mobilization of frontline workers to support RCCE anticipatory actions
	DSWD	Sectoral Cash: Unconditional cash transfer for child-centered needs	Coordination with DSWD and LandBank	Generation of list of households with children from DSWD Listahan	Confirmation is provided to DSWD/Landbank to include UNICEF top-up payments in their distribution; DSWD distributes through their FSPs which then credits to beneficiary accounts
	CWC, PNP, Plan International Pilipinas	Strengthening of child protection systems	Promotion of messages on preventing family separation; as well as abuse, violence, exploitation of children.	- Updating of referral pathway, facilitate its adaptation, and dissemination of by inter-agency members including recognizing signs of VAC. - Activation/ sensitization of helplines to support affected families in reporting concerns on protection, and access protection services. Activation or sensitization of helplines to provide MHPSS services. - Establishment of child protection help desks or screening points at key locations (such as reception and arrival areas, schools, food distribution centres, hospitals, etc.) and/or during	- Identification and activation of PNP VAWC/ Child Protection focal points at proposed evacuation centers. - Operational mobilization costs for Child Protection focal points to support coordination, communication, and transportation during emergency response. - Activation of Community Facilitators to support safe spaces, peer to peer activities, focused non-specialized psychological support, or referrals to specialized mental health clinical care.

				planned population movements to identify and prevent family separation.	• Movement of CFS tents (if deemed necessary) and other MHPSS supplies to critical installations/ locations. • Refresher orientation of staff and preparation logistical equipment for case management and immediate family tracing and reunification (FTR)
	NNC, DOH, LGUs, Plan International Pilipinas <i>health facilities</i>	Distribution of life saving nutrition commodities and supplies.	• Cluster coordination: inventory of health facilities in CERF AA areas; mapping of facilities that can provide alternative/surge support for nutrition and health services to typhoon-affected areas; and determining surge support capacities and agreements with LGUs. Access (NINA) Nutrition Initial Needs Assessment	• Distribution of child and adult MUAC tapes and intensified MUAC screening of PLW of children U5 will be completed.	• Delivery of and replenishment supplies to facilities where needed and surge of cases or acute malnutrition is anticipated.
	Plan International Pilipinas	WASH and COVID19 IPC	• Capacity-building (training) on WASH in Emergencies, including water quality monitoring & treatment and COVID19 IPC, for WASH and Health response personnel at provincial/PHO level, including formulation of emergency response plans • Procurement of water quality monitoring & treatment supplies and equipment (portable water testing equipment, e.g., PML, CBT, chlorine granules, sodium hypochlorite products, e.g., Aquatabs, Hyposol, etc.) and basic COVID19 IPC supplies (face masks for both adults and children, face shield, etc.) at the UNICEF PCO level • Setting up of digital water quality monitoring information management (IM) system (including reporting), e.g., Kobo Collect • Printing of WASH-COVID19 IEC materials • Provision of one (1) unit of water treatment unit (WTU) specifically in San Andres municipality in Catanduanes Province but with the intention of serving other municipalities that will be impacted by the typhoon in coordination with the provincial LGU	• Deployment of water quality monitoring & testing supplies & equipment, basic COVID19 IPC supplies, and WASH-COVID19 IEC materials in the target provinces/PHOs • Pre-testing of digital water quality monitoring IM system, including reporting system	• Prepositioning of water quality monitoring & treatment supplies, basic COVID19 supplies, and WASH-COVID19 IEC materials in the target LGUs/PHOs • Refresher training on water quality monitoring and treatment for WASH and Health personnel previously trained in the target PHOs • Activation of digital IM system for water quality monitoring • Distribution of IEC materials on WASH-COVID19 in line with pre-emptive evacuations being implemented by the LGUs, e.g., in designated evacuation sites

AGENCY	IMPLEMENTING PARTNERS	INTERVENTION	PREPAREDNESS ACTIVITIES D- 7/6 days	READINESS ACTIVITIES D -5/3 days	AA ACTIVITIES D -3/0 day
WFP	National Confederation of Cooperatives	Multipurpose cash assistance	- Coordination and information dissemination to WU and all local partners, e.g. PLGU, MLGUs - Capacity strengthening of partners and updating of SOPs to include measures to protect critical livelihood assets	- Coordination and information dissemination to WU and all local partners, e.g. PLGU, MLGUs - Participation in PDRA meetings - Information dissemination to Benes through SMS - Prepare payment advice files for WU - Coordination with local authorities on physical distribution of MTCNs - Setting up of CFM mechanism with NGO partner	- Final advisory to WU on activation - Delivery of MTCNs via SMS - Distribution monitoring - Physical distribution of MTCNs to beneficiaries with no cellphones - Distribution of cash in places with no SMS
	National Confederation of Cooperatives	Multipurpose cash assistance - sensitization	Coordination with Barangay LGU (BDRRC) and purok heads	Release of printed MTCN + community sensitization in the Barangay in coordination with the LGU; coordination with WU branches for an anticipated cash distribution and ensure minimum health protocols are followed in WU branches; ensure CFM mechanisms followed/implemented	
AGENCY	IMPLEMENTING PARTNERS	INTERVENTION	PREPAREDNESS ACTIVITIES D- 7/6 days	READINESS ACTIVITIES D -5/3 days	AA ACTIVITIES D -3/1 day
IOM	World Vision with CRS-Caritas	Multi-purpose cash assistance + Sectoral Top-up (Shelter)	Monitoring of PAGASA Typhoon Advisories; Deployment of Mobile IOM and IP AA Teams; Participation in PDRA meetings at Provincial/Municipal levels; Monitoring of Municipal Pre-Emptive Evacuation Plans; Alerting of target Barangay LGUs and Families; Alerting of Palawan (FSP) branches; Alerting of local hardware stores, grocery stores for AA purchases of beneficiaries	Monitoring of PAGASA Typhoon Advisories; Participation in PDRA meetings at Provincial/Municipal levels; Monitoring of Municipal Pre-Emptive Evacuation Plans; Alerting of target Barangay LGUs and Families; Advice Palawan on final number and list of MTCA recipients, transfer funds; preposition IOM & IP AA teams; monitor pre-emptive evacuation announcement of LGUs; Finalization of beneficiary lists and local suppliers list; Prepositioning of modular tents and IEC materials; Alert the target beneficiaries through SMS	Monitor the pre-emptive evacuation of the target families to ECs and host houses; Facilitate and monitor MPCA pay-out at Palawan on day 1 & 2 once people are already in ECs/host houses; ensure that all listed beneficiaries have received the MPCA at end of day 1 & 2; Distribute modular tents and IECs; facilitate and monitor visits of beneficiaries to grocery stores, markets, hardware stores (for recipients of SRKs); monitor the Shelter Strengthening activities of SRK recipients; monitor and ensure that all beneficiaries are already in the ECs on day 3
	CARE with ACCORD & Agri Aqua Development Coalition				
AGENCY	IMPLEMENTING PARTNERS	INTERVENTION	PREPAREDNESS ACTIVITIES D- 7/6 days	READINESS ACTIVITIES D -5/3 days	AA ACTIVITIES D -3/0 day

UNFPA	ACCORD, GNIP	A. Provision of Multi-purpose cash for Health for Pregnant and vulnerable Women	• Activate SRH and GBV Sub cluster coordination group • Alert warehouse and logistics providers • Prepared activation of Annual Workplans with implementing partners • Meeting with implementing partners for Re-orientation of AA action plans • Meeting with local actors to discuss readiness and activation actions.	• Re-orientation of barangay health care workers and community leaders • Re-orientation of community-based volunteers on cluster GBV actions including Referral Pathways • SRH, GBV, and PSEA information and dissemination for risk mitigation Transportation of dignity kits, printed SRHR and protection referral pathways •	• Establishment of SRH and GBV Surge teams • Printing and distribution of Localized GBV and MHPSS Referral Pathways • Procurement and distribution of SRH and protection commodities • Distribution of non-conditional cash for pregnant and vulnerable women • Support relocation of health/birth facilities at risk. • Community-level risk communications • *Procurement is for replenishment of supplies •
	ADRA, GNIP	B. Provision of SRH and protection commodities to pregnant, vulnerable women and girls C. Support relocation of health/birthing facilities at risk			

Annex 2 – DRAFT trigger messages

Readiness trigger message

From: Gustavo Gonzalez, RC/HC

To: CERF secretariat

CC: OCHA Philippines, Core Group

Dear CERF secretariat,

The readiness trigger has been reached as based on PAGASA and ECMWF data a Tropical Cyclone with potential to reach category level 2 or higher (greater than 154 km/h maximum 1-minute sustain wind speed/136 km/h 10-minutes sustain wind speed) is projected to directly impact areas within Region 5 and 8 (*or Region 8 and 13*). Scenario 1 under the Framework is now activated for readiness. Scenario 1 funding requirement is USD 7.08 M for FAO, IOM, UNFPA, UNICEF and WFP. (*Scenario 2 under the Framework is now activated for readiness. Scenario 2 funding requirement is USD 5.36 M for IOM, FAO, UNFPA and WFP.*)

Details are attached.

Grateful for your swift attention to this notice.

Sincerely,

Gustavo Gonzalez, RC/HC

Activation trigger message

From: Gustavo Gonzalez, RC/HC or OCHA Philippines Head on his behalf

To: Core Group

CC: CERF secretariat

Dear Core Group,

Since the readiness trigger has been reached, the Triggers Team together with HDX and 510 monitored every 6-12 hours the forecast model and its predictions on the number of totally damaged houses.

Based on the latest impact map, activation threshold has been reached as the predicted number of destroyed houses amounts to [XXX] with [xx%] probability, which falls within the range of 50% probability that 50,000 houses or more will be totally damaged and 85% probability that at least 8,000 houses will be destroyed.

Since we have activated for readiness Scenario 1 (*Scenario 2*), we are therefore activating the CERF anticipatory action Framework for Scenario 1 (*Scenario 2*) within the 72 hours (3 days) before projected landfall.

Further details are attached.

Good luck to the teams implementing anticipatory action interventions; stay safe!

Annex 3 - Evaluation of forecasts for anticipatory actions - April 2021

In April 2021, OCHA, Humanitarian Data Centre and the Philippines AA Core Team facilitated discussion among stakeholders about humanitarian anticipatory action work, especially focusing on the various forecasting models developed for typhoon early action.

The team discussed the models currently developed by three key actors (WFP, IFRC/DREF, Global Parametrics) to reach a conclusion on which model would be the most appropriate and what modifications may still be needed.

After careful review and consideration, the recommendation was made to move forward with the IFRC/DREF Typhoon model. We weighed several factors in coming to our decision, and here we will highlight what we consider to be our primary concerns.

Firstly, due to the tight timeline, we wanted to prioritize a model that can be operationalized quickly. The IFRC/DREF model has a demonstrated track record of being operational in a humanitarian context, for the full country down to an admin 3 level. Furthermore, using the same model as IFRC (even with modifications) could help foster interagency coordination.

A second major benefit of this model is that it is open source and free to use, which gives flexibility to modify or alter it to fit our needs, and allows us to freely share the full process as well as the model outputs with our partners, maximizing transparency, accountability and cost effectiveness.

Finally, the IFRC/DREF model developers are keen to address any possible shortcomings of the model, such as integrating PAGASA forecast data.

Find below the [Evaluation matrix](#) used to provide this recommendation and a summary of the three models considered (IFRC/DREF, Global Parametrics and WFP)

Evaluation Matrix

Criterion	IFRC/DREF	Global Parametrics	WFP
Is the trigger based on existing, public forecast data?	Yes: ECMWF tropical cyclone and wind speed forecasts	Yes: use public forecasts from agencies including: National Hurricane Center (NOAA), Central Pacific Hurricane Center (CPHC), Joint Typhoon Warning Center (JTWC), Hydrometeorological Prediction Center (HPC), Ocean Prediction Center (OPC), Fiji Met Service (RSMC Nadi), New Zealand Met Service (TCWC Wellington), METEO France, Australian Bureau of Meteorology (TCWC Darwin), Japan Meteorological Center, ECMWF, etc. However, also use private data such as PAGASA.	Yes (CHIRPS, ERA5), but also uses PAGASA data which is not available to the public
Does the model make use of PAGASA data?	No, but 510 Global is looking into it	Yes	Yes
Is the trigger simple, straightforward and easy to understand?	Partially: Uses a machine learning model to determine relationship between wind speed and housing damage.	Partially. The threshold is simple and based on the probability of a wind speed above a certain value occurring in a location. Several vulnerability indicators are combined to establish what the threshold should be.	Yes, very simple threshold based on rainfall anomaly %
Is the trigger impact basis appropriate for our partner's needs?	Yes. The trigger is based on expected impact (percentage of houses destroyed)	Yes. The trigger is based off the windspeed intensity that leads to an expected impact (eg percentage of houses destroyed)	Yes – people affected

Is the trigger forecast relatively easy to monitor at regular intervals?	Yes	Yes	Yes
Does the trigger provide us with adequate lead time?	Yes (72 hours or more)	Yes (72 hours or more)	N/A - The model doesn't use forecasted hazards data
Can the trigger be adapted to OCHA specifications by June?	Yes	Partially. It would require effort and budget. The model doesn't currently cover the full country	Likely not
Can we obtain the model output as data that we can edit and share?	Yes	Yes	Probably
Is the model open source?	Yes	No, but it could be	No, but it probably could be.
What would be the cost to get the model operational?	Low. The model is open and fully available.	Medium. Global Parametrics would need to provide a quote and a proposed timeline for this work.	Unclear
What would be the cost to keep the model operational?	Low. The processing is fully automated. Possibility of cost sharing maintenance costs with IFRC/DREF	Likely low to medium.. Global Parametrics would need to provide a quote	Unclear
How well does the model perform?	Precision, recall ~70% for classification model	The model has been running since 2019 and has accurately called the major storms that have passed.	Precision: 17% for Bicol

IFRC/DREF model card

Model Card - IFRC/DREF	
Model Summary - Main contacts: - Aklilu Teklesadik (ATeklesadik@redcross.nl) - Marc van den Homberg (MvandenHomberg@redcross.nl) - Link to model: presentation slides, GitHub 1. Intended Use A. In-scope use cases: what is the actual and potential scope of the model? a. What is the main output of the model? - Map of predicted percentage of completely damaged buildings per municipality b. What is the geographical scope? - All of the Philippines, down to municipality resolution (admin level 3) 2. Model Development A. Details of the datasets used to build the model. a. What hazard data is used? - ECMWF tropical cyclone and wind speed forecasts b. What vulnerability data is used?	


- Housing damage reports from [NDRRMC](#)
- B. Methodology - provide a description of the different analysis steps and how the input datasets are used to train the model.
- Typhoon track fields calculated using [Willoughby methodology](#)
 - Use XGBoost to correlate wind speed with damage as a function of building materials
- C. How is the trigger threshold defined? What are the known limitations?
- 10% houses totally damaged (as defined by DROMIC reports) in at last 3 municipalities (1 in 5 year)
 - Use both classification and regression model, and activate if either is above threshold (but for prioritization of areas, use regression model)

3. Model Evaluation

- A. How well does the model perform? Which metrics are used to evaluate it?
- Classification: Precision / Recall / F1 are all ~0.7 on test set
 - Regression: mean absolute error (MAE) 3%, root mean squared error (RMSE) 7% on test set
- B. How does performance depend on forecast lead time?
- Forecast worsens significantly with lead time, thus performance is reduced

4. Operational Readiness

- A. Is the model ready to be used to inform humanitarian response?
- a. Is the model kept up-to-date with the latest datasets?
- The model is updated continuously with previous storms and damage reports
- b. Who is responsible for model updating and/or recalibration?
- Aklilu Teklesadik, Marc van den Homberg
- c. Is the model ready to be deployed for use as an AA Pilot trigger? If not, what are the additional steps needed?
- TBD: need to explore if can be used for people impacted instead of houses damaged
- B. Has the model previously been used in humanitarian situations? Is it currently being used by humanitarian organizations for the 2021 typhoon season?
- Yes, used since 2019, including:
 - Tisoy 2019 (small scale)
 - Ulysses 2020
 - However, missed Goni (2020)

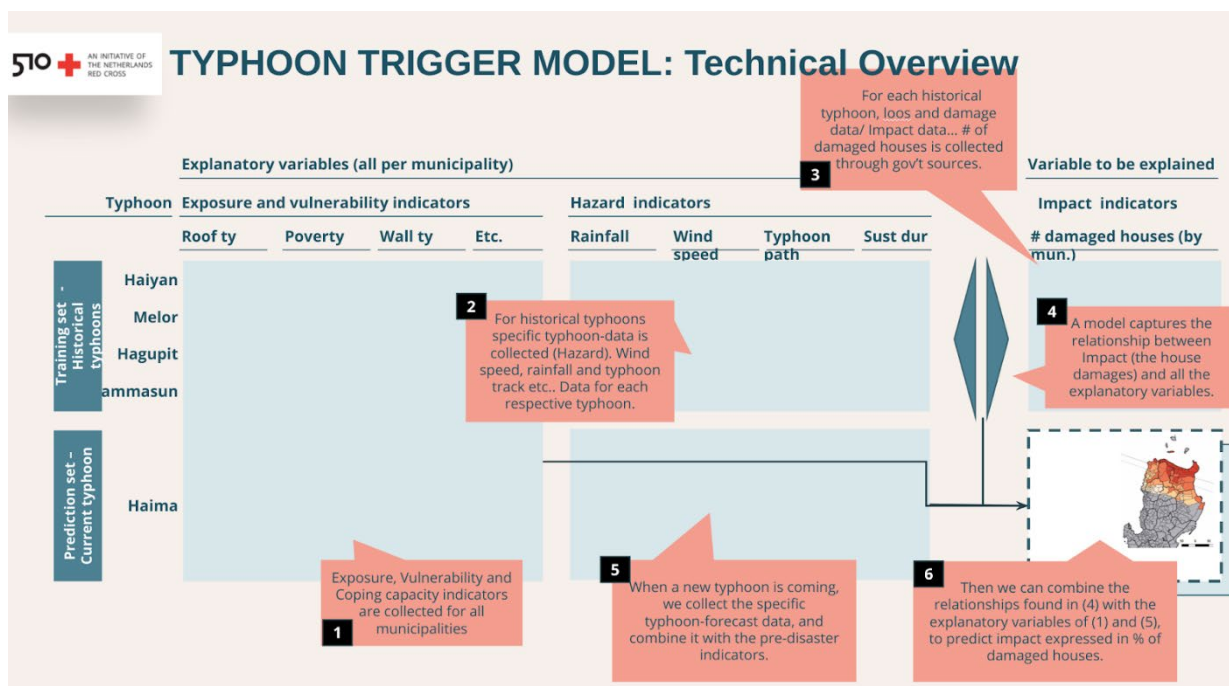

Global Parametrics model card

Model Card - Global Parametrics

Model Summary

- Main contacts:
 - Toby Behrmann (tbehrmann@globalparametrics.com)
 - Wendy Smith (wsmith@globalparametrics.com)
- Link to model: [presentation slides](#)

1. Intended Use

- A. In-scope use cases: what is the actual and potential scope of the model?
- a. What is the main output of the model?
- The probability of exceeding a specific wind speed (based on percentage of forecasts) at a particular location
- c. What is the geographical scope?
- Salcedo, Eastern Samar – currently being expanded in the Philippines

2. Model Development

- D. Details of the datasets used to build the model.
1. What hazard data is used?
 - Typhoon data from NASA, UKMET, NOAA, CPHC, JTWC, HPC, OPC, RSMC Nadi, TCWC Wellington, METEO France, TCWC Darwin, Japan Meteorological Centre, ECMWF, PAGASA
 - b. What vulnerability data is used?
 - Socioeconomic and damage data provided by Oxfam (Primarily construction of houses)
- E. Methodology - provide a description of the different analysis steps and how the input datasets are used to train the model.
- Typhoon track wind fields computed for each model & ensemble member
 - At each exposure location, if ≥ 5 tracks available, compute fraction above threshold
- F. How is the trigger threshold defined? What are the known limitations?
- Two components: wind speed, and probability. Tuned through internal vulnerability assessment.

3. Model Evaluation

- C. How well does the model perform? Which metrics are used to evaluate it?
- Model performance has been validated historically and real time since 2019. Full data is available.
- D. How does performance depend on forecast lead time?
- The main source of error is represented by the input typhoon models considered. The performance of the impact model is not dependent on forecast lead time.

4. Operational Readiness

- C. Is the model ready to be used to inform humanitarian response?
1. Is the model kept up-to-date with the latest datasets?
 - Yes, it is constantly running and kept up-to-date
 - b. Who is responsible for model updating and/or recalibration?
 - Global Parametrics (Alin Radu, Thom Johnson)
 - c. Is the model ready to be deployed for use as an AA Pilot trigger? If not, what are the additional steps needed?
 - Model is ready to deploy, would need the addition of new geographies
- D. Has the model previously been used in humanitarian situations? Is it currently being used by humanitarian organizations for the 2021 typhoon season?
- Oxfam tested trigger against tropical cyclones in 2019 & 2020 season (3 key events captured)
 - Next steps (in 2021) are to further validate model and increase geographical scope




Methodology

TC Phanfone

Date: 22-12-19

Time: 00:00:00

50 m/s
5 m/s

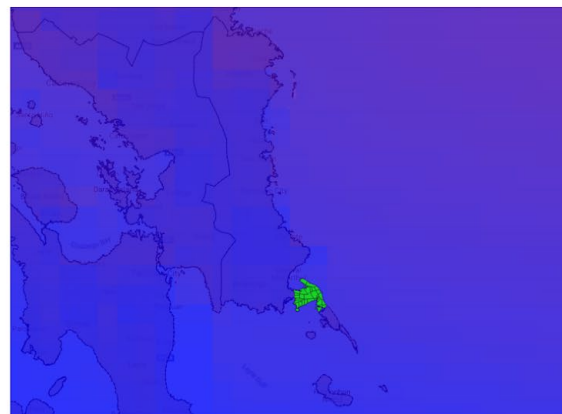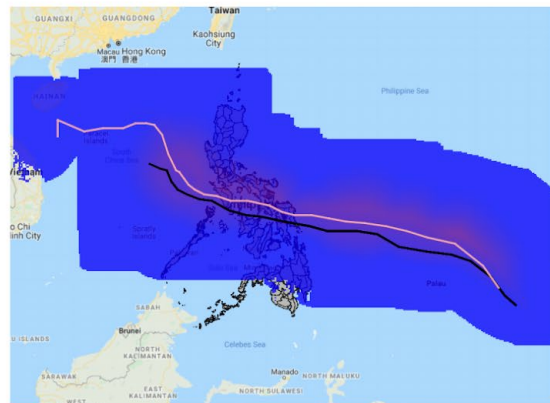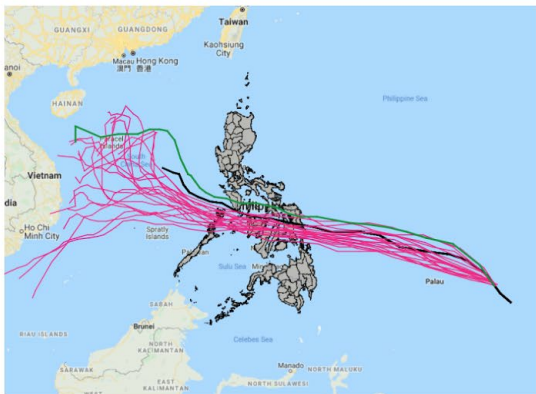

12

GP GLOBAL PARAMETRICS

WFP model card

Model Card - WFP

Model Summary

- Main contacts:
 - Analuisa Candanedo (analuisa.candanedo@wfp.org)
- Link to model: [Presentation slides](#)

1. Intended Use

- B. In-scope use cases: what is the actual and potential scope of the model?
1. What is the main output of the model?
 - Anomalous rainfall percentage, and trigger threshold for impact
 - b. What is the geographical scope?
 - Full national coverage, with analysis done on individual regions (admin level 2)

2. Model Development

- G. Details of the datasets used to build the model.
1. What hazard data is used?
 - NOAA IBTracks storm track frequency
 - CHIRPS & PAGASA precipitation anomalies
 - b. What vulnerability data is used?
 - Relief web (number of people impacted)
- H. Methodology - provide a description of the different analysis steps and how the input datasets are used to train the model.
- Use binary classification for people affected in vulnerability data (affected / not affected)
 - Create vulnerability and socioeconomic index, combine with hazard to get risk index

I. How is the trigger threshold defined? What are the known limitations?

- Use ROC curve to select precipitation anomaly threshold

3. Model Evaluation

E. How well does the model perform? Which metrics are used to evaluate it?

- For Region V (Bicol), ROC curve selection results in 17% precision with optimal rainfall anomaly threshold of 28%

F. How does performance depend on forecast lead time?

- N/A

4. Operational Readiness

E. Is the model ready to be used to inform humanitarian response?

1. Is the model kept up-to-date with the latest datasets?

- Not specified

b. Who is responsible for model updating and/or recalibration?

- Not specified


c. Is the model ready to be deployed for use as an AA Pilot trigger? If not, what are the additional steps needed?

- Would need to switch from real-time data to forecast, and possibly from rainfall to wind speed

F. Has the model previously been used in humanitarian situations? Is it currently being used by humanitarian organizations for the 2021 typhoon season?

- Not yet. The development so far has focused on creating a transparent trigger mechanism to use for response. To start using for AA, they will need to switch to using forecasts instead of real-time data.

HAZARD TIMELINE – Region V

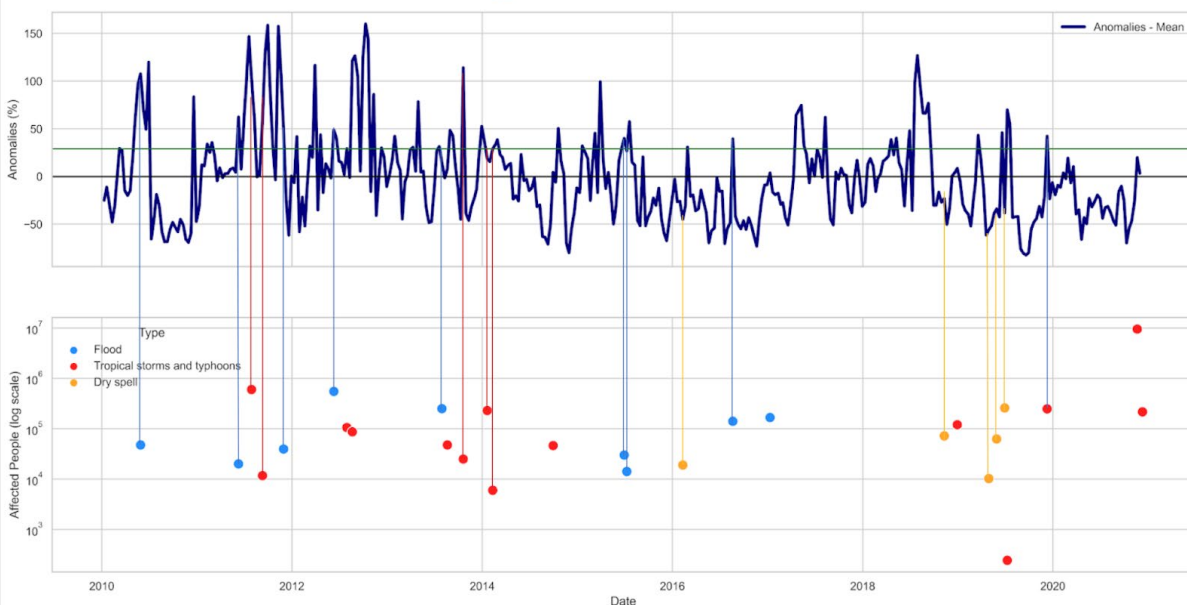

Annex 4: Contact Information

Agency	Name	Email
FAO	Ruth Georget	ruth.georget@fao.org
FAO	Sandro Pantua	sandro.pantua@fao.org
IOM	Kimberly Go Tian	kgotian@iom.int
UNFPA	Maria Lourdes Eudela	eudela@unfpa.org
UNICEF	Ziaul Hassan	mzhassan@unicef.org
UNICEF	Kamille Ruiz	kruiz@unicef.org
UNICEF	Jeonoah Kali Fornoles	jfornoles@unicef.org
WFP	Edlin Lumanog	edlin.lumanog@wfp.org
WFP	Zuhaina Abubacar	zuhaina.abubacar@wfp.org
GRC	Pone Nyet Khaing	P.Khaing@drk.de
STARTNetwork	Arvin Caro	Arvin.Caro@startnetwork.org
OCHA /HDX	Leonardo Milano	leonardo.milano@un.org
OCHA/HDX	Pauline Ndirangu	pauline.ndirangu@un.org
OCHA/HFSA	Hanna Paulose	hanna.paulose@un.org
OCHA/CERF	Yakubu Alhassan	yakubu.alhassan@un.org
OCHA ROAP	Daniel Gilman	gilmand@un.org
OCHA-PHL	Manja Vidic	vidic@un.org
OCHA-PHL	Melissa Correa	melissa.correa@un.org
OCHA-PHL	Joseph Addawe	addawe@un.org
OCHA-PHL	Carino Antiqueza	carino.antequisa@un.org
OCHA-PHL	Rhinadel Caneta	rhinadel.canete@un.org
OCHA-PHL	Ollie Westerman	oliver.westerman@un.org

Annex 5: Post Distribution Monitoring Indicators

General information	
1	Name of enumerator
2	Questionnaire nr.
3	Organization
4	Location (Barangay, Municipality, Province, Region)
5	GPC location
6	Distribution partner
7	Consent (Yes to proceed)
HH information	
8	Respondent Name
9	Respondent Sex (M, F, Non-binary)
10	Head of HH Sex (M, F, Non-binary) <i>Same person tick</i>
11	Head of HH Age
12	How many people (including you) live in this household?
13	How many of the following HH members live in this household? (Children U5, PLW, PWD, Chronically ill, elderly/senior citizens, indigenous peoples)
14	What is the type of your residence (owned home, rented house, temporary shelter, evacuation center, with host family, homeless, other (specify))
15	Is anybody in your household a member or enlisted in any government social protection program such as Listahanan, 4Ps, Social Amelioration Program SAP and/or Emergency Shelter Assistance (Yes, No, If Yes, how many in what program?)
16	If yes, how much money in PHP has your household received from government programs?
17	Has this household benefited from another UN or NGO support (Yes, No)
18	If yes, what support has been received (open)
19	What is your households main source of income (fishing, agriculture, own business, daily labourer/temporary employment, fixed-term job, pensioner/4Ps, none/unemployed)
20	Any secondary livelihood? (open)
21	What is your monthly income in PHP? (0-2500, 2501-5000, 5001-10,000, >10,000)
22	Do you or anyone in your household have a mobile phone with internet connection? (Yes, No)
23	If yes, would you be able to receive the cash transfer through Gcash, Maya or any other digital money transfer? (Yes, No)
Hazard Information	
24	Do you understand why you were selected for the program (Yes, No)
25	Did you know that a typhoon was coming (Yes, No).
26	If yes, Where you aware of the severity of the typhoon (Yes, No)
27	What have you done to prepare for the typhoon (Strengthen household, protect assets, stock up on essentials, evacuate/transport, saved the money for later, other (specify) - multiple
28	How severely, if at all, was your household affected by the typhoon (Severely affected, Partially affected, Not affected)
CVA Program - AA Specific	
29	Was the money available at the payout center? (Yes, No)
30	When did you receive the cash transfer? (in hours prior/post typhoon)
31	Did you purchase/use cash <i>before</i> the typhoon hit? (Yes, No)
32	If yes, what did you purchase - select top 3 (food, water, shelter materials, hygiene/medical items, non-food items, communication, transportation, utilities/rent, debt repayment, livelihood protection, savings, services, shared with relatives/neighbors, other (specify)) Multiple

33	Did you purchase/use cash <i>after</i> the typhoon hit? (Yes, No))
34	If yes, what did you purchase - select top 3 (food, water, shelter materials, hygiene/medical items, non-food items, communication, transportation, utilities/rent, debt repayment, livelihood protection, savings, shared with relatives/neighbors services, other (specify)) Multiple
35	To what extent do you agree with the following statement: "the distribution process did not impact my ability to evacuate from the danger zone?" (strongly agree, agree, neither agree/disagree, disagree, strongly disagree]
36	Did you have enough time to get back to the evacuation center/your home to continue with preparations for the typhoon? (Yes, No, if No specify)
37	Did you find everything you needed at the market/s (Yes, No, Not applicable if respondent didn't purchase anything, if no specify what was not available)
CVA Program - Standard	
38	How much cash did you receive?
39	Was the amount of money received equal to the amount you were told you would receive (Yes, No, if No was it more or less?)
40	Where was the money received (remittance center/pawn shop (specify), Bank/ATM (specify), Philpost, Host community cooperative, Gcash/Digital, other FSP (specify), physical cash delivered in hand)
41	How long was the process time to receive the money (travel time, queuing time, process time, sum)
42	How much money did you spend on transportation to receive the transfer?
43	To what extent do you agree with the following statement "The aid provided to help cope with the typhoon enabled my family to meet our basic needs" (met all our needs, most of our needs, met some of our needs, met none of our needs)
44	Were markets safe to access? (Yes, No, if no specify)
45	In which municipality did you buy the items mentioned (within the municipality, different municipality, N/A)
46	Have you noticed price increase of goods since distribution?(Yes, No, N/A)
47	Is your household in debt (Yes, No)
48	If yes, how much?
49	If yes, to who (sari-sari, cooperative, pawnshop, relatives or family, bank, other (specify))
50	If yes, has your debt reduced the amount of your cash transfer because you had to make immediate repayments? (Yes, No, if Yes how much reduced?)
51	Has your quality of life changed because of the the cash assistance received? (got much worse, got slight worse, no change, slightly improved, very much improved)
52	What is the percentage of target population living in safe and dignified shelters? (%)
Decision making & Access	
53	How did your household decide how to spend the money? (Male spouse, Female spouse, Elders, Jointly, Other specify)
54	To what extent do you agree with the following statement "The aid provided to help cope with the typhoon benefitted men and women equally within households" (men benefitted much more than women, men a little more than women, men and women benefitted equally, women benefitted a little more than men, women benefitted much more than men)
55	Was the distribution site easily accessible (Yes, No, if no explain)
56	What was the main mode of transportation to/from the distribution point for you or the person who went to the distribution for you? (On foot, bicycle, own motorbike or car, relative/friend or neighbor, bus, boat, taxi or other paid service, other specify) Multiple choice
57	What would you have done if you hadn't received the cash assistance (open)
Protection, Self Assessment	
58	Did you feel safe at the distribution place? (Yes, No, If no specify)

59	Do you foresee any tensions or difficulty within your household that may arise over this cash assistance? (Yes, No, if Yes specify)
60	Do you foresee any tensions or difficulty within your community that may arise over this cash assistance? (Yes, No, if Yes specify)
61	How satisfied are you with the cash assistance received? (Very satisfied, Somewhat satisfied, Undecided, Not very satisfied, Not satisfied at all, it not at all explain)
62	How satisfied are you with the process of cash distribution? (Very satisfied, Somewhat satisfied, Undecided, Not very satisfied, Not satisfied at all, it not at all explain)
63	To what extent do you agree/disagree with the following statement "The aid to help cope with the typhoon went to the households in my community who needed it most"(Strongly agree, Somewhat agree, Neither agree or disagree, Somewhat disagree, Strongly disagree)
64	If this distribution was done all over again, would you still prefer to receive cash or other items (Cash, Other items (specify))
65	Do you know who you can approach to get more information, leave feedback or complain if you have any problems? (Yes, No, if no enumerator to explain)
66	Would you like to leave any other comments/recommendations/suggestions to our team? (open)



Annex 6: CERF Application – Chapeau and agency templates
