

ANTICIPATORY ACTION FRAMEWORK PHILIPPINES

2021-2022

Table of Contents

1.	Overview	1
	Summary	1
	Executive summary	1
2.	Introduction	4
	Objectives of anticipatory action	4
	Core principles	5
	Tropical Cyclones in the Philippines	5
	Crisis timeline	5
3.	Forecast and Trigger	7
	Forecasts	7
	Triggers and thresholds	7
	Activation protocol	8
4.	Anticipatory Action Plan	10
	Overview	10
	Approach to targeting at-risk beneficiaries	11
	Organizational set up of the CERF AA Pilot Framework	11
	Partnerships and localization of anticipatory action	12
	Operational coordination with local authorities	13
	Mandatory pre-emptive evacuation procedure	13
	Consultation with communities	14
	Ensuring readiness for timely implementation	14
	Pre-emptive cash interventions	14
	Priority interventions	16
	Summary table	19
5.	Pre-agreed Financing	21
	CERF	21
	Anticipatory Action Partnership and Funding framework	22
6.	Learning	22
	Monitoring & Evaluation	22
	Agency-specific M&E: FAO	23
	Agency-specific M&E: IOM	24
	Agency-specific M&E: UNICEF	25
	Process learning	25
	Independent evaluation	26
	Advocacy and public communication	26
7.	Annexes	27
	Annex 1 - Anticipatory Action: Summary table	27
	Annex 2 – DRAFT trigger messages	31
	Annex 3 - Evaluation of forecasts for anticipatory actions - April 2021	32
	Annex 4: Contact Information	38
	Annex 5: CERF Application – Chapeau and agency templates	39

1. Overview

Summary

The purpose of this document is to present the framework for anticipatory action (AA) in the Philippines, including the forecasting trigger (the model), the pre-agreed action plans (the delivery) and the pre-arranged financing (the money).

This document should be read in conjunction with the *Anticipatory Action Concept Note for the Philippines*.

Executive summary

The Framework outlines an approach to a collective anticipatory action delivered at scale as an innovative attempt to pilot typhoon response in the Philippines. The document includes details about the forecasting trigger (the Model), the pre-agreed action plans (the Delivery) and the pre-arranged financing (the Money). As this is a learning pilot an investment will be made in documenting evidence and learning (the Learning). CERF has allocated \$7.5 million for this pilot in typhoon season 2021/2022.

The objective of the pilot is to mitigate, and to a certain extent prevent, the impact of typhoons on people's homes and livelihoods, while building on government's mandatory pre-emptive evacuation procedures that save lives. With this intervention, the most at-risk communities will have better financial resources to prepare prior to landfall. Multi-sectoral assistance will be delivered by the UN agencies, NGOs and the Red Cross/Red Crescent in close collaboration with local authorities. For example, IOM will provide cash assistance and support vulnerable families in strengthening their houses; FAO's intervention will promote preservation of livelihoods and income by supporting poor farmers and fisherfolks to rent a secure and safe place for their farming and fishing tools and livestock while FAO's cash-for-work will support early harvesting of high-value crops; and WFP's multi-purpose cash will support food and other relevant needs while in evacuation. Anticipatory action interventions will mount a collective humanitarian action at scale to mitigate the impact of a severe typhoon hitting Region 5 (Bicol) and Region 8 (Eastern Visayas). The pilot will cover most vulnerable communities living in prioritized 8 provinces, with the aim to reach about 270,500 people with multi-purpose cash assistance ahead of typhoon landfall.

The Model includes a trigger mechanism based on the ECMWF forecast and IFRC/ Netherlands Red Cross 510 probabilistic typhoon impact prediction model developed for the Philippines that is using the ensemble of forecasted tracks and wind speed from high resolution model to predict the impact.

The CERF AA follows a 2-stage trigger activation:

- 1. Readiness trigger (pre-activation): 4-7 days prior to forecast landfall**
 - a. Tropical Cyclone with potential to reach category level 4 or higher (greater than 200 km/h maximum 1-minute sustain wind speed).
 - b. Projected to directly impact areas within Region 5 and 8.
- 2. Activation trigger: on or before 72 hrs (3 days) prior to forecast landfall**
 - a. As soon as ECMWF forecasts are available for a certain TC, NLRC 510 Initiative will calculate the predicted total number of totally damaged buildings, produce an impact map, and updates every 6-12 hours.
 - b. **Threshold is reached and CERF anticipatory action activated if 72 hours (3 days) before landfall (or sooner)** the predicted number of houses to be totally damaged fall within the range of 50% probability that 80,000 houses will be totally damaged to 95% probability that at least 5,000 houses will be totally damaged.

The Delivery. In case of sudden-onset disasters such as typhoon response, the delivery of anticipatory action is time critical. For this pilot, anticipatory interventions have been selected to be rooted in the current operating environment and government mandatory evacuation and safety protocols. Consideration is given to the compounding effects of COVID-19, the agency's operational capacity to deliver within the limited time window, the ability to mitigate the impact of typhoon damage, CERF funding priorities addressing protection, and the no regrets approach.

Above all, proposed anticipatory action interventions that save shelter and livelihoods, should not interfere or disincentivize government's pre-emptive interventions that save lives. The contingency of operating in the COVID-19 pandemic context requires stricter adherence to health protocols in the evacuation centres, meaning that preparations for mandatory evacuations now commence even earlier.

Given the very short lead times and the conditionalities imposed by COVID-19 pandemic the following are the interventions under this pilot:

About 66% of the overall CERF anticipatory action pilot budget will be used through cash assistance, both multi-purpose as well as sectoral top-ups. Unconditional pre-emptive multi-purpose cash will be delivered as a blanket contribution (US\$58 or 75% of average regional wage for 10 days together with transportation costs) by WFP, FAO and IOM to 54,100 most vulnerable households (270,500 beneficiaries) living in prioritized provinces of Region 5 and Region 8. The pilot is designed around a two-staged approach to cash distribution. WFP and FAO will trigger cash distribution 72 hours before landfall, IOM will ensure its distribution in evacuation centres. FAO, together with OXFAM, PDRF and Philippines Red Cross (PRC) will work with local communities to rent schools, local community halls, and places of worship to store critical livelihood items, such as boats and nets for fisherfolk or tools and seeds for farmers. By providing safe-storage sites, the intervention will preserve hard-won development gains and key livelihoods for 500 households and most vulnerable farmers and fisherfolks. To 16,000 agriculture dependent families FAO will provide multi-purpose cash intervention and 80,000 agri-households will benefit from messaging and agro-climate advisories. The FAO-led interventions will consider market-based approach to anticipatory action, whereas PRC will provide cash for work for early harvesting and livestock evacuation to 150 households, while Oxfam will provide cash for vulnerable livelihoods to 50 agriculture-dependent families.

IOM will work with local authorities in the evacuation centres to distribute blanket multi-purpose cash intervention, distribute CCCM kits to 13,110 families and shelter kits for 11,970 families which will facilitate safe and early return of evacuees and promote early decampment. The proposed activities will reduce the risk of COVID-19 infection and community transmission among most vulnerable population during pre-emptive evacuation, as well as minimize the socioeconomic strain and psychological distress derived from the displacement.

UNFPA will distribute protection commodities to 5,000 most vulnerable women and girls, provide cash-for-work to 810 community-based women volunteers employed by local women-led NGOs, and enhance GBV protection capacities of local government response units, which will benefit women and girls in evacuation centres. It will also provide cash vouchers assistance to 3,000 pregnant women and adolescent GoBabs to 7,000 adolescent girls.

UNICEF is complementing cash interventions with sectoral top-ups for nutrition, education, child protection and WASH. It will strengthen child protection systems and provide community engagement and dissemination of information and key messages on family preparedness, IPC, health, nutrition, hygiene, protection, and education. By prepositioning water quality monitoring and treatment supplies and equipment, basic COVID19 IPC supplies, and materials on WASH, access to safe water for 10,000 vulnerable households will be immediately restored.

To solicit feedback from communities at risk, the UN agencies agreed to carry out a collective pre-crisis survey in Region 5 and Region 8 on the appropriateness and feasibility of their proposed anticipatory interventions. Anticipatory action interventions were developed also in consultation with ICCG and each cluster, as per the revised HCT Minimum Operations Protocol that incorporates anticipatory action as its standard way of responding to significant typhoons during the 2021/2022 typhoon season.

CERF Anticipatory Action Funding Requirement

Organization	Cluster	CERF Financing
FAO	Agriculture	1,719,076
IOM	CCCM and Shelter	2,259,999
UNFPA	GBV and SRH	733,953
UNICEF	Child Protect, Education, Nutrition, WASH	820,872
WFP	Food Security	1,951,216
Total		7,485,156

The Learning. Learning from the pilot aims to generate proof that when early action is possible, it is faster, cheaper and more dignified than a traditional humanitarian response.

An ad hoc M&E group, i.e. the Learning Team, was established to assess how collective and coordinated early action can work at scale for typhoon response in the Philippines as well as capture and share learning about how to improve the approach to planning and implementation of anticipatory interventions. To ensure the localization of learning, local actors such as the government, will form part of the M&E group.

Process learning has been applied throughout the development of this framework and a number of issues already surfaced that would merit further consideration, such as the importance of setting aside sufficient start-up funds to enable UN agencies with preparedness activities. Considering COVID-19 operational reality, additional focus was placed on supporting safe pre-emptive evacuations and ensuring hygiene protocols are observed in evacuations centres. The pilot has been developed jointly by UN agencies with deep expertise in forecast-based financing and those with operational capabilities and years of experience in responding to highly unpredictable typhoons in the Philippines.

If the pilot is triggered (3-day activation trigger), OCHA will commission an independent evaluation to gather and analyse data documenting the results by focusing on the delivery model and on evaluating impact on household income.

Communication activities. At the request of the RC/HC, the UN agencies and partners agreed to put strong emphasis on communication activities also to ensure communicating as “One UN” and communicating the story before, during, and after the AA response. OCHA prepared an operational communications plan for the project, including key messages, communication activities and approach to communicating impact.

2. Introduction

Objectives of anticipatory action

The possibilities of predicting the occurrence of shocks as well as its humanitarian impact have substantially increased in the last decade, particularly in the case of extreme climate events. By taking this anticipatory approach – using “evidence of risk”, instead of “suffering” – we can today protect better and save more lives, optimize resources and preserve hard-won development gains. This resilience-building thinking has also impacted on the way we plan and organize humanitarian action.

Today, we can predict with increasing confidence the occurrence and humanitarian impact of tropical cyclones. Anticipatory action is envisioned to contribute building community resilience especially if done alongside climate-smart disaster risk reduction and response efforts. By combining different analytical approaches, out-of-the-ordinary weather events could to an extent be predicted, which would enable their projected impact to be proactively mitigated based on pre-identified anticipatory actions. Building on growing evidence that acting prior to the onset of a predictable hazard is significantly more (cost-)effective than traditional humanitarian response, OCHA has facilitated the setup of an Anticipatory Action framework for the Philippines with FAO, IOM, UNFPA, UNICEF and WFP being the key UN agencies implementing early action interventions, working closely with Red Cross/Red Crescent, NGO partners as well as local authorities.

Building on growing evidence that acting prior to the onset of a predictable hazard is significantly more effective, collective Anticipatory Action Frameworks are being established by CERF and facilitated by OCHA. Each Framework comprises of 3 core elements, all of which are underpinned by a clear learning, monitoring and evaluation plan:

- A robust forecasting embedded in a clear decision-making process (**the model**).
- Pre-agreed action plans that can fundamentally alter the trajectory of the crisis (**the delivery**).
- Pre-arranged finance (**the money**).

Anticipatory action is still an innovative space, requiring “proof of concept”. Thus, in addition to the 3 core elements, an investment in documenting evidence and learning from each framework is necessary (**the learning**).



Objectives for the 2021/2022 typhoon season

The objective of the anticipatory action is to mount at scale a collective humanitarian action to mitigate the impact of a severe typhoon hitting Region 5 (Bicol) and Region 8 (Eastern Visayas). The pilot will cover most vulnerable communities living in prioritized provinces, with the aim to reach about 270,500 people with multi-purpose cash assistance ahead of typhoon landfall. Multi-sectoral assistance will be delivered by the UN agencies, NGOs and the Red Cross/Red Crescent in close collaboration with local authorities.

Core principles

The anticipatory action pilot Framework in the Philippines has been tailored to the local context as well as the RC/HC priorities, which are guiding its design and implementation:

1. The Philippines is not new to anticipatory action and there have been several small-scale activations for typhoons in the past five years. The pilot needs to learn from the wealth of this experience and good practice while remain adaptive, focused, practical and pragmatic to be able to activate at scale. It should be activated with 'No regrets' principle in mind.
2. Catalytic funding. As any CERF project, the pilot should be catalytic in funding and develop complementary projects to leverage additional resources and engage wider humanitarian community in piloting early action approaches.
3. Leverage existing know-how on forecasting and data analytics. The pilot should leverage existing expertise, including local, in forecast modelling and shock analysis for typhoons in the Philippines.
4. Cost efficiency. The pilot should remain nimble and prove cost-effectiveness of the model with investment going in the hands of the most affected people.
5. Supporting localization. The pilot is built on aid localization principle and ensures close collaboration with the government and ownership of national and local authorities. At least 30 per cent of the total allocated amount should go to NGOs and strategic partners.
6. Promoting accountability to affected population. The pilot embraces community-building approach and communities are consulted throughout the process.
7. Empowering the most vulnerable. Keeping in mind CERF four funding priorities, beneficiaries prioritized for assistance will be the most vulnerable groups, particularly interventions empowering women.
8. COVID-19 contingency. The pilot will integrate impact of COVID-19 and other compounding effects.
9. Striving for integration. The pilot design will prevent duplication of coordination mechanisms, ensure utilization of the HCT, ICCG and working groups. It will also foster linkages with long term programming, including resilience and development initiatives

Tropical Cyclones in the Philippines

According to the World Risk Report 2018, the Philippines, ranked third among all countries for disaster risks, with index value of 25% (World Economic Forum, 2018). At least 60% of the country's total land area is exposed to multiple hazards, and 74% of the population is susceptible to their impact (GFDRR, 2017). Largely contributing to these risks is the country's location and geography as the risk involving coastal hazards such as typhoons, storm surges and rising sea levels is high. The areas of the Philippines most frequently impacted by tropical cyclones are northern Luzon and eastern Visayas. Tropical cyclones frequently make landfall on the islands of Eastern Visayas, Bicol region, and northern Luzon.

Approximately twenty tropical cyclones enter the Philippine Area of Responsibility (PAR) each year, an average of five of these are potentially destructive. Tropical cyclones with 118 to 220 km/h wind strength or higher have significant impact to lives and properties. Tropical cyclones can hit the Philippines any time of the year, but the months of June to November are the most active and May the least active. Tropical cyclones normally move east to west across the country, heading north or northwest as they exit the PAR. Cyclones frequently make landfall on the islands of northern Luzon, Eastern Visayas, Bicol region, northern and eastern Mindanao. Due to warm coastal waters of the Philippine sea, exacerbated by climate change warming, rapid intensification ahead of landfall is common. Cyclones usually account for at least 30 per cent of annual rainfall in northern Philippines.

Crisis timeline

While the rainy season usually start in June, the more destructive tropical cyclones tend to hit the landmass later in the year, from September to November.

	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC
CLIMATE INFORMATION	Season											
	Monsoon											
	Cyclones											
ANTICIPATORY ACTION	Spread											
	Vaccination											
	Framework Devt											
	Triggers											
	Early Action											

Destructive tropical cyclones cause significant losses to agriculture and damages to infrastructure, particularly, health, schools, houses, markets, water facilities, communication, and have serious humanitarian consequences including loss of livelihoods, reduced income, disruption to continuing education and exacerbation of pre-crisis protection issues, such as GBV.

Embedding anticipatory action in the existing humanitarian coordination mechanisms

To prevent duplication of coordination platforms, the HCT, based on ICCG recommendation, endorsed in May 2021 [a review of the existing HCT Minimum Operations Protocol for Typhoon Response](#) to account for anticipatory action interventions, which will be used at least for the 2021-2022 typhoon season.

Consequently, clusters adjusted their cluster-specific contingency plans and identified most suitable early action interventions, relying on their technical expertise as well as by consulting with communities.




PHILIPPINES

Humanitarian Country Team Minimum Operations Protocol for Tropical Cyclone

As of 20 May 2021

Immediate actions undertaken by the Humanitarian Country Team (HCT) and Inter-cluster Coordination Group (ICCG) during a tropical cyclone event identified to have a potential significant humanitarian impact on any part of the country. Anticipatory Actions (AA) are considered as part of the Pilot Anticipatory Action implementation in the Philippines focusing on Bicol and Eastern Visayas for 2021-2022 typhoon season.

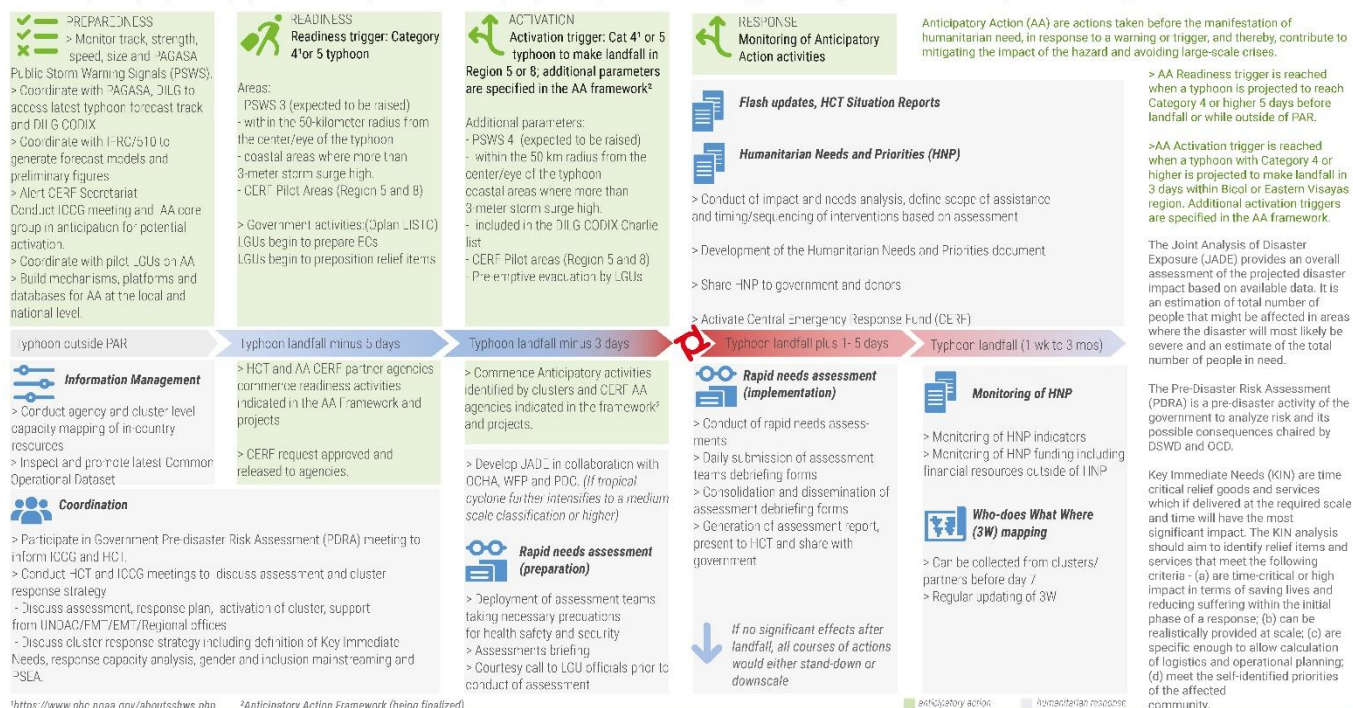

¹<https://www.nhc.noaa.gov/aboutshws.php> ²Anticipatory Action Framework (being finalized)


Creation date: 20 May 2021 Sources: OCHA, HCT, ICCG Feedback: palacio@un.org www.unocha.org/philippines www.reliefweb.int

3. Forecast and Trigger


Forecasts

Several organizations have implemented forecast-based financing (FbF) activities in the Philippines for small-scale typhoon response where they developed and used forecast and trigger mechanisms, while 3 key actors (WFP, IFRC/510, Global Parametrics) have developed their own models. OCHA and the Humanitarian Data Centre facilitated discussion among these organizations to understand various forecasting models developed for tropical cyclone and to determine the most appropriate methodology to use for the CERF AA Pilot in the Philippines. After a thorough analysis, it was decided to use the IFRC/510 model. The [summary and report link](#).

The Netherlands Red Cross 510 Initiative model was further revamped from a deterministic to a probabilistic impact forecast using ECMWF data. It is based on historical data that captures the relationship between impact (the houses totally damaged) and several explanatory variables (hazard, vulnerability and exposure). It uses typhoon forecast tracks, rainfall and wind speed to predict impact. There is an ongoing discussion and drafting of MOA between PRC and PAGASA to use PAGASA data as one input in the 510 model.

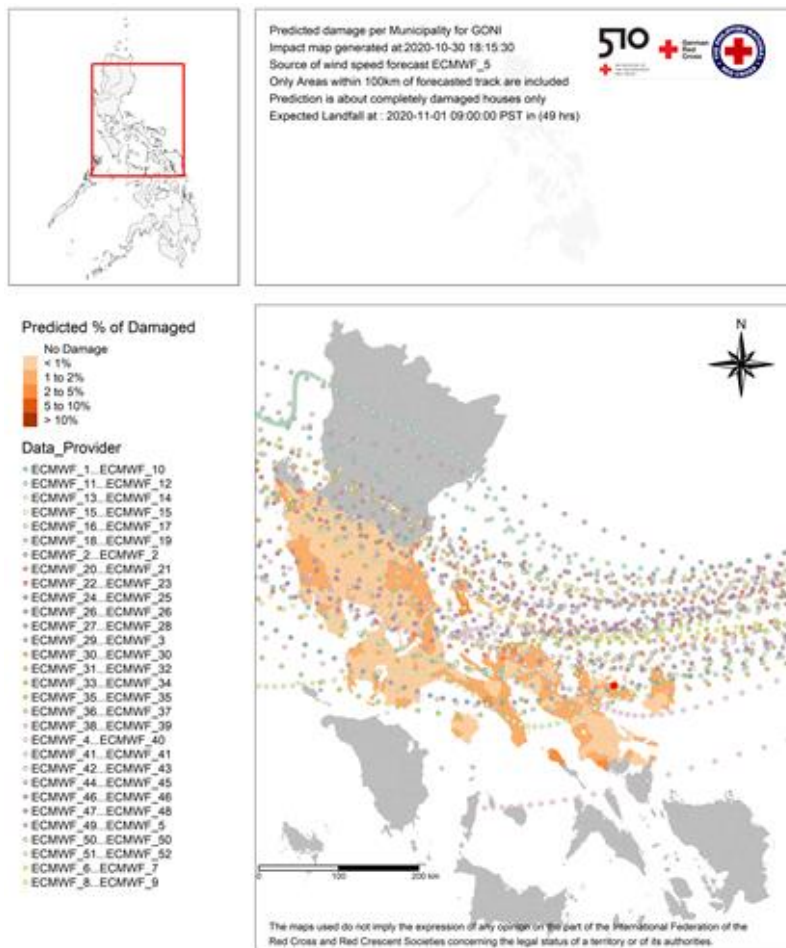

Triggers and thresholds




The CERF AA follows a 2-stage trigger activation:

1. Pre-activation triggers (readiness): 4-7 days prior to forecast landfall

- Tropical Cyclone with potential to reach category level 4 or higher (greater than 200 km/h maximum 1-minute sustain wind speed).
- Projected to directly impact areas within region 5 or 8.

2. Activation trigger: on or before 72 hrs (3 days) prior to forecast landfall

- As soon as ECMWF forecasts are available for a certain TC, NLRC 510 Initiative will calculate the predicted total number of totally damaged buildings, produce impact map, and updated every 6-12 hours.
- Threshold is reached and CERF AA is activated if 72 hours (3 days) before landfall**, the predicted numbers fall within this range: 50% probability that 80,000 houses or more will be totally damaged, or 95% probability that 5,000 will be totally damaged.

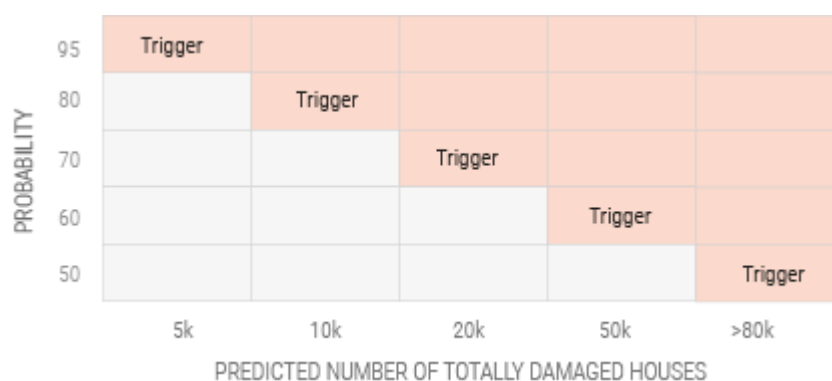


Activation protocol

The table and graphic below describe the activation protocol, including key roles and responsibilities in monitoring and activation of the Framework.

Organization	Activity	Timeline	Medium	Output
510, OCHA, Core group members	Monitoring of Tropical Cyclone (TC) formation	7-10 days prior to forecast landfall	Communication via the triggers skype group	Impact and probability estimates, impact maps and landfall map generated by 510
510	Generation of impact estimates	5-7 days prior to forecast landfall; every 6-12 hours based on ECMWF data	Sent via the Triggers skype group	Impact and probability estimates, impact maps and landfall map
OCHA and AA Core Group	If the readiness trigger is reached, a notice for readiness trigger is sent to AA partners	5-7 days prior to landfall	Via email with attached 510 products as well as other meteorological agency (i.e. PAGASA) reports	Readiness trigger notice sent to partners
RC/HC Or OCHA on behalf of RC/HC	Notify CERF on the readiness trigger and potential activation of AA	5-7 days prior to landfall	Sent via email	Email to the CERF secretariat and AA Core Group
510 and AA Triggers group	Compare and analyze different forecast models	3-5 days prior to landfall	Via triggers skype group	If there are significant differences in forecast tracks of meteorological agencies, 510 would acquire additional data to generate several models for the trigger thresholds
510	Generation of impact estimates	3-5 days prior to forecast landfall; every 6-12 hours based on ECMWF data and other available sources	Sent via the Triggers skype group	Impact and probability estimates, impact maps and landfall map
AA Core group	Inform local partners and partner government agencies	3-5 days prior to landfall	Meeting and email	Notice

	on the potential activation of AA in target areas			
OCHA, AA Core Group	If activation triggers are met on or before 72 hrs (3 days) prior to landfall, recommend to RC/HC for AA Activation	On or before 72 hrs (3 days) prior to expected landfall	Meeting and email	Activation notice sent to AA partners and to CERF
RC/HC	Notice to AA Core group on activation trigger to AA Core group	On or before 72 hrs (3 days) prior to expected landfall	Email	Notice
510, OCHA, AA Core Group	If activation triggers are not met 72 hrs prior to landfall, activation trigger stand down notice.	70 hrs prior to landfall	Meeting and email	Stand down notice sent to partners and to CERF
510, OCHA, AA Core group	Continue monitoring of TC development after stand notice	1-2 days prior to landfall	Skype group and email	Impact maps

The communication flow between partners involved in the AA CERF pilot in the Philippines.

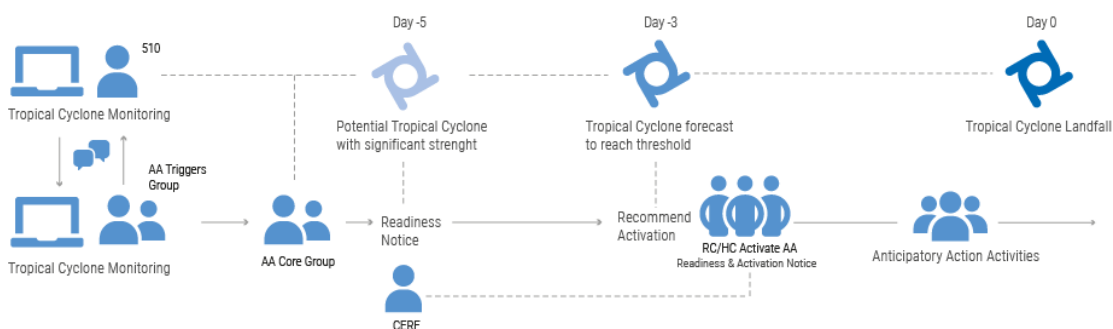

Known challenges, limitations and how to overcome these in the future

Key challenge in anticipating tropical cyclone path is the wide cone of uncertainty where the TC could change its track in a matter of hours. For example, there was a 150 km error in track position 72h ahead landfall for Super Typhoon Goni, which in an archipelago country poses significant operational challenges. A possible way to mitigate this uncertainty is to have assistance pre-positioned in several provinces and several partners on stand-by at the same time.

In the hours before landfall, TCs can also undergo rapid intensification that could effectively shorten the lead time from trigger activation. NLRC/510 is conducting a study to incorporate into their model the effect of rapid intensification in predicting the damage figures.

Due to a fairly wide cone of uncertainty within the TC track, all eight provinces in both regions will be activated under the proposed Framework. Some pilot areas might not be highly impacted but since these are highly vulnerable areas, losses and damages will still be incurred and the AA activities will provide assistance and help build capacity. As an improvement to the triggering methodology, target area activations per scenarios could be explored further.

With sudden-onset events, there is a chance of a false alarm, i.e. that the readiness trigger is reached but not the activation trigger. If the proposed trigger methodology is applied to recent strong typhoons that affected Regions 5 and 8 and would have reached the readiness trigger (Haiyan in 2013; Hagupit in 2014; Nock-ten in 2016; Kammuri in 2019 and Goni in 2020), only three (Haiyan, Nock-ten and Kammuri) would also reach the activation trigger 72 hours before landfall. In this case, readiness costs will be kept at a minimum (6% of the cost) to ensure that only very limited funding is used.

To ensure readiness for eventual activation of the pilot and as a form of simulation, the Triggers Team will monitor each tropical cyclone that enters the Philippine Area of Responsibility in 2021 and 2022 as per the above-mentioned procedures.

4. Anticipatory Action Plan

Overview

Destructive tropical cyclones cause significant losses to agriculture and damages to infrastructure, particularly houses, health, schools, markets, water facilities, communication, and have serious humanitarian consequences, including loss of livelihoods, reduced income, disruption to continuing education and exacerbation of pre-crisis protection issues, such as GBV.

To prevent or reduce the humanitarian impact of severe typhoon, anticipatory actions need to be delivered within the narrow window of opportunity, i.e. between the readiness trigger and the activation trigger, after which the implementation of anticipatory action interventions could no longer be safely delivered and would interrupt government mandatory evacuation procedures.

Example of activities a Filipino household is advised to undertake before a typhoon:

WHAT TO DO BEFORE A TYPHOON

 Monitor the news about weather disturbances. As the typhoon nears, watch out for the latest severe weather bulletin issued by PAGASA every six hours.		
 Check the ability of your house to withstand strong winds; strengthen it if necessary.	 Board up windows or put storm shutters.	 For farmers, harvest crops that can already be yielded.
 For fisherfolks, place boats in safe areas.		 Secure domesticated animals in a safe place.
 Make sure flashlights and battery-powered radios have fresh batteries or are electrically-charged; stock up on candles and matches.		
 Store adequate food supply and clean water. Have food that do not require cooking.	 Ready your emergency kit/ grab bag to include some first aid kit, candles/flashlight, clothes, food, and radio.	
 Secure important documents.	 Prepare a list of emergency hotline numbers, including contact details of authorities.	
	 Be on standby and assess when it may be necessary for you to evacuate to safer areas.	

Multiple sources: MMDA Disaster Awareness FAQ, Rappler, ABS-CBN, Red Cross

Agencies need significant operational capacity (sectoral, logistic, administrative, financial, human resources) to implement the interventions at scale in a timely and effective manner. It is critical to note that the success of actual implementation in a particular village or municipality relies on a number of factors, such as its geographic location, proximity to major roads, proximity to evacuation centres and designated financial service providers, early activations of mandatory evacuations, pre-emptive power cuts and interruptions of telecommunication lines, localized wind and rain events as well as landslides, which may be aggravated by previous rainfall events during the rainy season as well as COVID-19-related movement restrictions. All these factors are outside the scope of this Framework. Duty of care of humanitarian responders will be agencies' utmost priority when activating anticipatory action assistance.

For this pilot, interventions have been selected to be rooted in the current operating environment, including COVID-19, agency capacity to deliver, ability to mitigate the impact of typhoons and learning from past experiences.

To better understand how components of the AA framework come together in a coordinated manner based on the operational timeline, the Core Group organized a full-day workshop in July 2021 that served as a tabletop simulation exercise. The implementing agencies facilitated the sessions which focused on specific themes such as the Trigger Model; Preparatory and Readiness Activities six to four days before landfall; and the Anticipatory Actions to be implemented three days to a day ahead of the typhoon impact.


The details of UN-led anticipatory action interventions as part of the pilot are in the annexed CERF applications.

Approach to targeting at-risk beneficiaries

Region 5 (Bicol) and 8 (Eastern Visayas) were selected as they are most often where destructive typhoons made their initial landfall, which brings the greatest damage in terms of wind impact and storm surge.

As a starting point, the approach to selecting target municipalities used a common dataset disaggregated by geography, age, sex, disability and poverty to jointly plan for direct CERF assistance to those considered most vulnerable in Region 5 and 8. Municipalities were prioritized based on poverty incidence as per the latest available Philippine Statistics Authority data (2015), exposure to typhoon impact, number of women, and people living in houses made of light material. A composed index was developed that ranked all municipalities in the two regions according to the selected criteria. This prioritization was overlaid on a map with existing presence and operational capabilities of UN agencies, Philippine Red Cross and START Network Partners.

The outcome of this inclusive and consultative approach led the Core Group to identify in Region 5 a total of 20 municipalities in four provinces (Camarines Sur, Albay, Catanduanes, Sorsogon) and Region 8 a total of 24 municipalities in four provinces (Samar, Northern Samar, Eastern Samar, Leyte), where 2.2 million are at risk of being exposed to typhoon impacts.

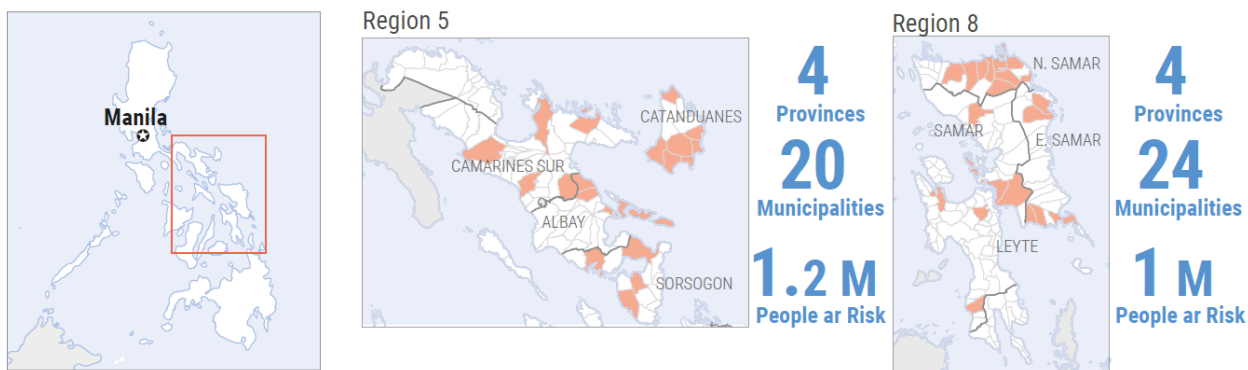

Organizational set up of the CERF AA Pilot Framework


To develop and deliver on the AA Pilot Framework, organizational project structure was set up with reporting lines to the Humanitarian Country Team (HCT) and in close collaboration with the Inter-Cluster Coordination Group (ICCG).

The AA Core Group was established as a principal decision-making body; it is convened by OCHA and composed of key UN agencies as well as an NGO representative from the START Network and IFRC. To work on specific technical issues, Team Triggers, Team Cash, Team Cross-cutting issues and Team on Learning were established and are led by respective UN agencies. NGO partners agreed to lead on accountability to affected population and ensuring communities are consulted in development of the Framework.

To ensure regular communication and operational coordination with partners and authorities in prioritized areas, provincial leads were selected. UN agencies were designated as a 'CERF anticipatory action pilot Lead' in each of the eight targeted provinces, with responsibility to ensure the relevant regional, provincial and municipal authorities are well informed of project objectives, are consulted on target beneficiary selection and input in validation, as well as that UN partners are

joining key-decision making coordination meetings, such as the Pre-Disaster Risk Assessment (PDRA) meeting organized by the Provincial DRRM office prior to a typhoon landfall. On behalf of the HCT, OCHA would attend national-level PDRA meeting of the National Disaster Risk Reduction and Management Council (NDRRMC).

The AA Core Group collaborates with the AA Technical Working Group, co-chaired by FAO and the national Office of Civil Defense.

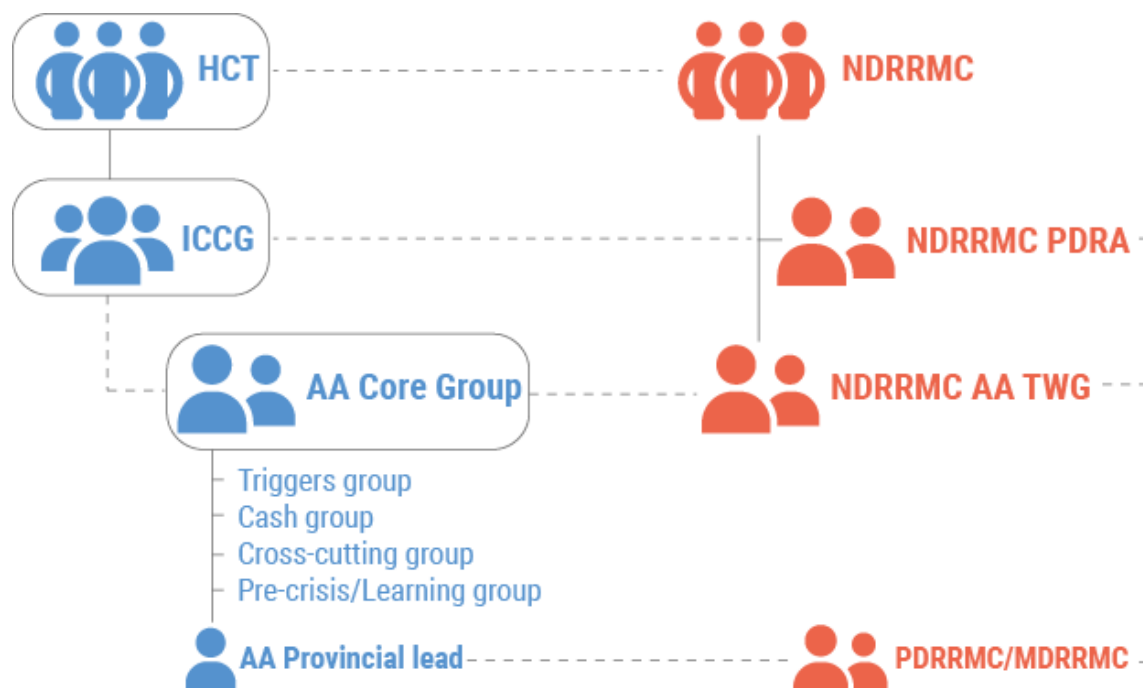

Partnerships and localization of anticipatory action

At the very onset of the pilot design, the RC/HC made a strong call for including local actors in its development and implementation. Both IFRC and START Network have formed part of the Core Group that meets weekly to develop the Framework, working through Team on Triggers, Team on Cash and Team on cross-cutting issues. Agencies with experience in early action interventions significantly contributed to the design of the pilot by sharing their learning with anticipatory action activations in the Philippines.

While the UN agencies are main recipients of CERF funding, each of them works with local partners, with the aim to ensure that 30% of allocated CERF budget for the Philippine pilot goes to NGOs and strategic partners, to the extent interventions allow such partnerships. As per the current framework, 29% of funding will go to NGOs, including local, and to Philippine Red Cross.

Working with partners and local actors and promoting local buy-in has been mainstreamed throughout the Framework development when preparing its Triggers, the Delivery Model, the Money and the Learning.

Organization	CERF-funded implementing partners
FAO	Oxfam; Philippine Red Cross (PRC), CARE, Philippine Disaster Relief Foundation (PDRF)
IOM	Philippine Red Cross; Catholic Relief Services (CRS); World Vision; CARE
UNFPA	World Vision; Oxfam; Fundacion Educacion Y Cooperacion (EDUCO); Plan International
UNICEF	Council for the Welfare of Children (CWC); World Vision
WFP	Bicol Consortium for Development Initiatives (BCDI)

Highlights of how working with local actors will be featured in the pilot:

- UNFPA interventions are designed to leverage and maximize leadership and humanitarian capacities of local Women Rehabilitation Organizations (WROs) who have trained many local women and girls-led CSOs on protection issues and community-based solutions such as the operation of Women-Friendly Spaces and GBV monitoring.
 - To support community engagement, UNFPA's Cash-for-Work intervention for 800 community volunteers will include 30% of women and youth leaders, 30% BHWs, 30% daycare workers, and 10% LGBTQI.
- FAO's implementation partner Oxfam will work with its local partner People's Disaster Risk Reduction Network (PDRRN) to implement multi-purpose cash transfer in Eastern Samar.
- In addition, local NGOs are particularly engaged in preparedness activities which are not all funded by CERF.
 - For example, FAO is working with CSOs on community preparations, validation of the pre-identified beneficiary lists, mapping of financial service providers and close coordination with local government units and other local actors.
 - Similarly, WFP is engaging a Bicol-based regional consortium, Bicol Consortium for Development Initiatives, to carry out community sensitization on the AA project, independent validation of beneficiary lists generated by the local government units, beneficiary registration in WFP's SCOPE platform, pre-crisis mapping, early warning messaging and assist with cash distribution in places where there is no financial service provider.
 - Agencies noted that one of the constraints of not engaging with local actors even more is their lack of capacity to work at scale and limited experience with anticipatory action, while at the same time CERF does not fund any capacity building activities that would help local actors develop these skills.
- Local government agencies too are involved in implementation of some activities. For example, UNICEF will be working directly with the Department of Social Welfare and Development (DSWD) and Landbank of the Philippine (LBP) to provide cash top-up to families with children enrolled in the government social protection programme.

Operational coordination with local authorities

The Government of the Philippines has made significant efforts to protect people and infrastructure, leveraging the investment made since Super Typhoon Haiyan of 2013 in improved early warning and reinforcing the important leadership role played by local officials. The Framework is built on existing government Disaster Risk Reduction and Management mechanisms and coordination architecture. The National Disaster Risk Reduction and Management Council through the Office of Civil Defense have been engaged with Forecast-Based- Financing (FbF) partners, FAO, IFRC, WFP and Start Network and is aware of several pilots undertaken in the past three years. OCD co-chaired the FbF Technical Working Group (TWG) with FAO. With the AA CERF Pilot, the Disaster Preparedness Pillar of the NDRRMC adopted the concept of Anticipatory Action and renaming the FbF TWG into AA TWG, with representation from government: DSWD, DoST, DILG and OCD and humanitarian agencies. It is envisioned that with the NDRRMC adopting the AA concept, the AA CERF Pilot can be well implemented at the regional and pilot areas, at the provincial and municipal levels.

As mentioned under the Organizational set up, provincial lead agencies were selected in each of the eight targeted provinces to ensure regular communication and operational coordination with partners and provincial and municipal authorities in prioritized areas. OCHA is leading coordination at a regional level with authorities in region 5 and 8.

Mandatory pre-emptive evacuation procedure

Since Super Typhoon Haiyan that resulted in over 6,000 casualties, the government strengthened its pre-emptive evacuation procedures. Once a mayor of a municipality triggers pre-emptive evacuations based on a PAGASA Tropical Cyclone Wind Signal and PDRA, it is mandatory for those living in at-risk areas to evacuate. People that actually evacuate to designated evacuation centres are often times those most vulnerable living in houses made of light materials and having no safer alternative, such as staying with relatives or friends living in sturdier shelter.

In line with government's early warning protocols, local authorities are expected to start with pre-emptive evacuations of areas to be most affected 48h before landfall, often times women, children and elderly going ahead, with all evacuations expected to be completed 24h before landfall. People weather the storm in evacuation centers and are allowed to start

returning to their homes 12 hours after landfall. Due to COVID-19 pandemic and adherence to stricter health protocols in evacuation centres, mayors are expected to commence preparations for pre-emptive evacuations 72h before landfall.

Pre-emptive evacuations are government's single most successful early action intervention that saves lives. For example, in November 2020 local authorities pre-emptively evacuated over 500,000 people ahead of Super Typhoon Goni and 230,000 people ahead of Typhoon Vamco, effectively saving many lives.

The CERF anticipatory action interventions were designed keeping these mandatory protocols in mind and incentivizing responsible behaviour for vulnerable households to find safer ground in evacuation centres.

Consultation with communities

The UN agencies agreed on a collective approach to consultation with communities and to carry out a pre-crisis survey, based on a similar methodology used by the HCT's Community of Practice Community Engagement for the HCT COVID-19 response consultations as well as for the preparation of the HCT Contingency Plan for the Metro Manila 7.2-magnitude earthquake. The pre-crisis survey was adjusted to account for anticipatory action interventions and will be carried out by the UN agencies with the support of implementing partners. Outcomes of the survey will fine-tune the design and implementation of interventions.

Ensuring readiness for timely implementation

In the context of the Philippines only about 48-hours will be available between the Readiness and Activation trigger and very few activities could be implemented in the Readiness phase. Compared to other, more slow-onset pilots, preparedness activities will be critical.

As previous activation attempts indicate, a number of potential operational challenges could hinder implementation of pre-emptive cash interventions, including losing precious hours if the trigger is reached in the hours when the banks are not operating or if telecommunication or power lines are pre-emptively disabled by the authorities. Once Tropical Cyclone Wind Signal 1 is raised, usually 72h ahead of landfall, all ports will be closed and any island will be out of reach.

Also important will be that agencies put utmost priority to duty of care and safety of staff that will be carrying out anticipatory activities. They require proper equipment, such as raincoats, flashlights if the work is carried out late at night, waterproof bags, as well as IDs and key documents explaining the pilot early action activities. Operational agencies will also need to pre-identify suppliers (trucks, van, etc.) as it is difficult if done few days before landfall.

To better prepare and plan for these contingencies, the Core Group organized in July a 1-day simulation exercise that produced a comprehensive Master Plan of the Pilot Operational Timeline (see Annex 1), planning detailed activities of each intervention from preparedness to activation.

Pre-emptive cash interventions

Given the very short lead times, unconditional pre-emptive multi-purpose cash is a major component of the pilot and will be delivered as a blanket contribution (US\$56 or 75% of average regional wage for 10 days and a top-up for transportation costs) by WFP, FAO and IOM to some 54,100 most vulnerable households (270,500 beneficiaries) living in prioritized provinces of Region 5 and Region 8. FAO will particularly target small farmers and fisherfolks with multi-purpose cash assistance and will de-conflict with any multi-purpose cash assistance delivered by WFP and IOM.


Considering operational realities and building on government emergency response efforts, the pilot is designed around a two-staged approach to cash distribution. Whereas WFP and FAO will trigger cash distribution 72 hours before landfall, IOM will ensure its distribution in evacuation centres, which are part of government's mandatory pre-emptive evacuation procedures commencing about 72-48 hours ahead of landfall. In both cases, the pilot aims to demonstrate that acting early will ensure more dignified, effective and faster approach to delivering humanitarian assistance.



PHILIPPINES

CERF Anticipatory Action Cash Based Intervention Snapshot

As of 15 Aug 2021

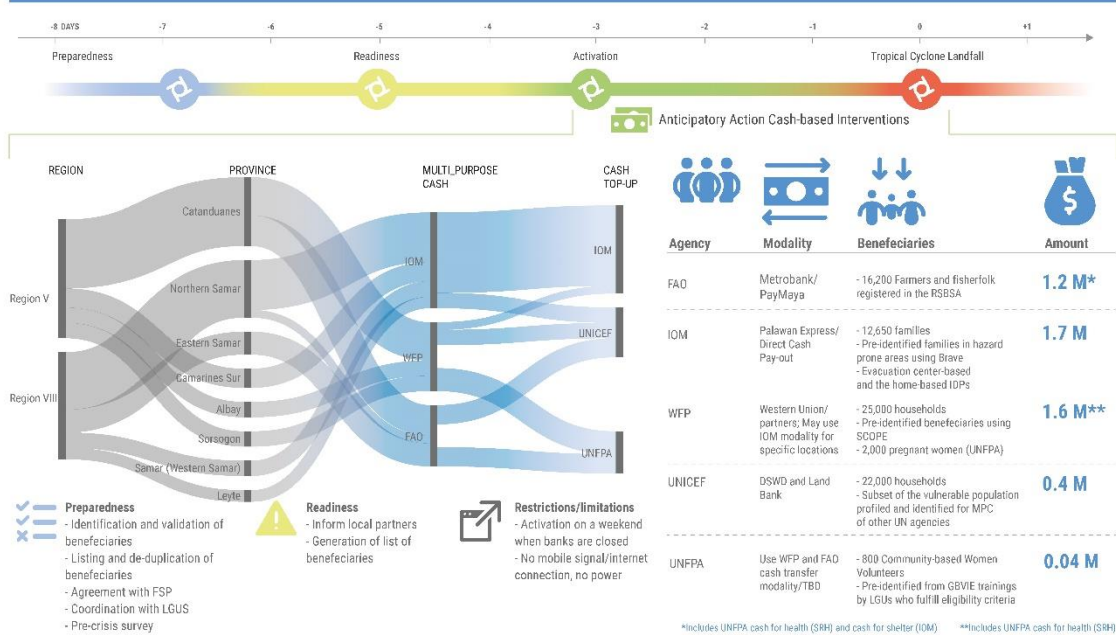

To ensure there will be no duplication between multi-purpose cash approaches of WFP, FAO and IOM, the agencies agreed to focus on different municipalities, with WFP targeting 15 municipalities in Region 5, while FAO will be targeting 15 municipalities and IOM 23 municipalities in both Region 5 and 8. Also for the purpose of learning, agencies will nevertheless overlap in several municipalities, where multi-purpose cash will be delivered by WFP or FAO, while in such instances IOM will only provide only shelter strengthening top-up in the evacuation centres. Where neither WFP nor FAO will provide blanket multi-purpose cash intervention, IOM will provide both the multi-purpose cash and sectoral top. This model should also allow for learning how different distribution models impact use of cash by beneficiaries.

By using government social safety net mechanism in the target municipalities, UNICEF will implement sectoral top-ups (\$20) to 42,200 children intended to finance needs of children for health, nutrition, WASH, education and child protection and will allow vulnerable households with children to procure basic needs and continue to access time-sensitive services before the landfall and before services may be disrupted.

UNFPA will provide Cash for Work to 810 pre-identified women and youth leaders in the community who have been trained as community-based GBV monitors as well as Cash Voucher Assistance to 3,000 pregnant women to support their access to continuing maternal health services. In total, about 66% of the overall CERF anticipatory action pilot budget will be used through cash assistance.

As there will be less than 48h between the Readiness trigger and the Activation trigger, significant preparedness activities for cash distribution will need to be carried in advance. Beneficiary registration, validation as well as possible de-confliction will all be implemented ahead of Readiness trigger activation. This is a significant investment in time and money that the agencies are making, as CERF anticipatory action pilot funding will not cover readiness activities if they occur ahead of Readiness trigger. For example, FAO, IOM and UNFPA have raised over \$1.3 million of internal funding to be spent for preparedness activities.

Priority interventions

Interventions by Food and Agricultural Organization (FAO)

Objective: FAO will work with OXFAM, CARE, Philippine Red Cross (PRC) and the Philippine Disaster Relief Foundation (PDRF) to reduce the impact of typhoon on the livelihoods (crops, fishes, and livestock) and increase the financial capacity of the most vulnerable farmers and fisherfolks ahead of pre-emptive evacuations.

Interventions: FAO will provide multi-purpose cash assistance to 16,000 most vulnerable households of farmers and fisherfolks based on the beneficiary list from the government's Cash and Food Subsidy for Marginal Farmers and Fisherfolk (CFSMFF) Program. The target beneficiaries are farmers and fisherfolk registered in the Registry System for Basic Sectors in Agriculture (RSBSA). Cash assistance will help to protect the livelihoods of those anticipated to be affected by the incoming typhoon while supporting and reinvigorating local markets in potential affected areas.

The Cash for work intervention of the PRC will protect the livelihoods of farmers and aquaculture fisherfolks from the impacts of the typhoon. Vulnerable farmers and fishermen will also be hired for 2-3 days before landfall of the typhoon to implement early harvesting of matured crops (such as abaca trees in Catanduanes island, or rice in Camarines Sur), early harvesting of fishes in aquaculture farms and livestock evacuation near evacuation centres.

FAO will also work with PDRF and local communities to rent schools, local community halls, and places of worship to store critical livelihood items, such as boats and nets for fisherfolk or tools and seeds for farmers. By providing safe-storage sites, the intervention will preserve hard-won development gains and key livelihoods. FAO will also issue agro-climate messaging to farmers and fisherfolks.

FAO will work with UNFPA to provide top-up cash for health to be given to 1,000 pregnant and lactating women (PLW) and with IOM to provide top-up cash for shelter to 2,400 families living in houses made of light materials

Recognizing the importance of supporting vulnerable agriculture and fisheries' livelihoods in target areas, the FAO-led interventions will adopt market-based approach and assist livelihoods of small holder farmers and fishers to generate income from the pre-emptive food needs as well as small merchants to serve as financial service providers of beneficiary households. This approach will help generate income to support vulnerable livelihoods that are anticipated to be affected by the incoming typhoon. Such interventions include cash for vulnerable livelihoods.

Interventions by International Organization for Migration (IOM)

Objective: To reduce and minimize harm, including the risk of COVID-19 transmission, and distress from the rapid displacement, IOM-led interventions will ensure that evacuees have immediate access to Shelter Strengthening Kits at the time of typhoons.

Interventions: IOM together with Philippine Red Cross (PRC), Catholic Relief Services (CRS), World Vision and CARE, will ensure evacuees have immediate access to Shelter Strengthening Kits through multi-purpose cash-based Interventions. The proposed activities seek to reduce the risk of COVID-19 infection and community transmission during the evacuation as well as minimize the socioeconomic strain and psychological distress derived from the displacement.

The IOM-led intervention will also preposition key CCCM items to be promptly delivered to the designated evacuation centres and communities within 72 hours after the pre-evacuation commences. The key items, for example, are personal protective equipment (PPE) including face masks, hand soaps, alcohol-based disinfectants and sanitizers, thermal scanners, and modular tents to prevent congestion and ensure physical distancing and privacy between families at places of evacuation.

The target beneficiaries will include those living in houses made of light materials less durable to typhoons, and in hazard-prone zones with high number of COVID-19 cases. To ensure list of beneficiaries can readily be prepared to meet the time-critical distribution pre-disaster, IOM and its implementing partners will identify vulnerable families in target municipalities residing in hazard-prone areas in coastal lines, flood plains and volcanic slopes, families living in shelters and houses made of light materials less durable to typhoons.

Interventions by United Nations Populations Fund (UNFPA)

Objective: Women, adolescent girls and transgender women especially the vulnerable have safe space, dignified access to protection services and participate in GBV risk prevention and response. Vulnerable women and girls have reduced risks from hazards that threaten their Sexual & Reproductive Health & Rights (SRHR) and are free from Gender-based Violence (GBV) and Sexual Exploitation & Abuse (SEA).

Protection actors will provide life-saving Protection information and services to more than 10,000 vulnerable women and girls. Key interventions include CP & GBV referral pathways in affected areas, modified dignity kits and cash for work as GBV monitors.

The provision of Cash for Work (CFW) to 810 pre-identified women and youth leaders (including BHWs, Daycare workers and LGBTQI) in the community (EC and non-camp based) who have been trained as community-based GBV monitors will provide protection information activities and community engagement to most vulnerable women and girls.

SRH interventions include provision of Cash Voucher Assistance to Pregnant women to support their access to continuing maternal health services; the Distribution of GoBags to 7,000 Adolescent Girls (10-19 years old) to support menstrual hygiene; distribution of life-saving SRH information through SMS and Social Media channels.

Protection is central to early actions that humanitarian workers need to take on. By providing life-saving information, commodities and cash assistance, individual IDP women and girls will be equipped to address their SRHR and protection needs, both before and after the onset of the typhoon that is expected to disrupt multiple supply chains and sources for SRHR and GBVIE commodities.

Interventions by United Nations Children's Fund (UNICEF)

Objective: To implement a series of multi-sectoral anticipatory action interventions related to Education, Nutrition, WASH and Child Protection, that will ensure 42,000 children living in 22,000 households have sufficient resources to address their most immediate needs and are better able to mitigate impacts of a significant typhoon. In addition, 125,000 people will be reached through messaging on key lifesaving behaviors and preparedness actions.

Interventions: By using social safety net mechanism of the government, an unconditional cash transfer of \$20 (Php 1,000) will be provided as a top-up, intended to finance the child-centered needs of vulnerable families that are projected to be impacted by a Category 4 or 5 typhoon. The inclusion of additional cash, representing a portion of the minimum expenditure basket computed for basic needs of children for health, nutrition, WASH, education, and child protection, will allow the vulnerable households with children to procure basic needs and continue to access time-sensitive services before the typhoon makes landfall, and before services are totally disrupted.

Complementing the cash component will be a number of services and distributions made three days before landfall:

- **Distribution and tracking of nutrition supplies and commodities** (e.g. RUTF, CMV, ReSoMal, MUAC tapes) for health facilities, to ensure that LGUs will have a ready stock of key supplies that may be immediately deployed after a typhoon.
- **Delivery of water quality monitoring and treatment supplies and equipment** to Provincial Health Offices to allow for the immediate testing of water quality and appropriate treatment, thereby maintaining or immediately restoring access to safe water by the disaster-affected population.
- **Activation of Child Protection help desks and help lines** to prevent or mitigate abuse, neglect, exploitation, and violence against children by strengthening child protection systems and support families and communities in their protective functions.
- **Distribution of family preparedness checklists and various sectoral messages** on health, nutrition, WASH, protection, and education to equip families with vital information needed to reduce the impacts of the typhoon.

These anticipatory action interventions require inter-cluster coordination to ensure the harmonization in the content and delivery of key messages to target beneficiaries. Coordination will be ensured with the CERF AA Cross-Cutting team, to facilitate delivery of common protection messaging across all sectors.

Interventions by World Food Programme (WFP)

Objective: Provide blanket multi-purpose cash assistance for beneficiaries to initiate preparatory actions to protect their assets, lives, and livelihoods before the arrival of a forecasted Category 4 or 5 typhoon. Beneficiaries will be able to use cash assistance for the procurement of food stocks and other essential needs, as well as for the early harvesting of crops and livestock evacuation, among others.

Intervention: The anticipatory action intervention of WFP intends to provide unconditional, cash assistance to up to 25,000 beneficiary households (125,000 individual beneficiaries) in three provinces in Region V (Bicol Region).

Cash will be released three days before the onset of the disaster once the activation triggers are met. WFP aims to register beneficiaries in SCOPE, corporate beneficiary information and transfer management platform, at least 6 weeks before the Readiness alert. To this end, beneficiaries will be pre-identified utilizing existing government databases that have determined the most vulnerable population in the prioritized barangays. These lists will be validated by WFP to ensure accuracy before being registered in the SCOPE platform.

WFP will work with UNFPA in providing a top-up cash for health on top of the multipurpose cash to be given to 2,000 pregnant and lactating women (PLW).

Other anticipatory action projects to be aware of

Interventions by OXFAM/ START Network

START Network members will be able to tap into funding from the Anticipation Fund of START Network, pending an alert is submitted by members in the Philippines and subject to the approval and allocation of the START Fund allocation committee, based on pre-agreed criteria and other factors (e.g. perceived capacity of government to respond, other actors responding, value added, etc.).

START Network is also setting up a DRF system for the Philippines, funding that would be automatically released when a trigger is breached. As per current plans, DRF may be able to activate by the last quarter of 2022 in target pilot areas in Surigao del Norte, Catanduanes and Eastern Samar. Resource mobilization activities are underway for this DRF project both for the Philippines and Bangladesh.

OXFAM will be able to activate its AA interventions already in 2021 for their BREADY project in Salcedo and SHARPER in Catanduanes, subject to the threshold set for activation and in concurrence with LGU partners.

Interventions by Philippine Red Cross (DREF)

The Philippine Red Cross Early Action Protocol is linked to the FbF by the DREF (Forecast based Action by Disaster Relief Emergency Fund) resulting in the automatic flow of funds to the chapters at-risk once the typhoon trigger is reached.

The typhoon Early Actions of the PRC will be triggered if the forecasted impact of the winds on housing, 72h before landfall, is more than 10% of houses predicted to be totally damaged in more than 3 municipalities. In terms of scale, PRC will activate in maximum three provinces (RC Chapters) at the same time with maximum amount of CHF 250,000.

Interventions by the Philippine Disaster Resilience Foundation (PDRF)

PDRF is a private sector network, bringing together Philippine private sector to support disaster resilience building before during and after emergency. As an observer to the HCT and a member of the OCHA and UNDP-led Connecting Business initiative (CBI), it is deeply integrated into activities of humanitarian partners in the Philippines.

OCHA, UNDP and PDRF were able to secure funding from CBI to enhance the role of the private sector in Anticipatory Action in the Bicol Region (Region V) in 2021. Particularly, the project will:

- Harness expertise of the private sector such as business continuity as part of Anticipatory Action objectives
- Create a toolkit for business owners to prepare and mitigate expected impacts of typhoons ahead of their landfall.

- Use lessons learned to support AA evaluation and contribute to the HCT learning about AA.

Summary table

Organization	Partners	Cluster/Sub-cluster	CERF Financing	CERF Financed Reached Population	Activities	Reach with additional funding source
FAO	Oxfam	FSAC	1,719,076	16,000 agriculture-dependent and/or vulnerable families	Multi-purpose cash	around USD 80,000 for preparedness activities
FAO		FSAC		80,000 households	Messaging to farmers and fisherfolks	
FAO		FSAC		500 households	Safe storage sites	
FAO	PRC	FSAC		150 families	Cash for work for early harvesting and livestock evacuation	
FAO	Oxfam	FSAC		50 livelihoods/small merchants	Cash for vulnerable livelihoods	
FAO	UNFPA			1000 pregnant women	Cash for Health (top-up)	
FAO	IOM			2500 families	Cash for Shelter (top-up)	
IOM	PRC/CRS/W V/CARE	CCCM	2,259,999	69 Evacuation Centers	CCCM Kits and IEC materials, inclusive of CCCM COVID-19 Operational Guidelines	
IOM	PRC/CRS/W V/CARE	CCCM		13,110 families	Multi-purpose CBI (Shelter Strengthening Kits) and IEC materials*	653,275
UNFPA	UNFPA, WVI, OXFAM, EDUCO, PLAN	GBV/SRH	733,953	135 local actors	Reorientation of local actors (LGU, CSO, volunteers) and coordination	USD 80,000 for capacity building activities for AA SRH and GBV
UNFPA	UNFPA, WVI, OXFAM, EDUCO, PLAN	GBV/SRH			Transportation of Commodities (Dignity Kits, GoBags for Girls) in Nine Municipalities	
UNFPA	UNFPA, WVI, OXFAM, EDUCO, PLAN	SRH		7,000 adolescent girls 10-19 years old	Provision and replenishment of GoBags for Adolescent	USD 250,000 for the prepositioning
UNFPA	UNFPA, WVI, OXFAM, EDUCO, PLAN	SRH		10,000 women and adolescent	SMS and Social Media SRH information sharing to women and adolescent girls and boys	USD 20,000 training for youth organizations - development of SRH core messages

UNFPA	World Vision, PLAN, Educo	GBV		810 Community-based Women Volunteers - Women leaders, BHWs & DayCare Workers, LGBTQ leaders	Provide Cash for Work to vulnerable women to do GBV risk mitigation before impact	
UNFPA	UNFPA, World Vision, PLAN, Educo	GBV		3,000 Women - Pregnant, Lactating, with Disability, Female headed household, Transgender, Adolescent Mothers	Replenishment and distribution of Protection Commodities (Dignity Kits) to vulnerable women & girls	USD 170,000 for the prepositioning
UNFPA	UNFPA, World Vision, PLAN, Educo	GBV		30,000 women and adolescents	Monitoring GBV protection in pre-evacuation and distribution of GBV referral pathways	USD 30,000 for the development and printing in advance
UNFPA	UNFPA, World Vision, PLAN, Educo affected target LGUs	GBV/SRH		Conduct of pre and post AA M&E activities	Post-distribution monitoring, evaluation and learning activities	USD 20,000 for the M&E design development and pre-AA data gathering
UNICEF		CP/Educ/Nutrition/WASH	820,872	22,000 households (110,000 boys, girls, men, and women)	Cash: Multi-purpose unconditional cash transfer for most vulnerable households to be provided as top-up	
UNICEF		CP/Educ/Nutrition/WASH		125,000 people	RCCE: Community engagement and dissemination of information and key messages on family preparedness, IPC, health, nutrition, hygiene, protection, and education	
UNICEF	CWC, World Vision, DILG, PNP	Child Protection		1,000 women, girls and boys accessing protection, GBV risk mitigation, prevention, or response interventions	Strengthening of child protection systems (including activation of help desks and helplines)	
UNICEF	NNC, DOH, LGUs, CSOs	Nutrition		1,000 Children; 1,500 pregnant and lactating women	Distribution of life saving nutrition commodities and supplies to targeted beneficiaries (RUTF, MUAC Tapes)	
UNICEF	TBD	WASH		At least 10,000 vulnerable households supported by 3 provincial health offices (PHOs)	Prepositioning water quality monitoring & treatment supplies & equipment, basic COVID19 IPC supplies, and materials on	

					WASH and COVID19 IPC	
WFP		FSAC	1,951,256	25,000 HH	Multi-purpose unconditional cash-based transfer	130,000 USD from WFP HQ and 23,000 USD from DFAT
WFP	UNFPA	Health/SRH		2000 pregnant women	Provision of Cash for Health for Pregnant and Lactating Women (top-up)	

5. Pre-agreed Financing

CERF

The Emergency Relief Coordinator agreed to allocate up to \$140 million from CERF to support a series of anticipatory-action interventions. All funds will be disbursed through CERF's Rapid Response window; CERF has not created a separate "Anticipatory Action" window.

CERF will disburse funds to anticipatory action pilots on a no-regrets basis once three conditions are met:

- Endorsement by the relevant Resident/Humanitarian Coordinator of the Anticipatory Action framework (this document) and the CERF application package comprising an application chapeau, agency-specific project proposals and agency-specific budgets (in annex); and
- Pre-approval by the Emergency Relief Coordinator of the Anticipatory Action framework (this document) and the CERF application package comprising an application chapeau, agency-specific project proposals and agency-specific budgets (in annex);
- Activation of either the readiness trigger or the action trigger within a maximum of two years from the ERC's pre-approval of the framework.

For the 2021/2022 anticipatory action pilot in the Philippines, the ERC has agreed to allocate up to \$7.5 million. The pre-arranged financing agreement with CERF is in place for one severe typhoon event over a two-year pilot period from the moment this framework document is pre-endorsed and pre-agreed. During this timeframe, CERF disbursement is guaranteed once a trigger is reached.

As the CERF funding will be activated and distributed as automatically as possible immediately once the defined triggers are reached, CERF will rely on a streamlined application process to ensure that funds are disbursed to UN agencies quickly. This will involve pre-filling and pre-approving project proposals in advance and maintaining those documents on file until the readiness trigger or action trigger is reached.

CERF will disburse funds on a no-regrets basis as soon as either the readiness trigger or the action trigger is reached. While a portion of the fund can be used immediately upon disbursement for readiness activities, the remaining portion of the funding can only be used if and when an action trigger is reached. The amount of funding for readiness vs action activities will be clearly defined in the pre-approved project proposals and budget. The need to distinguish between these two cost categories in advance is important given the different potential scenarios, though in the context of the Philippines there is indeed only hours available between the two triggers and very few activities could be implemented in the readiness phase. Compared to other, more slow-onset pilots, preparedness activities will be critical.

Of note, should there be no readiness trigger, but only an action trigger, the pilot would still be activated. CERF would disburse 100% of the funds as per the pre-agreed project proposals. Agencies will do their utmost to deliver assistance as quickly as possible, but within the 3-day timeframe envisaged by the project proposals. In practice, this means that some


actions can no longer be carried out ahead of landfall. This scenario would provide additional learning opportunities to be discussed in the learning committee.

Highlighting challenges and limitations of the current financing model

While financing is increasingly available to carry out anticipatory actions, collective anticipatory action at scale requires an investment in building the pilots. As with other CERF pilots, these “start-up costs” are incurred by participating agencies prior to the activation of a pilot set up effective anticipatory actions. In 2021, for example DREF revised its financing arrangements for the anticipatory action in the Philippines and allows for about a third of funds to be used for preparedness activities.

Anticipatory Action Partnership and Funding framework

AA Partnership and funding framework

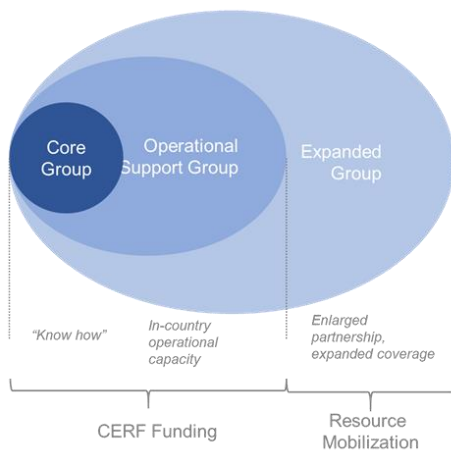

Considering significant interest among all the Philippines Humanitarian Country Team (HCT) partners to join humanitarian anticipatory action activities, the HCT sees the 2021-2022 typhoon season as a year when the humanitarian community in the Philippines is being invited to innovate with early action approaches, using CERF funding as a catalyst for it. Above all, the pilot has been identified as a learning opportunity between anticipatory action actors, humanitarian response community, the government, private sector and local academia. While a considerable funding has been secured by the CERF, additional funding opportunities are being actively pursued for the Expanded group of partners that will not directly benefit from the CERF funding.

IFRC DREF will activate FbF protocols if their trigger is reached. To be complementary with CERF, they will most likely not target the same municipalities.

6. Learning

An ad hoc M&E group, i.e. the Learning Team, was established to assess how collective and coordinated early action can work at scale for typhoon response in the Philippines as well as to capture and share learning about how to improve the approach to planning and implementation of anticipatory interventions. To ensure the localization of learning, local actors such as the government, will form part of the M&E group.

Monitoring & Evaluation

Learning from the pilot aims to generate proof that when early action is possible, it is faster, cheaper and more dignified than a traditional humanitarian response.

Some of the key questions to be answered through the Learning include: How does anticipatory action help households mitigate the shock in the immediate/short/long term? How do households use the cash given and which choices does it enable? What is comparative success among FAO’s, IOM’s & WFP’s multi-purpose cash approach, which modality worked

best and what are comparative advantages in terms of feasibility/logistics, beneficiary results achieved? What is the Impact of multi-purpose cash and EW messaging on key beneficiary outcomes? What is the added value of joint targeting/multi-sectoral support for beneficiaries who received AA support from multiple agencies? Does anticipatory action constitute a more cost effective and timely response? Particularly interesting will be to assess the synergies among interventions carried out by individual UN agencies and their partners and to derive lessons learned on the importance of coordination and scale.

In addition to agency-specific M&E indicators, a set of common indicators will be agreed to monitor impact and the delivery model as well as to measure cross-cutting issues such as PSEA and protection. Agencies delivering multi-purpose cash assistance will all use a control group to evaluate impact. IOM and WFP will compare results also with the CERF RR Response grant for Typhoon Goni (November 2020 – May 2021), which covered some of the same provinces in Region 5.

An initial list of common indicators aiming to connect multiple interventions:

Timing (in relation to 3-day trigger):

- When was funding released (by CERF and by implementing partner)?
- When did anticipatory action implementation begin (by implementing partner, if applicable)?
 - Warning
 - Mobilization
 - Field implementation
- # of beneficiaries in receipt of (full package of) anticipatory actions by end of day [1-3] after trigger, by location
- % of total target beneficiaries in receipt of (full package of) anticipatory actions by end of day [1-3] after trigger, by location
- If a traditional post-typhoon humanitarian response occurred or is underway, when did beneficiaries receive assistance by the agency/implementing partner? What assistance did they receive? Comparison with Typhoon Goni assistance.

Outputs / reach:

- # of beneficiaries who received the intervention, by intervention type (if more than one action or more than one population group targeted), by location
- % of total target beneficiaries who received the intervention, by intervention type (if more than one action or more than one population group targeted), by location
- [If action is deployed through distribution point] Wait time (in minutes) from arrival until benefit was received (ask at time of distribution)
- [If action involves distribution and modality allows for brief interaction with beneficiary] Ask a random sample of beneficiaries:
 - A. Did this assistance come timely regarding your needs?
 - B. How useful is what you received to help you avoid or cope with the impacts of the typhoon?
 - C. Is there anything that could have been done differently to help you better avoid or cope with the impacts of the typhoon?

Main implementation bottlenecks (main barriers or enablers that affected implementation):

- Financing / transfers
- Human resources
- Logistics and accessibility
- Beneficiary identification and reach
- Communication
- Safety and security

Agency-specific M&E: FAO

Objective

The impact analysis of FAO's AAs in the Philippines aims to assess whether the objectives of the intervention have been achieved. The analysis will focus only on FAO's interventions i.e. (1) multipurpose cash; (2) safe storage sites and (3) early warning messages. It will assess whether this assistance helped protect agricultural assets and food security of vulnerable households from the impact of a typhoon.

Activities

Quantitative Study

The following activities are envisaged to carry out the study:

1. Desk review on previous similar studies conducted in the Philippines and/or similar other contexts.
2. Preparation of the surveys and the data collection plan
3. Programming of questionnaires onto Kobo Toolbox
4. Training of enumerators
5. Pre-testing of the questionnaire
6. Sampling (based on sampling frames of beneficiary and control HH)
7. Data collection, either by phone or in person in the areas targeted by the project.
8. Analysis of survey
9. Presentation of the preliminary findings
10. Drafting of technical report and communication materials.

Qualitative Study – with individuals & donors

1. Preparation of survey questions and data collection plan
2. Programming of questions onto Kobo Toolbox (if required)
3. Training of interviewers
4. Data collection, either by phone or in person
5. Analysis of qualitative data
6. Presentation of preliminary findings (combined with above study)
7. Drafting of technical report and communication materials (linked to above study).

Outcomes

The following outcomes are envisaged from this analysis:

- Improved understanding of the benefits of AAs to protect agricultural livelihoods and food security ahead of sudden onset events such as typhoons.
- Lessons learned and programmatic insights on AA as a means to prevent and mitigate the impact of hazards, strengthening food security and building resilience of vulnerable households in hazard-prone areas.
- Learnings on the role of FAO within the OCHA/CERF AA Pilots, and the role of coordination and scale for the success of the AA approach.

Agency-specific M&E: IOM

IOM will develop a monitoring framework that is context sensitive and aligned to COVID-19 protocols. The monitoring framework will define the methodology, frequency, tools and mechanisms for data collection which are most appropriate and effective for measuring activity, output, impact indicators as reflected in the results matrix. In line with the principles of Do No Harm, transparency and accountability to affected populations (AAP) mechanisms will be integrated into the framework.

IOM will use a range of data collection tools and methodologies, ensuring that they meet the requirements to effectively monitor diverse types of activities and outcomes. Given the rapidly changing operational environment in emergencies, IOM has prioritized flexibility and adaptability in the roll-out of data collection methods. Where possible, IOM will use the Kobo Toolbox to improve the speed and quality of data collection across project sites. As the project will cover some remote, isolated and hard to reach areas, as well as to remain adaptable to the changing dynamics of COVID-19 in the country, remote monitoring strategies will be implemented as necessary. In safeguarding the privacy of beneficiary information, IOM's institutional data protection and data security principles will be adhered to.

To ensure data quality and integrity, the project will benefit from three streams of data collection, validation and triangulation. Output-level results monitoring, through regular site visits and post-distribution monitoring make up the first stream. This will be done through site assessments and surveys using a representative sample. A secondary data gathering through focus group discussions, key informant interviews, and learning exercises with local stakeholders make up the second stream and will be used where possible to further verify data received.

At the end of the project, IOM will conduct an After-Action Review (AAR) of project achievements to date, focusing on effectiveness of implementation and strategies undertaken, issues that required corrective action, best practices and lessons learned. The AAR exercise will also result in the formulation of concrete recommendations to further strengthen the AA pilot exercise.

Agency-specific M&E: UNICEF

With the proper conduct of an Evaluation, UNICEF hopes to gain enough learnings on whether its Anticipatory Action interventions have prevented further losses and strengthened security of households in the short run.

Among the areas that can be assessed through the evaluation are:

1. If the AA support has increased prevention activities at the household level
2. If the AA support has reduced asset losses for families
3. If the AA support has reduced other coping strategies
4. If the AA support has sustained or increased child and family food consumption (at time of survey)
5. If the AA support has increased well-being among children and families (at time of survey)
6. If the AA support has an impact on family's ability for quick recovery

Specific to the sectors that will be covered by UNICEF, we also aim to learn the following from this pilot:

Cash	▪ To understand what mechanisms enable or hinder the use of existing national government social protection systems for anticipatory action or ex-ante disaster financing ▪ To contribute to the policy dialogue on shock responsive social protection in the context of ex-ante interventions
RCCE	▪ To understand which communication interventions work best as entry points for multi-sectoral RCCE messaging ▪ To understand better how two-way communication interventions can better work in the context of AA, given feedback mechanisms and possible opportunities for dialogue.
Child Protection	▪ To identify AA entry points for improving and providing more timely Child Protection response initiatives, particularly on preventing and responding to family separation, VAC/ GBV and SEA concerns. ▪ To check feasibility of AA cash-based interventions to improve Child Protection in emergencies programming, particularly on improving help seeking behaviour for protection and MHPSS concerns.
Nutrition	▪ To determine the viable Nutrition-In-Emergencies (NiE) interventions for anticipatory actions ▪ To establish operational knowledge of the Nutrition Cluster to deliver NiE Minimum Service Package ▪ To identify AA principles and approaches that can be adapted in the strengthening of the NiE planning and implementation of the National and local sub-clusters
WASH	▪ To get a sense of effectivity of utilising cash transfer programming in the distribution of basic hygiene supplies over in-kind distribution ▪ To determine if anticipatory action could contribute to better promotion of maintaining good health and hygiene during disasters and emergencies and better prevent spread of (water-borne) diseases ▪ To identify further capacity-building needs of responder at the local level, e.g., provincial health offices, to deliver immediate and critical WASH responses, e.g., on water quality monitoring and treatment
Education	▪ To identify Education items households spend on in the context of anticipatory action ▪ To analyse the communication materials to support the rapid dissemination of messages related to education <u>and how it affects</u> the Education-related expenditures of the households

Process learning

Process learning will be applied throughout the development of this framework and a number of issues already surfaced that would merit further consideration, such as the importance of setting aside sufficient start-up funds to enable UN agencies with preparedness activities. Considering COVID-19 operational reality, additional focus was placed on supporting safe pre-emptive evacuations and ensuring hygiene protocols are observed in evacuations centres. The pilot has been

developed jointly by the UN agencies with deep expertise in forecast-based financing and those with operational capabilities and years of experience in responding to highly unpredictable typhoons in the Philippines.

Process learning will consider building blocks of the Framework as key themes for process learning:

1. Forecasting model and triggers (suitability of selected thresholds, learning from the 2-step trigger; evaluation of using a single scenario activation, risk of false alarms, etc.)
2. Coordination and Partnerships (to evaluate the use of coordination platforms, importance of localization, collaboration with the government (national/local); collaboration with AA TWG, etc.)
3. AA Intervention selection and design (beneficiary selection and registration, approach to cash interventions; coordination around in-kind distribution, centrality of protection, engagement with beneficiaries, etc.)
4. AA Financing (preparedness costs and the level of financial risk CERF and partners take; process of finalizing the proposals; how quickly were funds disbursed)
5. Implementation (issues with implementation of different cash modalities; assistance offered inside/ outside EC; appropriateness of interventions considering the risk, how was duty of care addressed)
6. Approach to learning, reporting, communication about the pilot

No funding has been centrally provided by OCHA for process learning for this pilot and agencies will look into hiring a local consultant with required expertise which may take a few months.

Independent evaluation

If the pilot is triggered (3-day activation trigger), OCHA will commission an independent evaluation to gather and analyse data documenting the results by focusing on the delivery model and on evaluating impact on household income. The ad-hoc pilot learning, monitoring and evaluation committee, chaired by OCHA, will oversee the evaluation.

Advocacy and public communication

At the request of the RC/HC, the UN agencies and partners agreed to put strong emphasis on communication activities also to ensure communicating as “One UN” and communicating the story before, during, and after the AA response. OCHA prepared an [operational communications plan](#) for the project, including key messages, communication activities, available resources and approach to communicating impact.

The focus of communications efforts will be on demonstrating that Anticipatory Action is not only possible from an operational and practical point of view, but that acting prior to the onset of a predictable shock is significantly faster, more dignified, and more effective than traditional humanitarian response.

The targeted audiences for this communication plan are humanitarian donors (including CERF donors, but not exclusively), the Government of the Philippines and other stakeholders in the humanitarian community.

Detailed and audience-tailored key messages will be developed by the communications working group in order to guide the messaging of all products, talking points, and activities.

This communication plan will focus on delivering activities and products that are guided by the following principles:

- Communications as “One UN” and “One Humanitarian Country Team.” While it is expected that individual agencies will won’t to produce their own specific communications, this plan will ensure complementary messaging and the delivery of joint products and materials that can be adapted as needed.
- Focus on affected people. The content and story gathering will focus on how Anticipatory Action can have a real human impact on people caught in humanitarian crises. This will include the stories of affected people whose story we will tell before and after the cyclone.

7. Annexes

Annex 1 - Anticipatory Action: Summary table

AGENCY	IMPLEMENTING PARTNERS	INTERVENTION	PREPAREDNESS ACTIVITIES D- 7/6 days	READINESS ACTIVITIES D -5/4 days	AA ACTIVITIES D -3/0 day
FAO	OXFAM TB: 16.000	Cash (multi-purpose)	- Validation of pre-registered beneficiary lists - Validation of mapped financial service providers (FSPs)	- Beneficiary lists are finalized and communicated to the Bank - Participate in national/local PDRA meetings	- FAOR approval for bank transfer given to the Bank (assumes AA funding is pre-positioned in FAO account) - Bank executes fund transfer to beneficiary accounts - Beneficiaries receive their cash in account or receive their transaction number in payout centers
	PRC 150 households	Cash for work for early harvesting and livestock evacuation	Standby / Monitor	CFW participants are identified for specific tasks/actions	- CFW participants are confirmed and assigned for specific tasks/actions - CFW for early harvesting and livestock evacuation are implemented
	OXFAM 50 livelihoods/ small merchants	Cash for vulnerable livelihoods	Standby / Monitor	Beneficiary lists are finalized	Beneficiaries receive their cash in account
	80,000 households	Messaging to farmers and fisherfolks	Finalize messaging specific to areas and sectors based on forecast track and impact	Issue Advisory # 1	Issue Advisory # 2
	500 households	Safe-storage sites	Prepare the pre-identified safe storage sites, ensure availability and safety (else identify alternative options)	- Disseminate locations of safe storage sites and opening schedule Again - Review SOPs on the operation of the safe-storage site	- Beneficiaries start to evacuate livelihood assets into safe sites - Ensure livelihood assets are properly tagged with owners' names - Ensure safe storage sites are secured by a guard
AGENCY	IMPLEMENTING PARTNERS	INTERVENTION	PREPAREDNESS ACTIVITIES D- 7/6 days	READINESS ACTIVITIES D -5/4 days	AA ACTIVITIES D -3/0 day
UNICEF	125,000 people reached	RCCE: Community engagement and dissemination of information and key messages on family preparedness, IPC, health, nutrition, hygiene, protection, and education	inter-cluster coordination to ensure the harmonization in the content and delivery of key messages to target beneficiaries.	- Printing and delivery of rapid assessment forms, anticipated communication materials (life-saving information) - Deployment of communication equipment - Discussion with LGUs on the establishment/use of feedback mechanisms	- Dissemination of key communication/information materials through various communication channels - Dissemination of information on hotlines and information centers - Mobilization of frontline workers to support RCCE anticipatory actions
	22,000 households (110,000 boys, girls, men, and women)	Multi-purpose unconditional cash transfer	Coordination with DSWD and LandBank	Generation of list of households with children from DSWD Listahan	Confirmation is provided to DSWD/Landbank to include UNICEF top-up payments in their distribution; DSWD distributes through their FSPs which then credits to beneficiary accounts

	CWC, PNP, NGO TBD <i>1,000 women, girls and boys</i>	Strengthening of child protection systems	Promotion of messages on preventing family separation; as well as abuse, violence, exploitation of children.	- Updating of referral pathway, facilitate its adaptation, and dissemination of by inter-agency members including recognizing signs of VAC. - Activation/ sensitization of helplines to support affected families in reporting concerns on protection, and access protection services. Activation or sensitization of helplines to provide MHPSS services. - Establishment of child protection help desks or screening points at key locations (such as reception and arrival areas, schools, food distribution centres, hospitals, etc.) and/or during planned population movements to identify and prevent family separation.	- Identification and activation of PNP VAWC/ Child Protection focal points at proposed evacuation centers. - Operational mobilization costs for Child Protection focal points to support coordination, communication, and transportation during emergency response. - Activation of Community Facilitators to support safe spaces, peer to peer activities, focused non-specialized psychological support, or referrals to specialized mental health clinical care. - Movement of CFS tents (if deemed necessary) and other MHPSS supplies to critical installations/ locations. - Refresher orientation of staff and preparation logistical equipment for case management and immediate family tracing and reunification (FTR)
	NNC, DOH, LGUs, CSOs <i>1,000 Children 1,500 pregnant and lactating women</i>	Distribution of life saving nutrition commodities and supplies.	Cluster coordination: inventory of health facilities in CERF AA areas; mapping of facilities that can provide alternative/surge support for nutrition and health services to typhoon-affected areas; and determining surge support capacities and agreements with LGUs. Access (NINA) Nutrition Initial Needs Assessment	Distribution of child and adult MUAC tapes and intensified MUAC screening of PLW of children U5 will be completed.	Delivery of and replenishment supplies to facilities where needed and surge of cases or acute malnutrition is anticipated.
	<i>10,000 vulnerable households</i>	WASH and COVID19 IPC	- Capacity-building (training) on WASH in Emergencies, including water quality monitoring & treatment and COVID19 IPC, for WASH and Health response personnel at provincial/PHO level, including formulation of emergency response plans - Procurement of water quality monitoring & treatment supplies and equipment (portable water testing equipment, e.g., PML, CBT, chlorine granules, sodium hypochlorite products, e.g., Aquatabs, Hyposol, etc.) and basic COVID19 IPC supplies (face masks for both adults and children, face shield,	- Deployment of water quality monitoring & testing supplies & equipment, basic COVID19 IPC supplies, and WASH-COVID19 IEC materials in the target provinces/PHOs - Pre-testing of digital water quality monitoring IM system, including reporting system	- Prepositioning of water quality monitoring & treatment supplies, basic COVID19 supplies, and WASH-COVID19 IEC materials in the target LGUs/PHOs - Refresher training on water quality monitoring and treatment for WASH and Health personnel previously trained in the target PHOs - Activation of digital IM system for water quality monitoring - Distribution of IEC materials on WASH-COVID19 in line with pre-emptive evacuations being implemented by the LGUs, e.g., in

			etc.) at the UNICEF PCO level - Setting up of digital water quality monitoring information management (IM) system (including reporting), e.g., Kobo Collect - Printing of WASH-COVID19 IEC materials - Provision of one (1) unit of water treatment unit (WTU) specifically in San Andres municipality in Catanduanes Province but with the intention of serving other municipalities that will be impacted by the typhoon in coordination with the provincial LGU		designated evacuation sites
AGENCY	IMPLEMENTING PARTNERS	INTERVENTION	PREPAREDNESS ACTIVITIES D- 7/6 days	READINESS ACTIVITIES D -5/4 days	AA ACTIVITIES D -3/0 day
WFP	25,000 families or 125,000 individuals	Multipurpose cash assistance	- Coordination and information dissemination to WU and all local partners, e.g. PLGU, MLGUs - Conduct of pre-crisis survey using OCHA instrument	- Coordination and information dissemination to WU and all local partners, e.g. PLGU, MLGUs - Conduct of pre-crisis survey using OCHA instrument - Participation in PDRA meetings - Information dissemination to Benes through SMS - Prepare payment advice files for WU - Coordination with local authorities on physical distribution of MTCNs - Setting up of CFM mechanism with NGO partner	- Final advisory to WU on activation - Delivery of MTCNs via SMS - Distribution monitoring - Physical distribution of MTCNs to beneficiaries with no cellphones - Distribution of cash in places with no SMS
	25,000 households or 125,000 individuals	Multipurpose cash assistance - sensitization	Coordination with Barangay LGU (BDRRC) and purok heads	Release of printed MTCN + community sensitization in the Barangay in coordination with the LGU; coordination with WU branches for an anticipated cash distribution and ensure minimum health protocols are followed in WU branches; ensure CFM mechanisms followed/implemented	
AGENCY	IMPLEMENTING PARTNERS	INTERVENTION	PREPAREDNESS ACTIVITIES D- 7/6 days	READINESS ACTIVITIES D -5/4 days	AA ACTIVITIES D -3/1 day
IOM	CRS, PRC, WV 13,110 families / approx 65,500 individuals	Multi-purpose cash assistance + Sectoral Top-up (Shelter)	Monitoring of PAGASA Typhoon Advisories; Deployment of Mobile IOM and IP AA Teams; Participation in PDRA meetings at Provincial/Municipal levels; Monitoring of Municipal Pre-Emptive Evacuation Plans; Alerting of target	Monitoring of PAGASA Typhoon Advisories; Participation in PDRA meetings at Provincial/Municipal levels; Monitoring of Municipal Pre-Emptive Evacuation Plans; Alerting of target Barangay LGUs and Families; Advice Palawan on final number and list of MTCA recipients,	Monitor the pre-emptive evacuation of the target families to ECs and host houses; Facilitate and monitor MTCA pay-out at Palawan on day 1 & 2 once people are already in ECs/host houses; ensure that all listed beneficiaries have received the MTCA at

			Barangay LGUs and Families; Alerting of Palawan (FSP) branches; Alerting of local hardware stores, grocery stores for AA purchases of beneficiaries	transfer funds; preposition IOM & IP AA teams; monitor pre-emptive evacuation announcement of LGUs; alert the target beneficiaries through SMS	end of day 1 & 2; facilitate and monitor visits of beneficiaries to grocery stores, markets, hardware stores (for recipients of SSKs); monitor the Shelter Strengthening activities of SSK recipients; monitor and ensure that all beneficiaries are already in the ECs on day 3
AGENCY	IMPLEMENTING PARTNERS	INTERVENTION	PREPAREDNESS ACTIVITIES D- 7/6 days	READINESS ACTIVITIES D -5/4 days	AA ACTIVITIES D -3/0 day
UNFPA	UNFPA, World Vision, PLAN, Educo, OXFAM, affected target LGUs <i>10,000 women and girls</i>	A. Provision of Adolescent GoBags B. Provision of Cash for Health for Pregnant and Lactating Women <u>Sub activity</u> SMS and Social Media SRH information sharing to women and adolescent girls and boys	- Alert warehouse and logistics providers - Prepared activation of Annual Workplans with implementing partners - Meeting with implementing partners for Re-orientation of AA action plans - Meeting with local actors to discuss readiness and activation actions.	- Transportation of GoBags for adolescent girls (10-19) - Re-orientation of barangay health care workers and community leaders - Social media and SMS text blasting on SRH information and dissemination for risk mitigation	- Procurement and distribution of GoBags for Adolescent Girls - Cash for Health for pregnant and lactating women *Procurement is for replenishment of supplies
	UNFPA, World Vision, PLAN, Educo, OXFAM, <i>10,810 women and girls</i>	A Distribute Protection Commodities (Dignity Kits) to vulnerable women & girls B. Provide Cash for Work to vulnerable women to do GBV risk mitigation before impact <u>Sub activity</u> Development and printing of GBV referral pathway		- Transportation of dignity kits, printed SRHR and protection referral pathways - Re-orientation of community-based volunteers on cluster GBV actions including Referral Pathways	- Procurement and distribution of Dignity Kits - Printing and distribution of Localized GBV and MHPSS Referral Pathways - Cash for Work for 800 women volunteers *Procurement and printing are for replenishment purpose

Annex 2 – DRAFT trigger messages

Readiness trigger message

From: Gustavo Gonzalez, RC/HC

To: CERF secretariat

CC: OCHA Philippines, Core Group

Dear CERF secretariat,

The readiness trigger has been reached as based on 510 model forecast and PAGASA data a Tropical Cyclone with potential to reach category level 4 or higher (greater than 200 km/h maximum 1-minute sustain wind speed) is projected to directly impact areas within Region 5 and 8.

Details are attached.

Grateful for your swift attention to this notice.

Sincerely,

Gustavo Gonzalez, RC/HC

Activation trigger message

From: Gustavo Gonzalez, RC/HC or OCHA Philippines Head on his behalf

To: Core Group

CC: CERF secretariat

Dear Core Group,

Since the readiness trigger has been reached, 510 and the Triggers Team monitored every 6-12 hours the forecast model and its predictions on the number of totally damaged houses.

Based on the latest impact map, activation threshold has been reached as the predicted number of destroyed houses amounts to [XXX] with [xx%] probability, which falls within the range of 50% probability that 80,000 houses or more will be totally damaged and 95% probability that at least 5,000 houses will be destroyed.

We are therefore activating the CERF anticipatory action Framework within the 72 hours (3 days) before projected landfall.

Further details are attached.

Good luck to the teams implementing anticipatory action interventions; stay safe!

Annex 3 - Evaluation of forecasts for anticipatory actions - April 2021

In April 2021, OCHA, Humanitarian Data Centre and the Philippines AA Core Team facilitated discussion among stakeholders about humanitarian anticipatory action work, especially focusing on the various forecasting models developed for typhoon early action.

The team discussed the models currently developed by three key actors (WFP, IFRC/DREF, Global Parametrics) to reach a conclusion on which model would be the most appropriate and what modifications may still be needed.

After careful review and consideration, the recommendation was made to move forward with the IFRC/DREF Typhoon model. We weighed several factors in coming to our decision, and here we will highlight what we consider to be our primary concerns.

Firstly, due to the tight timeline, we wanted to prioritize a model that can be operationalized quickly. The IFRC/DREF model has a demonstrated track record of being operational in a humanitarian context, for the full country down to an admin 3 level. Furthermore, using the same model as IFRC (even with modifications) could help foster interagency coordination.

A second major benefit of this model is that it is open source and free to use, which gives flexibility to modify or alter it to fit our needs, and allows us to freely share the full process as well as the model outputs with our partners, maximizing transparency, accountability and cost effectiveness.

Finally, the IFRC/DREF model developers are keen to address any possible shortcomings of the model, such as integrating PAGASA forecast data.

Find below the [Evaluation matrix](#) used to provide this recommendation and a summary of the three models considered (IFRC/DREF, Global Parametrics and WFP)

Evaluation Matrix

Criterion	IFRC/DREF	Global Parametrics	WFP
Is the trigger based on existing, public forecast data?	Yes: ECMWF tropical cyclone and wind speed forecasts	Yes: use public forecasts from agencies including: National Hurricane Center (NOAA), Central Pacific Hurricane Center (CPHC), Joint Typhoon Warning Center (JTWC), Hydrometeorological Prediction Center (HPC), Ocean Prediction Center (OPC), Fiji Met Service (RSMC Nadi), New Zealand Met Service (TCWC Wellington), METEO France, Australian Bureau of Meteorology (TCWC Darwin), Japan Meteorological Center, ECMWF, etc. However, also use private data such as PAGASA.	Yes (CHIRPS, ERA5), but also uses PAGASA data which is not available to the public
Does the model make use of PAGASA data?	No, but 510 Global is looking into it	Yes	Yes
Is the trigger simple, straightforward and easy to understand?	Partially: Uses a machine learning model to determine relationship between wind speed and housing damage.	Partially. The threshold is simple and based on the probability of a wind speed above a certain value occurring in a location. Several vulnerability indicators are combined to establish what the threshold should be.	Yes, very simple threshold based on rainfall anomaly %
Is the trigger impact basis appropriate for our partner's needs?	Yes. The trigger is based on expected impact (	Yes. The trigger is based off the windspeed intensity that leads to an expected impact (eg percentage of houses destroyed)	Yes -- people affected

	percentage of houses destroyed)		
Is the trigger forecast relatively easy to monitor at regular intervals?	Yes	Yes	Yes
Does the trigger provide us with adequate lead time?	Yes (72 hours or more)	Yes (72 hours or more)	N/A - The model doesn't use forecasted hazards data
Can the trigger be adapted to OCHA specifications by June?	Yes	Partially. It would require effort and budget. The model doesn't currently cover the full country	Likely not
Can we obtain the model output as data that we can edit and share?	Yes	Yes	Probably
Is the model open source?	Yes	No, but it could be	No, but it probably could be.
What would be the cost to get the model operational?	Low. The model is open and fully available.	Medium. Global Parametrics would need to provide a quote and a proposed timeline for this work.	Unclear
What would be the cost to keep the model operational?	Low. The processing is fully automated. Possibility of cost sharing maintenance costs with IFRC/DREF	Likely low to medium.. Global Parametrics would need to provide a quote	Unclear
How well does the model perform?	Precision, recall ~70% for classification model	The model has been running since 2019 and has accurately called the major storms that have passed.	Precision: 17% for Bicol

IFRC/DREF model card

Model Card - IFRC/DREF	
Model Summary - Main contacts: - Aklilu Teklesadik (ATeklesadik@redcross.nl) - Marc van den Homberg (MvandenHomberg@redcross.nl) - Link to model: presentation slides, GitHub	
1. Intended Use A. In-scope use cases: what is the actual and potential scope of the model? a. What is the main output of the model? - Map of predicted percentage of completely damaged buildings per municipality b. What is the geographical scope? - All of the Philippines, down to municipality resolution (admin level 3)	
2. Model Development A. Details of the datasets used to build the model.	


- a. What hazard data is used?
 - ECMWF tropical cyclone and wind speed forecasts
- b. What vulnerability data is used?
 - Housing damage reports from [NDRRMC](#)
- B. Methodology - provide a description of the different analysis steps and how the input datasets are used to train the model.
 - Typhoon track fields calculated using [Willoughby methodology](#)
 - Use XGBoost to correlate wind speed with damage as a function of building materials
- C. How is the trigger threshold defined? What are the known limitations?
 - 10% houses totally damaged (as defined by DROMIC reports) in at last 3 municipalities (1 in 5 year)
 - Use both classification and regression model, and activate if either is above threshold (but for prioritization of areas, use regression model)

3. Model Evaluation

- A. How well does the model perform? Which metrics are used to evaluate it?
 - Classification: Precision / Recall / F1 are all ~0.7 on test set
 - Regression: mean absolute error (MAE) 3%, root mean squared error (RMSE) 7% on test set
- B. How does performance depend on forecast lead time?
 - Forecast worsens significantly with lead time, thus performance is reduced

4. Operational Readiness

- A. Is the model ready to be used to inform humanitarian response?
 - a. Is the model kept up-to-date with the latest datasets?
 - The model is updated continuously with previous storms and damage reports
 - b. Who is responsible for model updating and/or recalibration?
 - Aklilu Teklesadik, Marc van den Homberg
 - c. Is the model ready to be deployed for use as an AA Pilot trigger? If not, what are the additional steps needed?
 - TBD: need to explore if can be used for people impacted instead of houses damaged
- B. Has the model previously been used in humanitarian situations? Is it currently being used by humanitarian organizations for the 2021 typhoon season?
 - Yes, used since 2019, including:
 - Tisoy 2019 (small scale)
 - Ulysses 2020
 - However, missed Goni (2020)

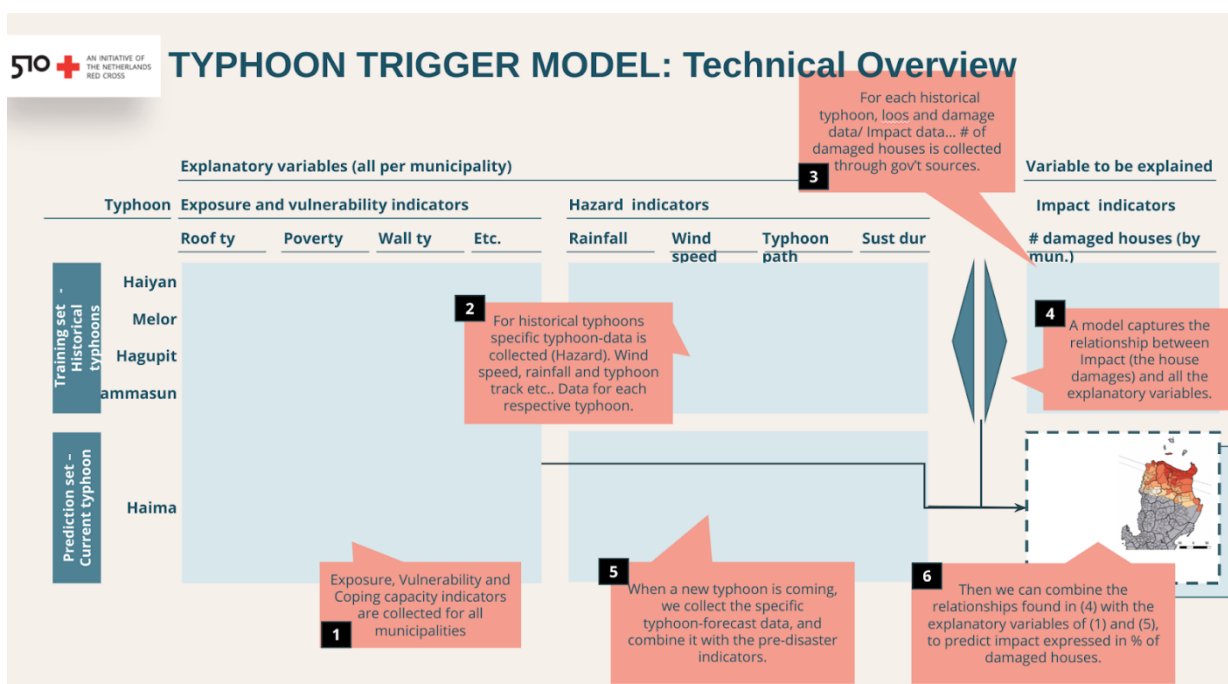

Global Parametrics model card

Model Card - Global Parametrics

Model Summary

- Main contacts:
 - Toby Behrmann (tbehrmann@globalparametrics.com)
 - Wendy Smith (wsmith@globalparametrics.com)
- Link to model: [presentation slides](#)

1. Intended Use

- A. In-scope use cases: what is the actual and potential scope of the model?
- a. What is the main output of the model?
- The probability of exceeding a specific wind speed (based on percentage of forecasts) at a particular location
- c. What is the geographical scope?
- Salcedo, Eastern Samar -- currently being expanded in the Philippines

2. Model Development

- D. Details of the datasets used to build the model.
1. What hazard data is used?
 - Typhoon data from NASA, UKMET, NOAA, CPHC, JTWC, HPC, OPC, RSMC Nadi, TCWC Wellington, METEO France, TCWC Darwin, Japan Meteorological Centre, ECMWF, PAGASA
 - b. What vulnerability data is used?
 - Socioeconomic and damage data provided by Oxfam (Primarily construction of houses)
- E. Methodology - provide a description of the different analysis steps and how the input datasets are used to train the model.
- Typhoon track wind fields computed for each model & ensemble member
 - At each exposure location, if ≥ 5 tracks available, compute fraction above threshold
- F. How is the trigger threshold defined? What are the known limitations?
- Two components: wind speed, and probability. Tuned through internal vulnerability assessment.

3. Model Evaluation

- C. How well does the model perform? Which metrics are used to evaluate it?
- Model performance has been validated historically and real time since 2019. Full data is available.
- D. How does performance depend on forecast lead time?
- The main source of error is represented by the input typhoon models considered. The performance of the impact model is not dependent on forecast lead time.

4. Operational Readiness

- C. Is the model ready to be used to inform humanitarian response?
1. Is the model kept up-to-date with the latest datasets?
 - Yes, it is constantly running and kept up-to-date
 - b. Who is responsible for model updating and/or recalibration?
 - Global Parametrics (Alin Radu, Thom Johnson)
 - c. Is the model ready to be deployed for use as an AA Pilot trigger? If not, what are the additional steps needed?
 - Model is ready to deploy, would need the addition of new geographies
- D. Has the model previously been used in humanitarian situations? Is it currently being used by humanitarian organizations for the 2021 typhoon season?
- Oxfam tested trigger against tropical cyclones in 2019 & 2020 season (3 key events captured)
 - Next steps (in 2021) are to further validate model and increase geographical scope




Methodology

TC Phanfone

Date: 22-12-19

Time: 00:00:00

50 m/s
5 m/s

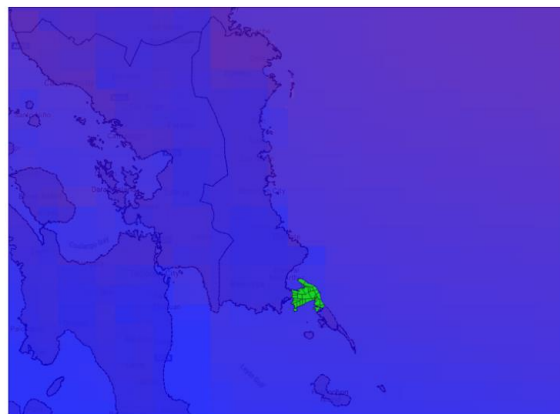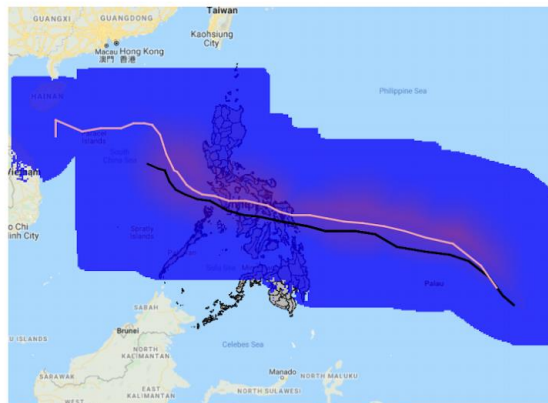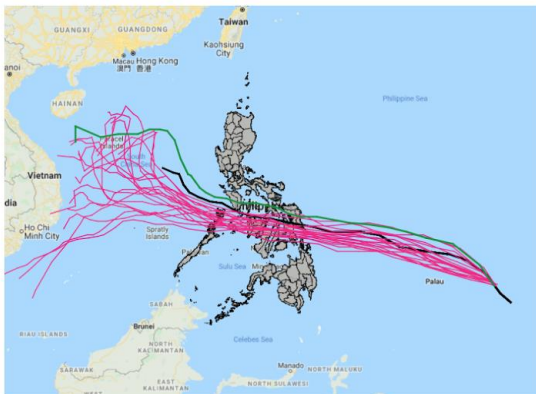

12

GP GLOBAL PARAMETRICS

WFP model card

Model Card - WFP

Model Summary

- Main contacts:
 - Analuisa Candanedo (analuisa.candanedo@wfp.org)
- Link to model: [Presentation slides](#)

1. Intended Use

- B. In-scope use cases: what is the actual and potential scope of the model?
1. What is the main output of the model?
 - Anomalous rainfall percentage, and trigger threshold for impact
 - b. What is the geographical scope?
 - Full national coverage, with analysis done on individual regions (admin level 2)

2. Model Development

- G. Details of the datasets used to build the model.
1. What hazard data is used?
 - NOAA IBTracks storm track frequency
 - CHIRPS & PAGASA precipitation anomalies
 - b. What vulnerability data is used?
 - Relief web (number of people impacted)
- H. Methodology - provide a description of the different analysis steps and how the input datasets are used to train the model.
- Use binary classification for people affected in vulnerability data (affected / not affected)

- Create vulnerability and socioeconomic index, combine with hazard to get risk index
- I. How is the trigger threshold defined? What are the known limitations?
- Use ROC curve to select precipitation anomaly threshold


3. Model Evaluation

- E. How well does the model perform? Which metrics are used to evaluate it?
- For Region V (Bicol), ROC curve selection results in 17% precision with optimal rainfall anomaly threshold of 28%
- F. How does performance depend on forecast lead time?
- N/A

4. Operational Readiness

- E. Is the model ready to be used to inform humanitarian response?
- Is the model kept up-to-date with the latest datasets?
 - Not specified
 - Who is responsible for model updating and/or recalibration?
 - Not specified
 - Is the model ready to be deployed for use as an AA Pilot trigger? If not, what are the additional steps needed?
 - Would need to switch from real-time data to forecast, and possibly from rainfall to wind speed
- F. Has the model previously been used in humanitarian situations? Is it currently being used by humanitarian organizations for the 2021 typhoon season?
- Not yet. The development so far has focused on creating a transparent trigger mechanism to use for response. To start using for AA, they will need to switch to using forecasts instead of real-time data.

HAZARD TIMELINE – Region V

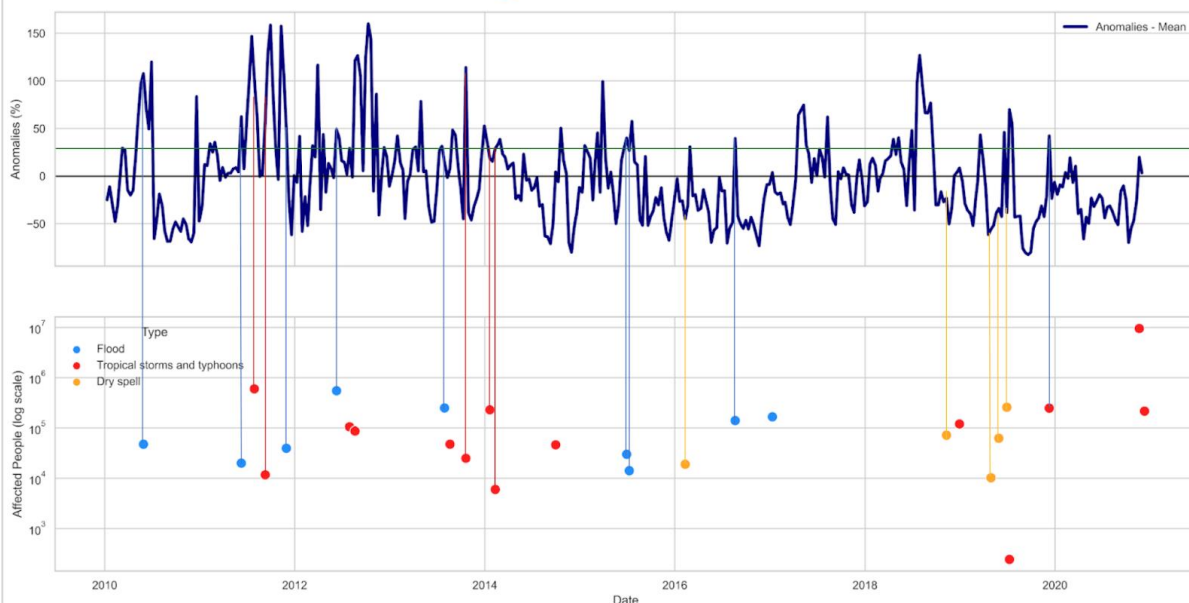

Annex 4: Contact Information

Agency	Name	Email
FAO	Catherine Jones	Catherine.Jones@fao.org
FAO	Maya Manocsoc	maya.manocsoc@fao.org
FAO	Maria Quilla	Maria.Quilla@fao.org
IOM	Conrad Navidad	cnavidad@iom.int
IOM	Troy Dooley	tdooley@iom.int
IOM	Erina Yamashita	eyamashita@iom.int
UNFPA	John Ryan Buenaventura	buenaventura@unfpa.org
UNFPA	Maria Aimee Santos	msantos@unfpa.org
UNICEF	Paul Del Rosario	pdelrosario@unicef.org
UNICEF	Kamille Ruiz	kruiz@unicef.org
UNICEF	Behzad Noubary	bnoubary@unicef.org
UNICEF	Rodeliza Barrientos	rbarrientos@unicef.org
WFP	Giorgi Dolidze	giorgi.dolidze@wfp.org
WFP	Mark Cervantes	mark.cervantes@wfp.org
WFP	Alica Follosco	alicia.follosco@wfp.org
GRC	Elena Suero	fbf1@grc-philippines.org ; elena.suero@germanredcross.de
STARTNetwork	Ana Dizon	Ana.Dizon@startnetwork.org
STARTNetwork	Arvin Caro	cvcaro.startdrf@gmail.com
OCHA GVA/HDX	Leonardo Milano	leonardo.milano@un.org
OCHA GVA/HDX	Monica Turner	monica.turner@un.org
OCHA NY	Zinta Zommers	zommers@un.org
OCHA/CERF	Daniel Ham	daniel.ham@un.org
OCHA/CERF	Samir Mahmoud	mahmoud14@un.org
OCHA ROAP	Daniel Gilman	gilmand@un.org
OCHA-PHL	Manja Vidic	vidic@un.org
OCHA-PHL	Agnes Palacio	palacio@un.org
OCHA-PHL	Tristan Arao	arao@un.org
OCHA-PHL	Joseph Addawe	addawe@un.org
OCHA-PHL	Almudena Montoliu	almudena.montoliu@un.org

Annex 5: CERF Application – Chapeau and agency templates
