



Approved by the UN RC on 15 December 2025

Endorsed by the USG/ERC OCHA on 17 December 2025

Fiji National Anticipatory Action Framework for Tropical Cyclones

Fiji National Anticipatory Action Framework for Tropical Cyclones.....	1
1. Introduction	3
2. Policy Setting and Governance.....	5
2.1 Policy Setting.....	5
2.2 Governance of the Framework.....	7
3 Other Anticipatory Action Initiatives in Fiji.....	10
3.1 Meso-Level Anticipatory Insurance Scheme	10
4 The Risk/Hazard	11
5 The Model: Forecasts, Triggers, and Activation Protocol	12
5.1 The Model/Forecast	12
5.2 Trigger Conditions.....	12
5.3 Trigger Monitoring Process	14
5.4 Activation Protocol	15
6 The Activities: Anticipatory Activities and Operational Plan	17
6.1 Overview	17
6.2 Anticipatory Activities Selection Criteria	17
6.3 Cluster-led Anticipatory Activities	17
6.4 Community-based Anticipatory Activities.....	27
6.5 Cross-Cutting Services	27
6.6 Coordination, Targeting and Information Management during activation	29
6.6 Preparedness and Operational Readiness	30
6.7 Community Sensitisation (Non-Alert Risk Communication)	32
7 The Money: Pre-Arranged Financing.....	33
7.1 Financing Overview	33
7.2 Build Funding	33
7.3 Pre-arranged financing: “Fuel”	34
8 The Learning.....	37
9 Final Provisions	39



Advocacy and Public Communication.....	39
Annex 1 – Sendai GAP policy brief on GBV and SRH	40
Annex 2 – Overview of Stakeholders	41
Annex 3 – Historical Analysis.....	42
Annex 4 – Distribution Lists	44
Annex 5 – DRAFT Trigger Messages	47
Annex 6 – DRAFT Trigger Information Messages.....	48
Annex 7 – Overview of Activities.....	51
UN-funded Activities	51
Fiji Red Cross Early Action Protocol	52
Annex 8 – MoU MWCSP-MoF-WFP.....	53
Annex 9 - Common Early Warning Messages	85
Annex 10 - Common Early Warning Messages Testing Results.....	90
Annex 11 – Coordination Standard Operating Procedure	95
Annex 12 – IDA Forms	100
Annex 13 – Awareness Sheet for Community Leaders.....	102



1. Introduction

Pacific Island Countries are among the most vulnerable to natural hazards, particularly tropical cyclones, whose impacts are being intensified by climate change. These hazards continue to destroy homes, livelihoods, and essential infrastructure, with the greatest consequences borne by the most vulnerable. Fiji has long recognised the need to strengthen preparedness, reduce disaster losses, and build resilience. In this context, the Government of Fiji, through the National Disaster Risk Management Office (NDRMO), decided to pilot Anticipatory Action (AA) with support from the United Nations and humanitarian partners.

By using early warning systems and scientific advances in predicting disasters, AA maximises the window of opportunity between the moment of prediction and the arrival of a specific forecasted shock to trigger interventions that prevent or mitigate imminent humanitarian impacts. AA is defined as acting ahead of predicted hazards to prevent or reduce acute humanitarian impacts before they fully unfold. AA works best if triggers and decision-making rules (the model) and activities (the delivery) are pre-agreed to guarantee the fast release of pre-arranged financing (the money). In line with best practices for AA, this framework pre-agrees the tropical cyclone forecasting trigger and the activities which are launched thanks to pre-arranged financing. In addition, documenting evidence and learning is part of the framework.

NDRMO led the development of a Collective Anticipatory Action Framework for Tropical Cyclones, facilitated by the United Nations Office for the Coordination of Humanitarian Affairs (OCHA) and with the support of the Pacific Humanitarian Team (PHT). The Framework was designed as a government-led system to deliver early, pre-arranged assistance in the critical window between a credible cyclone forecast and landfall. The initiative was enabled by a pre-arranged allocation from the Central Emergency Response Fund (CERF) and co-financing from United Nations agencies, and is rooted in national systems and policies.

Following validation by the NDRMO, the Fiji Meteorological Service, the national cluster system, and relevant line ministries, the Framework was first endorsed by the United Nations Resident Coordinator for Fiji, Solomon Islands, Tonga, Tuvalu and Vanuatu in November 2023, and subsequently by the United Nations Emergency Relief Coordinator. It was then formally endorsed by the Cabinet of the Republic of Fiji in February 2024. This sequence of endorsements provided both international recognition and high-level national legitimacy, positioning Fiji as the first Pacific Island Country to adopt a nationally endorsed AA framework for tropical cyclones.

During the pilot phase (2023–2025), the Framework catalysed a shift from reactive response to proactive planning. It established a nationally owned trigger mechanism based on cyclone forecasts, developed sectoral Standard Operating Procedures (SOPs), introduced joint early warning messaging, and created harmonised financing arrangements. While no activation occurred, the Framework strengthened national coordination, enhanced operational readiness, and integrated anticipatory approaches into Fiji's disaster preparedness architecture.

Two learning exercises informed the next phase. An independent Process Learning conducted by the University of the South Pacific confirmed these achievements and highlighted the need



for stronger community sensitisation, broader sub-national engagement, diversified financing and more systematic readiness monitoring. Separately, a May 2025 Framework Revision Workshop—hosted by NDRMO with support from OCHA and the United Nations Agency for Disaster Risk Reduction (UNDRR) and attended by all stakeholders—translated lessons into practical adjustments to the framework: maintaining core activities; strengthening the trigger (e.g., incorporating rainfall and population data); adapting interventions (e.g., a voucher approach for selected health/protection actions); expanding community outreach; and aligning financing with disaster-risk financing strategies.

On this basis, the Government and partners agreed to extend the Framework into a second phase covering the 2025–2027 cyclone seasons. The revised Phase 2 Framework (2025–2027) reflects these findings and recommendations. It consolidates the achievements of the pilot phase while addressing identified gaps, ensuring that AA is further institutionalised, aligned with Fiji’s disaster risk management priorities and better integrated with community-based approaches. In line with best practices for AA, the Framework pre-defines the conditions under which it will be activated, the financing arrangements that will be triggered, and the pre-agreed activities to be implemented, while also including provisions to monitor and document its impact.



2. Policy Setting and Governance

2.1 Policy Setting

The Fiji Anticipatory Action Framework for Tropical Cyclones is anchored in the country's broader disaster risk management and climate policy environment. Fiji has a strong foundation of national legislation, strategies and institutional arrangements that provide the enabling environment for AA.

The National Disaster Risk Management Act 2024¹ provides the overarching legal framework for disaster governance in Fiji. It reaffirms national and sub-national disaster risk management structures, mandates government agencies to budget for preparedness and risk reduction, and creates a Disaster Risk Management Fund. Importantly, Section 61 of the Act requires the NDRMO, in liaison with relevant agencies, to establish and maintain a people-centred, multi-hazard warning system. This includes not only hazard monitoring, forecasting, and dissemination, but also *“systems and processes that enable early or timely action to reduce disaster risk”* and *“pre-agreed actions that may be taken to minimise impact of the hazard, in accordance with forecasted hazard impact.”* These provisions provide a clear legal foundation for AA in Fiji.

The Act also establishes the procedures for declaring a State of Disaster. A National State of Disaster may be declared by the Cabinet, on the advice of the National Disaster Risk Management Council, when a hazard is *“likely to cause or has caused”* significant impact. Divisional Commissioners and other delegated authorities may also declare divisional or local states of disaster. This formulation — *“likely to cause”* — is particularly important for AA, as it provides explicit legal backing for preparedness and early interventions before a hazard strikes.

In addition, Fiji's National Disaster Risk Reduction Policy (2018–2030)² and National Adaptation Plan (NAP)³ prioritise strengthening preparedness, early warning systems, and proactive responses to climate-related hazards. They identify tropical cyclones as a major climate hazard that the country is facing and will continue to face in the future. The NAP outlines several measures that Fiji can take to address the risks posed by tropical cyclones, including the building of community resilience, as well as strengthening of early warning systems and disaster response preparedness. The midterm review of the Sendai Framework for Disaster Risk Reduction⁴ further identified the need to expand early warning and anticipatory approaches.

¹ *National Disaster Risk Management Act 2024*, Republic of Fiji. <https://www.ndmo.gov.fj/wp-content/uploads/2024/12/NDRM-Act-2024.pdf>

² *Fiji National Disaster Risk Reduction Policy 2018–2030*, Republic of Fiji, available at: <https://www.preventionweb.net/publication/fiji-national-disaster-risk-reduction-policy-2018-2030>

³ *Republic of Fiji National Adaptation Plan: A pathway towards climate resilience 2018–2030*, Ministry of Economy, available at: https://www4.unfccc.int/sites/NAPC/Documents/Parties/NAP_Fiji.pdf.

⁴ *Fiji Sendai Mid-Term Review Report 2023*, NDRMO, available at: <https://ndmo.gov.fj/wp-content/uploads/2023/05/Fiji-Sendai-Mid-Term-Review-Report-2023.pdf>



At the community level, the Community-Based Disaster Risk Management (CBDRM) Policy⁵ provides an entry point for embedding AA in local preparedness systems. The policy mentions AA and forecast based financing as a key approach under *Risk-Informed Development and Finance*, encouraging the development of triggers and pre-agreed plans to activate funding and preparedness before disasters strike. AA is also being integrated into the annual National Disaster Awareness Week and other public sensitisation initiatives, reinforcing its role as part of national preparedness.

In alignment with these institutional and policy arrangements, the Government of Fiji, through the Ministry of Finance and with support from partners, is currently developing a National Disaster Risk Financing (DRF) Strategy, which remains under consultation. The strategy aims to strengthen Fiji's financial resilience to disasters by establishing an integrated framework for mobilising and managing pre-arranged and contingent financing instruments. It seeks to ensure timely and predictable access to funds before and after disasters, reducing fiscal shocks and enabling faster recovery. The DRF Strategy builds on existing instruments such as the Pacific Catastrophe Risk Insurance Company (PCRIC) parametric insurance,⁶ the World Bank's Catastrophe Deferred Drawdown Option (CAT-DDO),⁷ and the Contingency Emergency Response Components (CERCs)⁸ embedded within sectoral projects. It also considers the potential for integrating micro- and meso-level instruments, including adaptive social protection and parametric insurance for households, MSMEs, and the agriculture sector under the Pacific Insurance and Climate Adaptation Programme (PICAP).⁹

Once finalised, the DRF Strategy will provide a comprehensive policy framework to guide the layering of financial instruments across sovereign, private, and community levels, complementing existing risk reduction and preparedness investments. Importantly, it will offer a critical policy entry point for embedding anticipatory financing mechanisms within national disaster risk management and climate adaptation systems—enabling pre-arranged funding to be released based on early warning information. By aligning with the Anticipatory Action Framework and broader climate and fiscal policies, the DRF Strategy will help ensure that Fiji's disaster response is not only faster but also more risk-informed, sustainable, and financially secure.

Anchoring on the Sendai Gender Action Plan (GAP), which aims to integrate gender-responsive approaches to decrease gender-related disaster risk by 2030, a policy brief has been developed

⁵ The CBDRM Policy is currently under revision.

⁶ The Pacific Catastrophe Risk Insurance Company (PCRIC) is a regional risk-pooling facility that provides sovereign parametric insurance products to Pacific Island Countries. Its Tropical Cyclone and Excess Rainfall policies provide rapid, pre-arranged payouts based on modelled windspeed or rainfall intensity once pre-defined thresholds are met, enabling governments to access immediate liquidity following severe weather events. For more information, see <https://pcric.org/tropical-cyclone/> and <https://pcric.org/excess-rainfall/>

⁷ <https://documents.worldbank.org/en/publication/documents-reports/documentdetail/099053024122674516>

⁸ <https://openknowledge.fao.org/bitstreams/4fc526cb-0454-48fa-b9e8-48098eda8910/download>

⁹ <https://www.uncdf.org/pacific-insurance-and-climate-adaptation-programme>



to assist Pacific Islands Countries and Territories (PICTs) and provide evidence-based recommendations on how to integrate and strengthen interventions on sexual and reproductive health (SRH) and gender-based violence (GBV) into Disaster Risk Reduction (DRR), AA and climate change policies (Annex 1). This is to ensure that people, especially women and girls have access to essential lifesaving health services during and after a disaster. Gaps regarding SRH and GBV can hinder effective planning and coordination across Government Ministries and clusters of fragments of the response. Strengthening Government leadership, cross-sector coordination and prioritization of SRH and GBV, in partnership with communities, particularly women and youth – led organizations, is essential to building inclusive, resilient systems. This policy brief provides practical, evidence-based recommendations to bridge these gaps governance by focusing on 4 key areas; 1) Institutionalize SRH and GBV within DRR, climate and AA policies and protocols, 2) Strengthen inclusivity through community leadership and localisation 3) Expand flexible, gender responsive financing for DRR.

Finally, the national cluster system, officially recognised under government leadership, brings together the work of humanitarian actors under the stewardship of relevant line ministries, forms the backbone of humanitarian response in Fiji and provides a natural institutional home for AA planning and coordination.

Together, these policies and commitments establish a strong enabling environment for AA, ensuring that the revised Framework is fully aligned with Fiji's legal and policy mandates in disaster risk management, climate adaptation, and humanitarian response.

2.2 Governance of the Framework

The governance of the Anticipatory Action Framework for Tropical Cyclones is rooted in Fiji's disaster management system and anchored in the National Disaster Risk Management Act 2024. The Act mandates the National Disaster Risk Management Office (NDRMO) as the coordinating authority, under the oversight of the National Disaster Risk Management Council and with ultimate political authority resting with the Cabinet of the Republic of Fiji.

The Framework was developed under NDRMO leadership, with triggers designed in collaboration with the Fiji Meteorological Service (FMS), and anticipatory activities elaborated by the line ministries which lead the national clusters together with the PHT and its dedicated Anticipatory Action Technical Working Group (PHT AA TWG). All activities under the Framework, implemented both by line ministries and humanitarian partners, were validated by the NDRMO and the respective line ministries, ensuring national ownership and high-level oversight. A full list of stakeholders engaged in the Framework's design and validation is provided in Annex 2.

A central pillar of governance is the national cluster system, which provides the operational platform through which anticipatory actions are coordinated and delivered. Each AA activity is channelled through the relevant government-led cluster. Members of the PHT support these clusters with technical expertise, operational capacity and additional resources. This governance arrangement ensures that pre-agreed interventions are embedded in existing




preparedness and response arrangements, that accountability runs through the cluster system, and that there is a seamless transition from AA to humanitarian response when needed.

At the divisional and sub-national levels, governance is exercised through structures established under the NDRM Act 2024. Divisional Commissioners play a central role in coordination, readiness monitoring and communication, working closely with Provincial Administrators, District Officers and community committees. Divisional Disaster Risk Management Committees, together with Provincial and District Disaster Committees, provide formal mechanisms to ensure that AA decisions are communicated, adapted and implemented locally. At the community level, Community-based Disaster Risk Management Committees, alongside faith-based and civil society organizations, play a critical role in last-mile dissemination, community sensitization and feedback. This depicts that this framework favours a decentralised approach with participatory humanitarianism.

This layered governance approach, with the cluster system providing horizontal coordination across sectors, and the divisional and provincial structures ensuring vertical integration from the national to the community level — ensures that AA is nationally led, legally grounded, and implemented in partnership with all relevant stakeholders.



National Disaster Management Structure

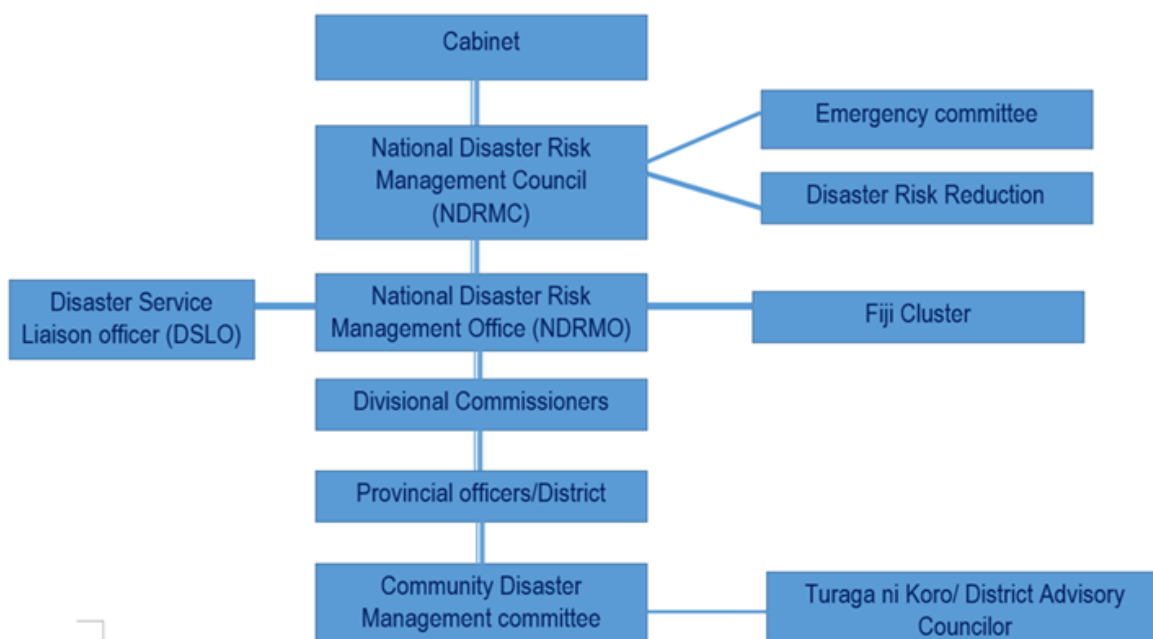


FIJI

Humanitarian Coordination Structure

As of 03 September 2025

The Humanitarian Coordination Structure in Fiji comprises of three levels: at the strategic level, the National Disaster Management Council chaired by the Minister for Rural and Maritime Development & Disaster Management (MRMDDM), at the coordination level, are three sub-committees; Mitigation & Prevention, Preparedness and Emergency committees chaired by the Permanent Secretary for MRMDDM - who is also the Disaster Controller. At the operational level, the National Emergency Operations Centre (NEOC) is managed by the National Disaster Management Office (NDMO). The legislative framework for the coordination of humanitarian affairs (preparedness, response, early recovery) is the National Disaster Risk Management Act 2024. The national cluster system is based on the global cluster system which was introduced in 2005 during a major reform of the humanitarian coordination, known as the Humanitarian Reform Agenda, to enhance predictability, accountability and partnership. National clusters are led by relevant ministries or government departments and in few cases co-led by international organizations. The national clusters are being supported by the Pacific Humanitarian Team's regional clusters.

National Coordination Structure

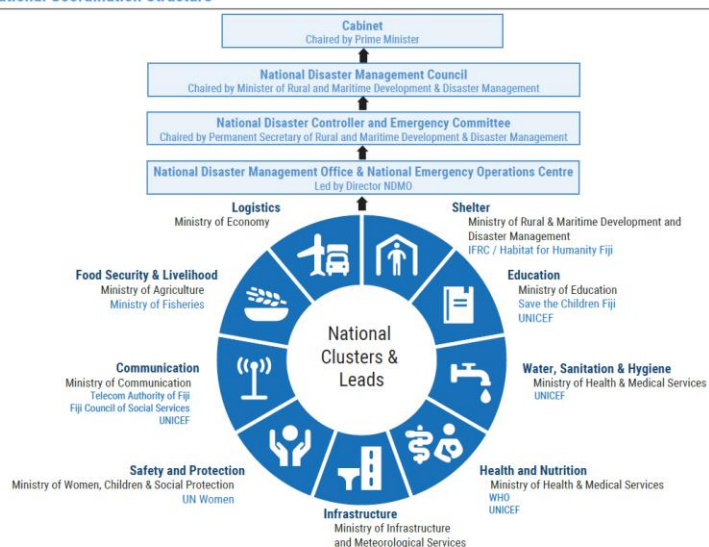

Location Map



The boundaries and names shown and the designations used on this map do not imply official endorsement or acceptance by the United Nations. Creation date: 03/09/2025 Sources: Government of Fiji OCHA/ReliefWeb Feedback: ocha@pacif@un.org www.unocha.org www.reliefwf.org

■ National Cluster
■ National Lead Ministry
■ Cluster Co-lead



3 Other Anticipatory Action Initiatives in Fiji

In parallel to the Collective Anticipatory Action Framework for Tropical Cyclones, other initiatives are advancing anticipatory approaches in Fiji through complementary models and financing mechanisms.

3.1 Meso-Level Anticipatory Insurance Scheme

An innovative meso-level anticipatory insurance scheme was piloted under the Pacific Insurance and Climate Adaptation Programme (PICAP), jointly implemented by the United Nations Capital Development Fund (UNCDF) as the convening agency, the United Nations Development Programme (UNDP) as the administrative agency and the United Nations University Institute for Environment and Human Security (UNU-EHS) as the technical agency, with technical and funding support from the UNDRR.¹⁰

The scheme links pre-arranged insurance payouts to early-warning triggers derived from forecasted tropical cyclone windspeeds, allowing community cooperatives to access funds 24–48 hours before an expected event. The anticipatory component releases between 10 and 20 percent of the insured sum once pre-defined thresholds are met, followed by post-event payouts of up to 80 percent based on verified windspeed data.

Launched in 2023 by Sun Insurance Company Limited with approval from the Reserve Bank of Fiji, the pilot initially covered four cooperatives — the Cane Farmers' Cooperative Savings & Loans Association, Fiji Rice Limited, the Sugarcane Growers Council and the Tailevu Dairy Farmers Cooperative Association — representing more than 10,000 members. The policyholders receive guidance on the use of payouts based on community consultations and focus group discussions conducted with UNDRR and PICAP. Following strong interest and no trigger activation in 2023–2024, the pilot has been extended into 2024–2025 and expanded to twelve communities nationwide.

The anticipatory insurance model provides a private-sector-led pre-financing solution that complements the government-led anticipatory action framework. It reduces the financial burden on government and humanitarian actors by shifting part of the disaster-risk cost to the insurance sector while enabling communities to act early. This approach represents one of the first global examples of anticipatory insurance at the meso-level targeting sudden onset events and aligning with Fiji's ambition to integrate pre-arranged, risk-informed financing across its national disaster risk management and resilience agenda.

PICAP and UNDRR are now exploring opportunities to scale the scheme to other communities in Fiji and across the Pacific, while ensuring coherence with government policies on disaster risk financing and anticipatory action.

¹⁰ <https://www.uncdf.org/article/8428/pacifics-first-anticipatory-action-pilot-insurance-scheme-to-provide-fijian-farming-groups-with-funds-to-better-prepare-for-cyclones>



4 The Risk/Hazard

Fiji is one of the most vulnerable countries in the world to tropical cyclones with significant impact on infrastructure, the economy, and the Fijian people, displacing thousands, creating humanitarian suffering, and causing loss of life. Beyond destructive wind speeds, tropical cyclones in Fiji are often accompanied by intense rainfall, resulting in flash floods, riverine flooding, and storm surges that further exacerbate the country's exposure and vulnerability.

Since 1969, there have been 33 tropical cyclones (TCs) (Category 1 or higher) that have passed within 10 km of Fiji, and 16 that made landfall. Some of the most devastating cyclones to hit Fiji in recent history include Cyclone Winston (2016), the strongest cyclone ever recorded in the Southern Hemisphere, Cyclone Yasa (2020) which was the second-strongest cyclone on record to make landfall in Fiji, and Cyclone Harold (2020). For these three most recent storms, international support was mobilized, including financial support from the Central Emergency Response Fund (CERF). Cyclones can also cause significant damage from rainfall while having relatively low wind speed. For example, Cyclone Cody (2022) affected around 70,000 people in Fiji while only being a Category 1 cyclone. Its heavy rains (over 200 mm, averaged over the whole country) caused significant flooding.

Climate change leading to warmer oceans is having a significant impact on tropical cyclones, making them more frequent, intense, and destructive. In addition, climate change is also expected to lead to stronger storm surges, more extreme rainfall events, and rising sea levels. Fiji's government estimates (NDC) that by 2050, over 6.5 per cent of Fiji's GDP could be lost due to tropical cyclones and floods, with the number of people being pushed into poverty every year increasing by 25 per cent. While the Government of Fiji has made significant investments in disaster preparedness and resilience, the country remains at high risk from the loss and damage caused by tropical cyclones.



5 The Model: Forecasts, Triggers, and Activation Protocol

5.1 The Model/Forecast

Cyclone Track Forecast

World Meteorological Organization's Tropical Cyclone Programme, the Regional Specialized Meteorological Centre (RSMC) in Nadi has the responsibility for detecting and forecasting tropical cyclones (TCs) in its zone of responsibility, which is from the equator to latitude 25°S and from longitude 160°E to 120°W (spanning the international date line)¹¹. As such, RSMC Nadi's TC forecasts are the internationally recognized authoritative source for TCs in this zone. RSMC Nadi is operated by Fiji Meteorological Services (FMS).

RSMC Nadi issues official TC track forecasts with a 72-hour lead time, which include the TC's forecasted category and position, as well as 5-day TC formation risk outlooks. This framework uses the official 72-hour track forecast for its action trigger. To provide more advance warning for implementation, this framework also includes a readiness trigger, which is based on RSMC Nadi's unofficial 120-hour forecast (an additional 48 hours)¹².

Observed rainfall

The NASA IMERG dataset is the lowest-latency publicly available global rainfall dataset. It offers daily rainfall at a 0.1-degree resolution at "early", "late", and "final" times, each corresponding to an increasing latency and accuracy. For the purposes of an observational trigger, the "late" option was selected as a balance between latency and accuracy, which is issued roughly half a day after the rainfall has occurred.

5.2 Trigger Conditions

This framework will be triggered by a tropical system¹³ that either:

- is forecasted by RSMC Nadi to cause winds of at least 64 knots¹⁴ in zones where at least 5,000 people live¹⁵, **OR**

¹¹ <https://community.wmo.int/en/tropical-cyclone-regional-bodies>

¹² Due to the relative uncertainty of the additional 48 hours of forecast, this part of the forecast is used only to determine whether the readiness trigger has been met.

¹³ This includes tropical depressions, tropical storms, and tropical cyclones.

¹⁴ Sometimes referred to as "hurricane-strength" winds. Note that 64 knots (118 km/h) is the minimum value for a tropical cyclone to be a Category 3 on the Australian scale (used by RSMC Nadi) <https://www.bom.gov.au/resources/learn-and-explore/tropical-cyclone-knowledge-centre/tropical-cyclone-categories>

¹⁵ Based on the WorldPop 2020 1km UN-adjusted population distribution <https://hub.worldpop.org/geodata/summary?id=46199>



- is observed to cause¹⁶ at least 190 mm of rainfall¹⁷ over two consecutive days, averaged over the whole country.

Every time RSMC Nadi produces a tropical cyclone track forecast, it will be evaluated by an automated script to determine whether the trigger conditions have been met.

The framework follows a 3-stage trigger activation, each part of which is triggered based on the lead time of the points in the forecast, or the observational data:

- **Readiness trigger:** If the wind field indicated by the 120-hour forecast meets the trigger conditions, the readiness trigger is activated.
- **Action trigger:** If the wind field indicated by the forecast truncated up to a lead time of 72 hours meets the trigger conditions, the action trigger is activated.
- **Observational trigger:** If the average rainfall over the whole country during two consecutive days meets the threshold (190 mm), the observational trigger is activated.

By definition, the action trigger has a detection/confirmation rate of 100% (*i.e.*, any cyclone whose actual track meets the trigger conditions will cause the framework to activate). This is because the actual track of the cyclone is effectively included in the forecast, as the forecasted position at a lead time of 0 hours.

The historical performance statistics of the trigger are shown in the table below.

Trigger Mechanism Statistics			
Stats by trigger			<i>Analysis seasons: 2001-2024</i>
<i>Trigger</i>	<i>Return period</i>	<i>Activation probability</i>	<i>Storms activated</i>
Readiness	3.6 years	28%	Yasa 2021, Harold 2020, Keni 2018, Winston 2016, Evan 2013, Tomas 2010, Ami 2003
Action	3.6 years	28%	<i>same as Readiness above</i>
Observational	6.2 years	16%	Coy 2022, Ana 2021, Yasa 2021, Sarai 2020, Winston 2016
Overall stats			
<i>Overall return period</i>		3.1 years	<i>Average period for total budget spend / Effective return period</i> 3.1 years
<i>Overall probability of activation</i>		32%	<i>Probability of total budget spend</i> 32%
<i>Average total CERF spending per year with activation</i>		\$2.4M	<i>Average total CERF spending per year</i> \$0.8M

¹⁶ The cyclone is deemed to "cause" rainfall if the rainfall occurs while the centre of the storm is observed by RSMC Nadi to be within 250 km of Fiji, plus one day on either side (resulting in a minimum span of three days).

¹⁷ Based on the IMERG v07b Late satellite precipitation measurement
https://gpm1.gesdisc.eosdis.nasa.gov/data/GPM_L3/GPM_3IMERGDL.07/



5.3 Trigger Monitoring Process

While this Framework remains valid for a two-year period (2025–2027), activation may only occur between 1 October and 31 May each year, corresponding to Fiji’s official tropical cyclone (1 November to 30 April) season extended by one month on each end, during which the triggers are actively monitored.

Readiness and Action Triggers

Every tropical cyclone track forecast produced by RSMC Nadi is evaluated to determine whether the trigger conditions have been met. The process involves the following steps:

1. A 120-hour forecast is produced by the Fiji Meteorological Services Senior Scientific Officer on duty on the Tropical Cyclone Forecasting Bench.
2. The Officer emails the forecast, in its standardized CSV export format from the TC Module software to the Data Science team at the OCHA Centre for Humanitarian Data.¹⁸
3. An automated script¹⁹ evaluates whether the trigger conditions have been met for either the readiness trigger or the activation trigger.
4. The automated script sends an email to the Distribution List defined in Annex 4 to notify that the trigger has been met.

As a backup to the above steps, the Data Science team email will also be included on emails of the 72-hour official forecast from RSMC Nadi to the NDRMO, which happen after the 120-hour has been truncated to 72 hours (an already existing activity, undertaken for the NDRMO to produce impact forecasts).


This process is outlined in the figure below.

¹⁸ data.science@humdata.org

¹⁹ All code used for analysis in this framework is available publicly at <https://github.com/OCHA-DAP/pa-aa-fji-storms>



Times are estimates based on TC bench schedule, for satellite information published at 06:00

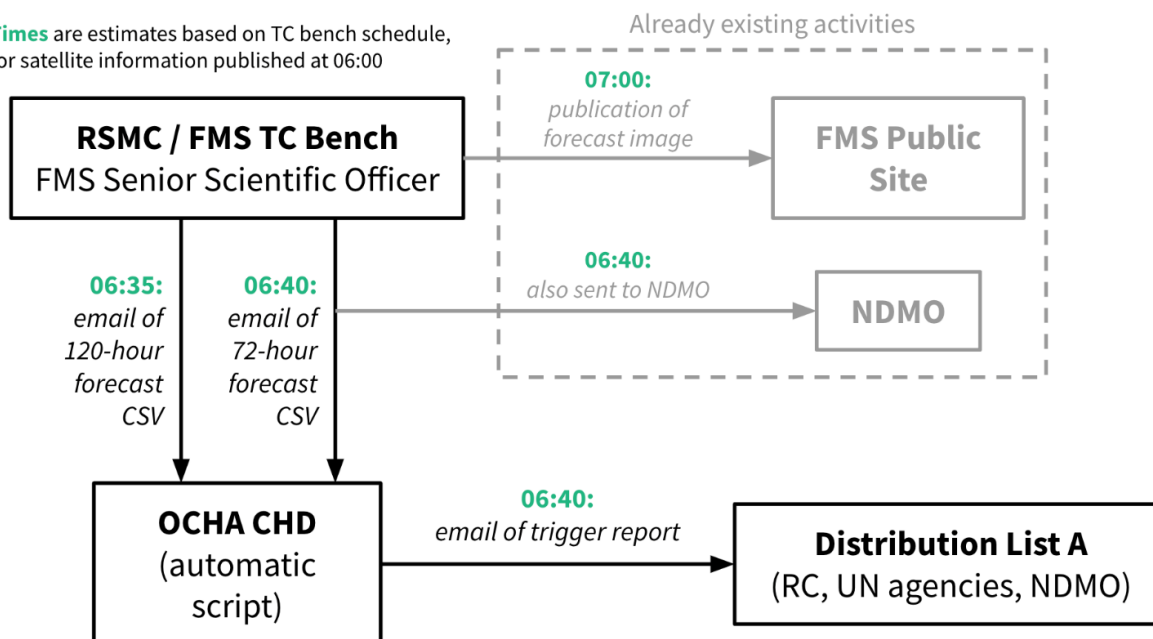

Observational Trigger

Every day, an automated OCHA CHD script reads the IMERG data from the NASA server and determines whether the trigger conditions have been met. If the trigger conditions are met, an email will be automatically sent to Distribution List A, as above.

5.4 Activation Protocol

The activation protocol outlines how the Framework is automatically activated once the trigger conditions are met. Activation means that the anticipatory activities detailed in Section 6 can be carried out at readiness and activation triggers as defined by the plan, and that pre-arranged financing becomes available as outlined in Section 7.


Stakeholders are notified about the trigger conditions being met via an automated email produced by OCHA. To support geographic prioritisation, OCHA will produce an information email on the cyclone track (email sample in Annex 6).

Any triggering of the framework should lead to action. However, for theoretically possible outlier cases where a track of a storm clearly would result in minimal impact, the Resident Coordinator, in consultation with the government, may pause any activation.

Who	What	How	When
RSMC Nadi / Fiji Meteorological Services	Send 120-hour forecast to OCHA Centre for Humanitarian Data	Email of CSV to data.science@humdata.org	As soon as forecast is produced, and before forecast is truncated to 72 hours
OCHA Centre for Humanitarian Data	Evaluate whether trigger has been met, and send email to distribution list A (official trigger email) and B (complementary trigger information email)	Using automated script	Automatically as soon as forecast CSV is received from RSMC Nadi
CERF	When a readiness trigger is issued (or an action trigger without a previous readiness trigger), CERF will immediately	Endorsed framework and CERF application by RC and Emergency Relief Coordinator (ERC)	As triggers are reached



Implementing Partners (UN agencies, NGOs, Red Cross, etc.)	send the approval letters to the agencies Upon activation and receipt of the approval letters, implementing partners will proceed to implement readiness and/or action activities.	Pre-approved CERF approval letters to UN agencies As described in the agency-specific project proposals and implementing SoPs.	As triggers are reached
Fiji Red Cross Society	When the activation trigger is reached, pre-approved funds from the IFRC Disaster Response Emergency Fund (DREF) will be transferred to FRCS from IFRC Suva for agreed early actions. The FRCS can pause the activation process upon discussion with the NDRMO	Direct contact/Liaison between RC and NDRMO followed by email notification to distribution list A (Annex 4)	Once the framework is activated, in the possible outlier cases where a track of a storm clearly would result in minimal impact.
NDRMO	The NDRMO can discuss with the RC if it is the case to pause the activation	Direct contact between RC and NDRMO (it can be facilitated by OCHA HoO) followed by email notification to distribution list A (Annex 4)	Once the framework is activated, in the possible outlier cases where a track of a storm clearly would result in minimal impact.

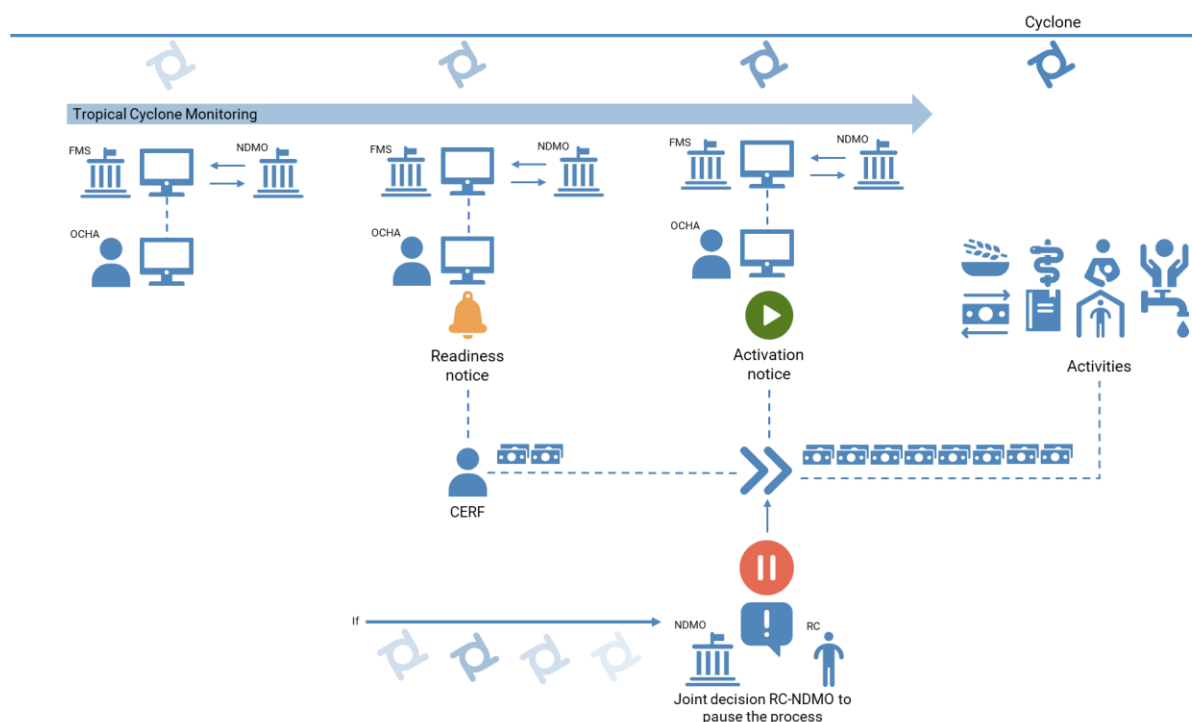



6 The Activities: Anticipatory Activities and Operational Plan

6.1 Overview

Tropical cyclones and rainfall have a profound, devastating impact on communities in Fiji experiencing greatest vulnerability. These populations, often living in precarious housing and lacking essential resources, bear the brunt of disasters. While they possess the knowledge and skills to mitigate the impacts of cyclones, they often lack the necessary materials and resources to effectively reduce their vulnerability to them.

There is only a very short window of opportunity between a trigger and the impact of tropical cyclones in Fiji. In addition, some areas are remote and difficult to access, especially with impending storms. This combination may create challenges to carry out AA in full before the impact of the cyclone. This is why the partners have resolved to act as fast as possible and as anticipatory as possible once a trigger is reached. However, in some circumstances, especially for remote areas, assistance may only reach communities after the cyclone has passed, turning ex- ante anticipatory action into ex-post early action.

6.2 Anticipatory Activities Selection Criteria

Anticipatory actions aim to mitigate the impacts of out-of-the-ordinary tropical cyclones and heavy rainfall by targeting those people who face the greatest vulnerability. The following criteria were applied to select the pre-agreed activities:

1. Anticipatory character: Is the action effective in preventing or reducing the humanitarian impact of the shock?
2. Ability to deliver within the window of opportunity: Is it possible to carry out the action effectively with the available forecast lead time, i.e. in the window of opportunity?
3. Operational capacity: Do the agency and its IPs have the institutional capacity (thematic, logistic, administrative, financial, human resources) to implement the action effectively given the lead time and scale?
4. No regrets approach: In the case of a false alarm, will the proposed actions benefit rather than negatively affecting the targeted population?

6.3 Cluster-led Anticipatory Activities

Cluster-led anticipatory activities represent the operational core of the Framework. Each activity has been identified and validated by the government-led national clusters in collaboration with the relevant UN agencies and partners. The actions are designed to address priority humanitarian needs that can be mitigated ahead of impact and are implemented through existing coordination structures under the leadership of the respective line ministries. The activities are delivered through different projects under the Framework and financed through multiple pre-arranged channels, as outlined in Section 7 on financing.

A detailed summary of activities by project is provided in Annex 7.



Protection

Activity 1: Multi-Purpose Cash Assistance to existing recipients of social support schemes identified by the Government

Leads: Ministry of Women, Children and Social Protection (MWCSP) and World Food Programme (WFP)

Partners: MWCSP, World Food Programme, Ministry of Finance. The tripartite MoU between MoF, MWCSP and WFP describing the collaboration can be found in Annex 8.

Objective: Mitigate the impact of the cyclones on household food and nutrition security and general wellbeing of their families.

Description: Given the short lead time, unconditional multi-purpose cash transfer (MPC) is a major component of the framework. WFP, in partnership with the MWCSP, will support a projected 15,000 households (75,000 people) with anticipatory cash transfers in areas identified to be in the tropical cyclone's path at the time of the activation trigger. A transfer value of FJD200 endorsed by the Fiji cash working group will be transferred by the DSP to targeted households. In the absence of a minimum expenditure basket, transfer value determination was based on the default transfer value and aligned to Fiji basic needs poverty line.

WFP will channel resources through the government for provision of cash assistance to the existing recipients of social support schemes identified by the Government under four parts of the national social protection scheme namely: 1) the Family Assistance Scheme, 2) the Care and Protection Allowance, 3) the Disability Allowance and 4) the Social Pension Scheme. This MPC is designed to enable targeted households to prepare for the cyclone (evacuation costs, protecting livestock and homes etc.), buy essential needs (food, medicines etc.) and mitigate the impact of the cyclones on household food and nutrition security and general wellbeing of their families. WFP will collaborate with government and UN agencies in the development of early warning messages under the leadership of NDRMO and support the Department of Social Protection (DSP) to disseminate early warning messages including cash assistance messages to the final list of targeted households. The DSP will engage field-based staff to support community sensitization about the tropical cyclone and potential for assistance before impact. Messages about the assistance will be designed and delivered in such a way that they do not raise expectations for cash transfers in areas not affected by the tropical cyclone.

Challenges and potential improvements in the future:

Sudden onset disasters, such as tropical cyclones, affect everyone in their path, whereas the use of a social registry for targeting restricts anticipatory support, such as multipurpose cash, to households in the social protection beneficiary registry. In addition, while the use of the national social protection beneficiary registry contributes to the strategic objective of strengthening government systems, there is limited oversight over inclusion and exclusion errors when a disaster occurs. As a mitigating measure, regular deduplication, graduation, and retargeting to include households below the poverty line can increase the likelihood that the most vulnerable individuals will be included on the beneficiary list. While the above is a medium



to long-term solution, there is a clear need for early action plans, particularly when using the government beneficiary registry. The early actions can be activated promptly after the disaster has passed to support and prioritize those who were affected but not targeted through government beneficiary registry (horizontal expansion). The AA pilot is an opportunity to showcase how existing government policies and legislative frameworks for financing disaster risk management, social protection, and climate change adaptation can reduce impact of climate disaster through anticipatory actions. This strategy ensures that AA interventions are localized, owned by the government and hence sustainable and cost-effective.

Activity 2: Distribution of Pacific customized Dignity Kits for GBV risk mitigation

Leads: MWCSP and United Nations Population Fund (UNFPA)

Partners: MWCSP and Fiji Disabled Peoples Federation

Objective: To ensure women, girls, and persons with disabilities receive essential hygiene and menstrual health supplies through timely anticipatory actions that are pre-positioned and distribute kits before disasters, reducing GBV risks and promoting safety, dignity, and protection during emergencies.

Description: Partnering closely with MWCSP, UNFPA will provide essential dignity kits for GBV risk mitigation and dignity of women and girls in forecasted cyclone impact areas. UNFPA's intervention has a strategic emphasis on minimizing life-threatening risks associated with GBV. These efforts encompass the distribution of Pacific customized kits, complemented by informational messages stressing the importance of seeking timely support and care from trained healthcare professionals and service providers. These kits comprise of the following: Dignity Kits for women aged 15-49, including those with disabilities and menstrual health kits for girls ages 10 and above. The comprehensive strategy aims to safeguard the health and wellbeing of women and girls in the face of impending tropical cyclones, addressing their unique needs and vulnerabilities.

Challenges & Potential Improvement in the future

- **Limited prepositioning capacity:** Current storage and logistical arrangements may not be sufficient to ensure timely distribution to all high-risk areas before disaster onset. Future efforts to expand warehouse capacity and improve last-mile delivery systems in coordination with local government and CSO networks.
- **Targeting and data gaps:** Limited sex, age, and disability-disaggregated data can affect accurate targeting of women and girls most at risk. Strengthening data collection systems and community-based mapping will improve equitable coverage.
- **Monitoring and feedback:** Limited real-time monitoring and feedback mechanisms hinder adaptive improvements. Establishing simple, confidential feedback channels—especially for women and persons with disabilities—will help ensure kits meet user needs and protection standards.

Lead: MWCSP and UN Women



Partners: Department of Women & Department of Child Services and Social Protection, and Fiji Safety and Protection Cluster Members.

Objective: To ensure safety and protection concerns are assessed and appropriately factored into post needs assessments and responses of the different key sectors.

Description: From the alert or trigger phase, social welfare officers and women's interest officers in the rural and maritime areas, as part of their preparedness activities to respond, are usually already moving through location where their services are based to check on the facilities, the services it's meant to provide in safety and protection. During the past year, the cluster had also revised their rapid assessment form to be deployed on Kobo. A series of workshops has been held in the various divisions over the past year to finalize the form. During the readiness phase, the officers will be refreshed on the use of the form on Kobo and how to collect protection data. This will be facilitated online whilst in their various rural locations.

Challenges and potential improvements in the future:

- The designation of staff (usually public servants) that would support protection assessments will only be determined at the time of the looming emergency. In future, the ministry, as part of their preparedness could already obtain a list of individual staff that would be on call and able to deploy for assessments as soon as restriction to movements has been lifted.
- Virtual training will only depend on the strength of the network in the divisions and the available devices which assessors will use for accessing Kobo and collecting data. In future, a series of data collection devices could be acquired and issued out on receipt of a warning (as an asset of the organization) so that there won't be any issues in accessing the kobo form. Data credit can also be pushed out to the sim card on the devices to ensure connectivity during the refresher trainings.

Health

Activity 4: Health and Nutrition Cluster Coordination

Leads: Ministry of Health and Medical Services (MHMS) and World Health Organisation (WHO)

Partners: Fiji MHMS, Fiji Health and Nutrition Cluster, Adventist Development and Relief Agency (ADRA), Empower Pacific, International Federation of the Red Cross (IFRC), International Planned Parenthood Federation (IPPF), The Pacific Community (SPC), Save the Children, United Nations Population Fund (UNFPA), United Nations Children's Fund (UNICEF), World Health Organization (WHO).

Objective: To work in support of the MHMS and other national authorities to improve the health and nutrition outcomes of affected populations through timely, predictable, appropriate and effective coordination of health and nutrition action in emergencies.

Description:

- Support Fiji's Health and Nutrition Cluster in coordinating national-level preparedness, emergency response and recovery efforts, as requested/directed by MOH leadership.



- Support Fiji's Health and Nutrition Cluster with assessments, preparedness and service delivery in emergencies through the provision of technical support, operational support (i.e. implementation), and in-kind support, as requested/directed by MOH leadership.
- Support Fiji's Health and Nutrition Cluster to identify core advocacy concerns, including resource requirements, and contribute key messages to advocacy outlets.

Challenges and potential improvements in the future: A resilient health system must include the ability to both maintain the provision of basic health care and respond to health system shocks. A strong and equitable health system is resilient in the face of potential threats, including but not limited to the climate crisis, public health emergencies and disasters. The ongoing work of health and nutrition cluster partners to build a resilient health system will support Fiji throughout the preparedness, anticipatory action, response and recovery phases.

Activity 5: Health promotion

Lead: FRCS and MHMS

Description: In coordination with the MHMS, Fiji Red Cross will disseminate tailored health alerts and prevention messages, focused on relevant water and vector borne diseases, including LTDD. These timely messages will reinforce programming being undertaken by the Fiji Red Cross health team (funded through other sources) to strengthen epidemic and pandemic preparedness and prevention across Fiji. A minimum of 400HHs will be reached through these health promotion messages.

Activity 6: Multi-Purpose, Unconditional Cash Assistance for Term High Risk pregnant women identified by the Ministry of Health and Medical Services

Leads: MHMS and United Nations Population Fund (UNFPA)

Partners: MHMS, Medical Services Pacific, Reproductive and Family Health Association of Fiji.

Objective: To safeguard the health and dignity, of pregnant women and girls in cyclone-prone areas through anticipatory actions that ensure timely access to life-saving maternal and reproductive health services before, during, and immediately after disasters.

Description: UNFPA in partnership with MHMS will support a projected 1500 households (750 high risk term pregnant women) with multipurpose unconditional anticipatory cash in time of activation trigger to support access to lifesaving safe delivery and essential newborn care.

The transfer value of approximately FJD 224 (UN USD-FJD exchange rate: 2.24) has been informed by MHMS after three divisional consultations with health workers including those based in rural remote locations. The value has been decided based on the cost of transportation in health emergencies from the community to sub- divisional level health facility for life saving health services.

UNFPA had multi stakeholder consultation with financial service providers to ensure timely delivery of cash and is working on finalizing an agreement with the Vodafone Fiji and Digicel to ensure timely delivery of the cash during anticipatory action.



Beneficiary data will be profiled and shared by MHMS by sub-division which will be then put on common beneficiary data platform with access to UNFPA and financial service providers. For risk mitigation, two accesses will be provided to UNFPA, one for the unloader and one for the approval before the cash is disbursed. Data protection measures have been put in place by the mobiles service provider, and the beneficiary will have to be the primary recipient registered on these planforms. UNFPA is working on designing one pager messages for the beneficiary to advocate for the intended use of cash and not to raise expectations.

Challenges and potential improvements in the future:

Reaching women & girls who live in the remote rural setting where access to mobile network coverage is limited and beneficiary most in need for this assistance can be a challenge therefore UNFPA is expecting to learn from this pilot and look at ways to extend access to assistance in the non- coverage areas in future frameworks.

Timely Data sharing can be challenge due to women booking late for antenatal care and losing out on the much-needed assistance however a cut date had to be determined for beneficiary to be profiled and entered in the system. However, UNFPA is working with MHMS financial service providers to ensure a more flexible to ensure more beneficiaries can be profiled and entered into the system to accommodate late bookers.

Water, Sanitation and Hygiene (WASH)

Activity 7: Distribution of WASH Kits

Leads: MHMS and UNICEF

Partners: MHMS, Ministry of Education and Human Resource Development, WASH Cluster CSO partners (Contingency partnerships in progress).

Objective: Mitigate the impact of the cyclones on access to water and sanitation services and ensuring effective hygiene practices.

Description: UNICEF will work with the MHMS to improve and maintain access to Water, Sanitation, and Hygiene (WASH), through the following activities:

- Coordinate the WASH cluster response with technical advice, such as assessments, (inter-)cluster coordination, information management (4Ws) and reporting.
- Prepositioning of WASH related non-food items at likely impacted evacuation centres and key public infrastructures (hygiene kits, water containers, menstrual hygiene management supplies).
- Support coordination and innovation management across government led WASH, cluster.
- Targeted support at evacuation centres to ensure WASH response is gender and disability sensitive.
- UNICEF will monitor and evaluate the implementation of the project to measure the impact of anticipatory action in cooperation with the Government counterparts.



Challenges and potential improvements in the future:

Much work needs to be done to improve preparedness in Fiji including training for cluster coordinators and information managers, onboarding of contingency partnerships for rapid response, increasing number of long-term agreements with contractors to deliver local supplies, review and strengthen local long-term agreements with Non-Food Items (NFIs) suppliers. These are all ongoing actions but as cyclone season arrives are still in progress to develop and may not fully be in place if there is an early activation. Contingency partnerships with local NGOs are being considered as an alternative option to overcome some of these challenges.

Activity 8: Distribution of Jerry Cans and Soap

Laed: Fiji Red Cross Society

Objective: To mitigate the hygiene-related and waterborne disease outbreaks resulting from water source contamination because of TCs and associated extensive flooding.

Description: Fiji Red Cross will distribute jerry cans and soap so HHs can collect and safely store water in advance of the event. The distribution of jerry cans will be guided by the information provided by the National Disaster Risk Management Office (NDRMO) and through ongoing communication with WASH cluster members, particularly UNICEF. The specific locations for distribution will be determined based on the projected cyclone path. A total of 400 HHs will be selected, using agreed criteria for identifying those who are at risk of greatest vulnerability. Each HH will receive two jerry cans and soap. Fiji Red Cross will adopt the 'no regret approach' as outlined in the national Anticipatory Action Framework to ensure resources are allocated efficiently and effectively, minimizing the potential for missed opportunities.

Shelter

Activity 9: Distribution of Shelter Strengthening Kits

Leads: Ministry of Rural & Maritime Development and Disaster Management, UN International Organisation for Migration (IOM), Fiji Red Cross

Partners: Ministry of Rural & Maritime Development and Disaster Management, IOM, IFRC, Fiji Red Cross, Habitat for Humanity

Objective: To minimize the damage caused by cyclones to weak shelters belonging to vulnerable community members.

Description: IOM and the Fiji Red Cross, with technical and coordination support through Fiji's Shelter cluster and IFRC, will work with active Shelter Cluster members, agencies, offices, and organisations to provide the following:

- IEC materials on shelter reinforcement and the basics of tying down a shelter, as well as on safe evacuation and local service providers in the event of an emergency.
- Ropes, fasteners, screws, tarpaulins, and other shelter materials to support the strengthening of shelters ahead of the landfall of a cyclone.



- Construction Tools to support communities in the shelter strengthening process.

At readiness trigger, Fiji Red Cross will conduct training with communities on how to use safe shelter kits as well as raise awareness with communities about securing houses, removing potential flying objects, and trimming branches around houses to mitigate possible damages.

Challenges and potential improvements in the future:

There are several envisaged challenges to shelter interventions conducted within the AA Framework, the majority of which revolve around the provision of support to the most vulnerable or in need communities. Three core challenges have been discussed amongst the National Shelter Cluster members: 1) with shelter materials often spiking in cost after a cyclone makes landfall, deploying prepositioned kits before landfall leaves a risk of supporting households who may be less in need than others following landfall. With the spike in price and less prepositioned kits, response efforts may be hampered. 2) The timeframe of the AA activities leaves little room for capacity building, so interventions will need to largely rely on construction knowledge already present in any given community. The need to manage expectations for what can be achieved in this window, as well as focusing targeting on communities with experience in repairing/strengthening shelters, is a challenge. 3) Reaching maritime islands will pose a significant challenge to the cluster as most warehouses and stocks are in Viti Levu and Vanua Levu, with the greatest concentration in Suva and Nadi. Movement to maritime islands right before a cyclone may be too high of a risk.

Education

Activity 10: Delivery of Learning Materials

Leads: Ministry of Education and Human Resource Development (MEHRD) and UNICEF

Partners: Education Cluster CSO partners.

Objective: Ensure that children return to safe learning environments and are provided with relevant learning resources to continue their education.

Description: To provide vulnerable children access to learning, UNICEF will distribute school-in-a box kits to targeted schools. Education cluster would support teachers/students with PSS- and Refresher training for PFA providers to be on standby. Quick improvements to the school's buildings to reduce the risk of damage from cyclones (reinforcing roofs, securing windows, doors, and equipment etc will be undertaken).

- Coordinate the Education cluster response with technical advice, such as assessments, (inter-)cluster coordination, information management (4Ws) and reporting.
- Prepositioning of education-related items at schools (tents, school kits).
- Support coordination and innovation management across government-led Education cluster.
- UNICEF will monitor and evaluate the implementation of the project to measure the impact of AA in cooperation with the Government counterparts.

Challenges and potential improvements in the future:



- Detailed data on school populations and vulnerability is not available. Better data in the future can lead to better targeting of supplies and improved prepositioning.
- Tents appropriate as an emergency response only and adequate recovery planning needed to ensure they are not used for prolonged periods. Local expertise and capacity to erect tents without training is limited. Further training will be needed in the future to support first responders.

Food Security & Livelihood

Activity 11: Fishing-boat Strengthening Kits and Hermetic Dry Bags Distribution

Leads: Ministry of Agriculture and Waterways, Ministry of Fisheries and Forestry, Food and Agriculture Organization of the United Nations (FAO), Fiji Red Cross

Objective: Reducing the loss of livelihoods by securing boats, tools, and cash crops.

Description: To mitigate the potential impacts on the agriculture sector, FAO and the Fiji Red Cross, in agreement with the Ministry of Agriculture and Department of Fisheries, will distribute fishing-boat strengthening kits to at-risk fisherfolk and water-tight drums to farmers. The fishing-boat strengthening kits will enable fisherfolk to pull their boats ashore and store them in secure areas such as mangroves or along sandbars, where they can be tightly secured. Hermetic dry bags will present a viable solution for farmers to securely store their cash crops, providing a dry sanctuary that mitigates the risk of damage. It has dual purpose: firstly, to facilitate the preservation of harvested crops, and secondly, to provide a repository for clippings for replanting. By pre-emptively stockpiling crops prior to the cyclone's arrival, the potential for crop damage and loss can be mitigated. The decision to use the bag for either crops/fishing gear, or both, will be at the discretion of the household. This will be complemented by early warning messages delivered to high-risk households in accordance with the established communication protocols outlined by NDRMO and other UN agencies.

Challenges and potential improvements in the future: One of the primary obstacles is related to logistics. It will be crucial to preposition and store items in advance of the season to maximize their impact. While the necessary items can be largely be sourced locally, they are predominantly found in Suva or Nadi, with the hermetic bags coming in from Australia. Ensuring their accessibility from various locations across the country and maintaining their safety in readily accessible warehouses will be of utmost importance. As we progress, we'll need to refine and scale up this process, envisioning what the expansion might entail. This will require collaboration with the Ministry of Agriculture and Department of Fisheries, building on the lessons learned during this initial pilot stage and real activation learnings.

Communication

Activity 12: Common Approach to National Early Warning Messages

Leads: NDRMO and UNICEF

Partners: Ministry of Rural & Maritime Development and Disaster Management; National Disaster Risk Management Office (NDRMO); Communication Cluster (CCE WG), UNDRR, and World Health Organization (WHO).



Objective: Protect and minimise the loss of lives and livelihoods by disseminating timely and actionable early warning messages to communities via multiple channels.

Description: Building on the existing “Get Ready Disaster Happen” multi-media campaign, this activity will support dissemination of timely early warning messages to the public through radio, television, social media and SMS platforms. The early warning messages (Annex 9) have been developed in consultation with all the framework’s stakeholders and tested with the support of WHO (Annex 10). The early warning messages are linked to the specific readiness and activation triggers and provide sector-specific messages, including WASH, Health, Nutrition and Protection issues, Food Security, and education. These messages include sign language interpretations and will be broadcasted in English, iTaukei and Hindi.. During the readiness trigger, the messages will constantly air on radio and television platforms, through SMS blasts and social media. The frequency of these messages on all platforms will increase once the Action Trigger is Activated. Additionally, through the partnerships with CSO partners, volunteers will be mobilized into communities that would fall on the potential path of the disaster to assist in cyclone preparations. Turaga ni Koros, village leaders and advisory counsellors who would be sensitized on AA will be engaged through digital platforms and mobilized in their respective communities.

Challenges and potential improvements in the future:

- Dissemination of messages through media and SMS platforms can be disrupted should the telecommunications infrastructure be damaged by the disaster.
- Community mobilization can be hindered with restricted movements in communities.
- Need to revise and develop more messages with the input from each cluster/sector.

Activity 13: Local-level Early Warning Messages and Risk Communication

Leads: Fiji Red Cross Society

Description: Complementary to the national-level EWMs dissemination, Fiji Red Cross Society will disseminate early warning messages to communities through social and mainstream media. Fiji Red Cross will provide continuous updates and information on the status of the track path to communities, including advice on what needs to be done and what assistance is available to communities. Drawing on the common messages developed for the Framework (Annex 9), Fiji Red Cross Communications team will work closely with the DM team to tailor communication of the early warning messages appropriately to meet the differentiated needs of community members based on the National Society’s understanding of the local context across the operational areas. Fiji Red Cross will ensure that messages are channeled in ways that are accessible to, and can be easily understood by, the communities they are intended to reach. Early warning messages will be disseminated to at least 2000 people.

Continuous updates are essential to keep at-risk communities informed of any changes as the situation evolves. Fiji Red Cross staff and volunteers will also coordinate with local leaders and Community Disaster Committees with whom Fiji Red Cross has established relationships to monitor the needs of different groups to ensure those most at risk are prioritised for inclusion in all relevant activities. While management of evacuation centres is the responsibility of the Fiji



Government, Fiji Red Cross will work with the government to ensure communities are aware of where these centres are located and how to access them but will not duplicate government efforts with regard to evacuation centre management.

6.4 Community-based Anticipatory Activities

Under NDRMO leadership and within the national cluster system, a community delivery channel complements cluster-led activities where last-mile access and short lead times demand locally driven action. Community-based activities are cluster-aligned, NDRMO-validated, and coordinated with Divisional and Provincial authorities. They may be financed bilaterally or through the pooled fund, and they do not create a parallel mechanism: all planning, implementation and reporting run through the relevant government-led clusters and established SOPs. Communities may also undertake self-led measures, consistent with CBDRM training, acting on public advisories and official Early-Warning Messages (EWMs) they receive.

6.4.1 Other CSO/NGO projects (future additions)

Pursuant to the National Disaster Risk Management Act 2024—in particular Section 61 on people-centered multi-hazard warning systems that include systems for early/timely action and pre-agreed actions—and consistent with the Cabinet-endorsed Framework, the NDRMO may approve additional community-based NGO/CSO anticipatory actions without revisiting Cabinet, provided they: (i) align with the Framework’s triggers and cluster SOPs; (ii) are validated through the national cluster system; and (iii) do not alter the Framework’s core governance, trigger logic or scope.

6.4.2 Community self-led measures.

Communities may carry out self-led anticipatory measures consistent with CBDRM trainings and local preparedness plans—such as tie-down of dwellings, protection of documents/medicines, identification and outreach to high-risk households, safe evacuation planning, and community-watch arrangements for Protection—acting on the public advisories and official EWMs disseminated by NDRMO/FMS. Where appropriate, these actions are coordinated with Turaga ni Koros, village leaders and advisory counsellors and reflected in divisional situation updates.

6.5 Cross-Cutting Services

Accountability to Affected People (AAP)

Lead: NDRMO, UNICEF, Fiji Council of Social Services (FCOSS)

Accountability to affected people (AAP) is recognised as an important component of AA and will be applied during the planning and activation of the Framework.

UNICEF, in collaboration with the Fiji Council of Social Services (FCOSS), is advancing a pioneering approach to community engagement through the development and piloting of a digital Community Feedback Mechanism (CFM). This initiative is designed to ensure that communities across Fiji can share real-time feedback during emergencies using accessible platforms such as Viber, Facebook Messenger, SMS, and in-person channels. The programme’s



relevance lies in its culturally appropriate and inclusive design, which addresses communication gaps and empowers communities to actively participate in emergency preparedness and response. The mechanism leverages FCOSS's extensive network of District Councils of Social Services (DCOSS), enabling decentralised implementation that respects local customs and languages. This grassroots connectivity ensures that feedback is not only collected efficiently but also interpreted within the cultural context of each division, enhancing the responsiveness and relevance of humanitarian actions.

The CFM has already been piloted and endorsed by several organizations and is currently under review by NDRMO for national-level adoption. Once endorsed, it will become a standard tool for emergency operations, including AA activations, serving as a standardised tool for community engagement and accountability.

Logistics

Efficient operational logistics are paramount for the success of AA in Fiji. UN Agencies in Fiji have access to the UNCT SharePoint, a central platform for operational collaboration and information exchange. To streamline and improve operational logistics, each UN Agency's program and supply units have access to the Long-Term Agreements (LTAs) Directory, which is available on the UNCT SharePoint. This directory contains comprehensive information and instructions for effectively piggybacking existing LTAs, thereby leveraging the global UN Mutual Recognition Agreement. It is noteworthy that all UN agencies involved in the current proposal have endorsed a Mutual Recognition Statement. It's crucial to emphasize that OMT Representatives and Operations Teams in all UN Agencies across the Pacific region are well-versed in the operational procedures associated with this Mutual Recognition Agreement.

Access to LTA Directory: Within the UNCT SharePoint, all UN Agencies in Fiji can access the Long-Term Agreements (LTA) Directory. This directory serves as a valuable resource, providing comprehensive information and instructions on how to efficiently piggyback existing LTAs. The utilisation of this directory is instrumental in capitalising on the global UN Mutual Recognition Agreement.

Mutual Recognition Statement: All UN agencies involved have signed a Mutual Recognition Statement, emphasising the commitment to cooperation and harmonisation in operational logistics. This shared agreement fosters a collaborative and unified approach among UN Agencies, ensuring streamlined and efficient logistics processes.

Global LTA Requests: In addition to the UNCT SharePoint, UN Agencies in Fiji have the flexibility to request copies of global LTAs listed on the United Nations Global Marketplace (UNGM) website. This option allows each UN Agency to directly contact the respective UN Agency responsible for a particular LTA, ensuring timely access to essential resources.

Piggybacking Process: The well-established piggybacking process is an efficient means of streamlining operational procurement and logistics. This process extends to various types of LTAs, including those related to transport, NFIs, warehouse storage capacity, and more. UN Agencies in Fiji can leverage this process to bolster their operational capabilities.



UN Agencies in Fiji, through their access to the UNCT SharePoint and commitment to the Mutual Recognition Agreement, possess the necessary tools and cooperative spirit to optimize logistics and procurement and distribution processes. Leveraging global LTAs from UNGM further enhances their operational capabilities.

6.6 Coordination, Targeting and Information Management during activation

Coordination

Activation is coordinated in line with the AA Coordination SOP in Annex 11. Nationally, the NDRMO chairs inter-cluster meetings; the FMS provides authoritative forecasts and impact; line-ministry co-leads direct sector actions through the government-led clusters; and OCHA supports with automated trigger notifications, regular facilitation of AA TWG meetings, and consolidated updates. Sub-nationally, Divisional Commissioners convene divisional operations, with Provincial Administrators and District Officers linking decisions to community delivery via existing CBDRM structures and leaders. Partners implement through clusters and report via agreed IM tools (5Ws), and the National Emergency Operations Centre (NEOC) is placed on standby/activated as required. Meeting cadence and core information products are specified in Annex 11.

Targeting

Geographical targeting is based on the forecast cyclone path issued every four hours by the OCHA Centre for Humanitarian Data (example in Annex 6), informed by FMS analysis. The trigger information email also includes vulnerability at Admin 3 from the Fiji Children's Climate Risk Index – Disaster Risk Model (CCRI-DRM) led by UNICEF.²⁰ The Risk Index for Climate Displacement (RICD), which is being developed and piloted in Fiji by IOM through its Climate Mobility Innovation Lab, focuses on identifying displacement triggers and risk hotspots. The RICD will be used to support and inform the targeting of AA activities once available.²¹ Once a decision is made, the geographical targeting decision is recorded using the standard template. NDRMO consolidates targeting submissions into a national view and shares updates through inter-cluster and divisional coordination. OCHA facilitates the daily AA TWG meetings and provides consolidated updates to NDRMO.

Information Management

Information management ensures that geographic targeting decisions and activity updates are consistent, traceable and usable for a seamless transition from anticipatory action to response.

All partners report implementation through the 5Ws platform with an "AA" flag to distinguish anticipatory records, capturing: who is delivering (organisation/cluster), what modality is used (as per pre-agreed package/SOP), where activities occur (mappable admin locations/sites), when delivery happens (window/status), and for whom (people targeted/reached with feasible disaggregation), including brief notes on inclusion/safeguarding/AAP where relevant.

²⁰ <https://unosat-geodrr.cern.ch/apps/FJI/CCRI-DRM/>

²¹ https://environmentalmigration.iom.int/sites/g/files/tmzbd11411/files/documents/2025-07/iom_asiapacific_cmil_projectsheet1ricd_print_draft7-1_0.pdf



Handover/Transition to response

After landfall, the Targeting Decision Log and AA-flagged 5Ws provide the starter dataset for any immediate response under the same clusters and, where activated, the NEOC. As part of the Clutransition, Initial Damage Assessments (PDAs/IDAs) are initiated using national forms that include an AA module (Annex 12), allowing teams to (i) verify impact in areas targeted ex-ante, (ii) capture unmet needs, and (iii) document immediate outcomes of anticipatory actions.

6.6 Preparedness and Operational Readiness

Preparedness and operational readiness ensure that anticipatory actions can be delivered within the short window between trigger and impact. NDRMO and OCHA are responsible for overall coordination preparedness, while line ministries and humanitarian partners are responsible for preparedness related to their respective AA activities, under the government-led national cluster system.

Coordination (NDRMO and OCHA)

- Regular coordination meetings of the Fiji Anticipatory Action Technical Working Group (Fiji AA TWG) to maintain readiness and resolve operational bottlenecks.
- A multi-stakeholder table-top exercise at the start of each cyclone season to test roles, timelines and information flows.
- In-house trainings for NDRMO staff and District Officers (DOs) to refresh SOPs and activation procedures.
- Inclusion of AA briefing sessions in NDRMO-led preparedness activities (e.g., Disaster Awareness Week, National Emergency Response Training, briefings and related events).

Protection (MWCSP and WFP)

WFP together with MWCSP and Financial Service Providers conducted a refresher workshop and simulation exercise in December 2024 on multi-purpose cash payout to social welfare beneficiaries based on geographical and vulnerability targeting for a rapid cash payout. Elements of effective communication, accountability to affected population through a complaints and feedback mechanism and a post distribution monitoring were also part of the refresher exercise.

WASH (UNICEF and MHMS)

UNICEF is supporting the MHMS and the national WASH coordinator on WASH cluster coordination. Critical WASH supplies such as hygiene kits and MHM supplies, water storage containers are prepositioned in Suva. Minimum critical WASH supplies are also prepositioned in the warehouse of MHMS at Lautoka, Ba, Tavua and Suva and Nabouwalu.

Protection (Fiji Red Cross)

Training on Protection, Gender and Inclusion will be conducted for staff and volunteers of Fiji Red Cross to ensure all readiness and early action activities are considerate of differentiated needs and the most marginalised members of the community are prioritised for support (including women, children, the elderly, people with disability).



GBV & SRH (MWCSP, MHMS, UNFPA)

As part of anticipatory action preparedness, UNFPA, in collaboration with the MWCSP, conducted frontline dignity kit distributor training and simulation exercises across all four divisions in Fiji. The two-day training sessions focused on strengthening the capacity of government and community actors to manage prepositioned supplies, plan and execute timely distributions, and report effectively ahead of potential crises. Participants also practiced after-action reviews and communication documentation, including capturing beneficiary stories and quotes, to enhance community engagement, strengthen accountability to affected people programming, and visibility of anticipatory interventions before an emergency strikes.

To complement this effort, UNFPA organized a one-day divisional consultation and simulation exercise with MHMS sub-divisional staff to strengthen coordination and preparedness within the health sector. The exercise focused on identifying beneficiary selection criteria for unconditional cash support and establishing clear data-sharing mechanisms to ensure timely and equitable assistance once early warning triggers are activated. In parallel, UNFPA facilitated engagement meetings with financial service providers to streamline mechanisms for the rapid release of cash to pre-identified beneficiaries, ensuring that anticipatory actions translate into faster, more efficient protection and support for women, girls and vulnerable groups at risk.

Education (UNICEF)

UNICEF and partners will provide refresher training to teachers and support workers on PSS (Psychosocial Support) to ensure vulnerable children are protected, supported to continue learning and referred for further support when necessary .

Food Security and Livelihood (FAO and Fiji Red Cross)

FAO and the FRCS conducted a simulation of the livelihood protection activities in June 2024²² to test the last mile delivery of the plan. The simulation showed that building on existing Community Disaster Committees speeds buy-in and helps embed AA in community plans, while simulations are a practical way to test community-led targeting and rapid distribution. Operationally, it also showed that early monitoring and pre-positioning are essential for hard-to-reach coastal sites, and the intervention package (boat-protection kits and hermetic bags) should be iterated to match user needs and regulatory requirements.

ADRA

ADRA started a 2-year AA project leading to the implementation of Early Action Protocol which will be integrated to this Framework. The planned preparedness and operational readiness activities include:

1. Conduct training for ADRA Fiji staff
2. Develop and share a position paper on integrating AA, with technical input from ADRA Germany, to engage donors, corporate partners, and government stakeholders.

²²Logavatu, N., Liebrechts, M., Temo, K., Jones, C., Jang, I., Ji, L. & Talakai, M. 2025. *Simulating anticipatory action for tropical cyclones in Fiji*. FAO. Apia. '[Simulating Anticipatory Action for Tropical Cyclones in Fiji](#)'.



3. Undertake a study on traditional and indigenous knowledge related to AA and early warning systems, to inform community-level awareness and preparedness.
4. Pilot an Early Action Protocol (EAP) in a selected community, ensuring active involvement of local authorities.
5. Test and validate the EAP through simulation exercises, integrate it into ADRA Fiji's emergency system, and align it with the National Emergency Management Plan (NEMP).
6. Disseminate lessons learned and best practices with regional stakeholders and ADRA offices.
7. Advocate for EAP financing and partnerships through targeted meetings, documentation, and donor engagement.
8. Strengthen coordination mechanisms with local and national authorities to support AA implementation.

6.7 Community Sensitisation (Non-Alert Risk Communication)

Community sensitisation plays a critical role in ensuring that individuals and households understand AA – what it is, how to respond when official alerts are issued, and why government is piloting anticipatory approach to support the most ahead of storm. Building on the recommendation from the Process Learning study, community sensitization will be led by NDRMO and delivered with Divisional, Provincial, District, local authorities, cluster partners and civil society, sensitisation complements—and is aligned with—the Early-Warning Messages set out in Activity 1. The objectives of community sensitization are:

- Building public awareness of anticipatory action;
- Reinforcing practical household and community measures from CBDRM training (for example, tying down dwellings, protecting documents and medicines, checking on high-risk households, and confirming safe evacuation plans);
- Managing expectations by explaining that pre-impact assistance targets the most vulnerable in forecast impact areas.

The approach relies on simple, accessible materials in English, iTaukei, Hindi and sign, used both pre-season and in-season (non-alert). Delivery channels include a short community sensitisation video (produced by UNICEF with NDRMO and the Fiji AA TWG), a one-page awareness sheet for community leaders (Turaga ni Koros, village leaders and advisory counsellors) disseminated via Divisional Commissioners and mainstreamed through the inter-cluster system, and the integration of AA into DRM policy orientations, CBDRM trainings and Disaster Awareness Week activities (Annex 13). To complement this approach, ADRA will conduct training for ADRA Fiji staff, church leaders, local authorities, and communities on anticipatory action (AA), focusing on its role in disaster risk management and stakeholder responsibilities.



7 The Money: Pre-Arranged Financing

The financing architecture of Anticipatory Action (AA) is fundamental to its success. It is structured around two complementary pillars: “build” and “fuel.” The “build” component refers to long-term investments that establish the systems, capacities, and infrastructure necessary to enable anticipatory action. This includes strengthening early warning systems, developing policy frameworks, training implementing partners, and pre-positioning essential supplies. In contrast, the “fuel” component refers to pre-arranged, operational funding that is released automatically once a pre-agreed trigger is met. This funding enables the timely implementation of pre-defined interventions such as cash transfers, evacuation support, and protection measures. In essence, “build” enables the system, while “fuel” powers the response—and anticipatory financing ensures both are in place and ready when needed.

7.1 Financing Overview

Funding overview in US\$ for coordinated framework

Organization	Source 1	Amount (US\$)	Source 2	Amount (US\$)	Total (US\$)
WFP	CERF	948,990	Agency financing	500,000	1,448,990
FAO	CERF	274,990	Agency financing	200,000	474,990
UNICEF	CERF	774,187	Agency financing	400,000	1,174,187
UNFPA	CERF	200,075	Agency financing	200,000	400,075
IOM	CERF	200,000			200,000
UNW			Agency financing	50,000	50,000
WHO			Agency financing	30,000	30,000
	Simplified early action protocol	140,232			140,232
FRCS	ADRA	19,500			19,500
	Germany Deutschland Hilft				
ADRA ²³					
TOTAL					3,937,974

7.2 Build Funding

Partners invest in the foundations that make anticipatory action work season after season: people-centred early warning and risk communication; clear SOPs tested through simulations; pre-positioning of NFIs and maintenance of Long-Term Agreements (LTAs) with suppliers; robust information management (IM); supplier readiness, warehousing and surge rosters; and community sensitisation and training of implementing partners. Examples of activities funded through the “build” component are included in session 6.6.

²³ The amount refers to “fuel” funding under ADRA’s project to fund and Early Action Protocol activation. These will be released when the Early Action Protocol will be finalized.



These “build” investments are the start-up and maintenance costs of a collective approach (the build → fuel → evaluate cycle) and include enabling projects that are covered up front by implementing agencies but are not always financed through emergency windows (including CERF). The Fiji Red Cross’ Early Action Protocol includes funds for procurement of pre-positioned stocks and readiness activities. ADRA’s AA project includes provisions for build funding.

7.3 Pre-arranged financing: “Fuel”

Pre-arranged finance to fuel anticipatory action is critical—especially for sudden-onset cyclones—to enable timely, effective delivery in the short pre-impact window. Financing for this Framework is pre-arranged through multiple channels that complement one another and operate to the same triggers, SOPs and operational plan under Government leadership. Each channel follows its own fiduciary rules but reports into a single operational picture, ensuring coherence, preventing double-funding and duplication, and directing resources to priority locations.

Central Emergency Response Fund (CERF)

The Emergency Relief Coordinator agreed to pre-arrange up to \$2.4 million from CERF to support anticipatory action in Fiji. CERF will disburse funds for anticipatory action on a no-regrets basis once three conditions are met:

- Endorsement by the relevant Resident/Humanitarian Coordinator of the Anticipatory Action framework (this document) and the CERF application package comprising an application chapeau, agency-specific project proposals and agency-specific budgets (in annex 7); and
- Pre-approval by the Emergency Relief Coordinator of the Anticipatory Action framework (this document) and the CERF application package comprising an overall strategy, agency-specific project proposals and agency-specific budgets (in annex 7); and
- Activation of either the readiness trigger or the action trigger within a maximum of two years from the ERC’s pre-approval of the framework.

CERF funding is guaranteed and will be activated and disbursed as automatically as possible immediately after the defined trigger(s) is/are reached. CERF will disburse funds on a no-regrets basis. While a portion of the fund can be used immediately upon disbursement for readiness activities, the remaining portion of the funding can only be used if and when an action trigger is reached. The amount of funding for readiness vs action activities will be clearly defined in the pre-approved project proposals and budget. The need to distinguish between these two cost categories in advance is important given the different potential scenarios.

Pre-arrangement and/or receipt of CERF funding for anticipatory action does not preclude or guarantee additional CERF funding for a complementary rapid response to save lives resulting from the same or other shocks. This means that the pre-arranged funding by CERF for anticipatory action is for the hazards and triggers outlined in this framework. Should there be additional needs or other disasters, CERF’s other funding modalities can be requested.

Exact details on financing per agency can be found in the CERF application documents annexed.



UN Agencies Co-Financing

WFP

With support from the German Federal Foreign Office, a sum of USD500,000 has been allocated by WFP to be disbursed upon confirmation of activation triggers to co-finance the CERF allocation intended to reach 10,000 households with multipurpose cash assistance, as well as other readiness and activation costs. Five thousand (5000) additional households will benefit from WFP's co-financing. In total 15,000 households are planned to receive multipurpose financial assistance through the Anticipatory Action pilot project

UNFPA

UNFPA is uniquely positioned to lead anticipatory and preparedness actions that safeguard the SRH and GBV needs of women, girls, and vulnerable populations in humanitarian contexts. The proposed USD 212,413 in AA funding will strategically complement UNFPA's ongoing USD 200,000 disaster preparedness and response initiatives in Fiji, supported by national partners and the Government. By leveraging both core and donor resources, UNFPA will expand the reach and effectiveness of existing interventions, ensuring that essential SRH and GBV services remain accessible and responsive in the face of emergencies.

UNICEF

UNICEF is strategically poised to proactively address humanitarian needs in target communities, with a dedicated allocation of USD 400,000 from the Global Humanitarian Thematic Funds. This funding enables UNICEF, both independently and in collaboration with its trusted partners on the ground, to swiftly provide vital assistance to those most vulnerable in the face of impending crises. Furthermore, UNICEF's ongoing two-year work plan in cooperation with the Government of Fiji demonstrates the organization's commitment to preparedness and anticipatory action. Within this comprehensive plan, there exists a flexibility that allows for the seamless transition of existing activities into anticipatory actions when required. This proactive approach underscores UNICEF's dedication to ensuring the well-being and safety of communities at risk, reinforcing its role as a steadfast humanitarian leader.

FAO

Under FAO's Anticipatory Action Window, with generous support from the German Federal Foreign Office, a sum of USD 200,000 has been strategically allocated to Fiji. This allocation is in reaction to the elevated probability of an above-average cyclone season in the region. The funds will be directed towards facilitating anticipatory action activities by prepositioning and distributing watertight drums and reinforcing fishing boats. Furthermore, this financial support plays a pivotal role in fostering collaboration with the Fiji Red Cross, thereby streamlining the logistical and operational procedures to expedite action in light of the trigger.

The IFRC-DREF Early Action Protocol

The Fiji Red Cross Early Action Protocol²⁴ is financed through the International Federation of Red Cross and Red Crescent Societies' Disaster Response Emergency Fund (IFRC-DREF) Anticipatory Pillar. It provides a pre-agreed envelope for pre-positioning stocks, readiness

²⁴ https://www.anticipation-hub.org/Documents/EAPs/sEAP_Fiji_Tropical_Cyclone.pdf



activities (eg mobilisation, awareness raising) and early actions. Funding for early actions is only released upon activation of the protocol when the trigger is reached. Financial management follows FRCS/IFRC fiduciary rules.

ADRA

AA ADRA 2025 Activities are financed under the 2 year (July 2025-June 2027) CANDO 4 Project, which includes 8 primary activities under Result 2 on CANDO 4 Project funding by ADRA Germany Deutschland Hilft.

Government-led financing (Disaster Risk Finance and Climate Finance).

Together with the Ministry of Finance, and with facilitation support from OCHA, NDRMO will explore how internal government resources can finance anticipatory action under this Framework. The National Disaster Risk Management Act 2024 provides a basis through the Disaster Risk Management Fund (Emergency Trust Fund), which can be used in line with government rules and the Framework's triggers, SOPs and reporting., which can be used in line with government rules and the Framework's triggers, SOPs and reporting.

Disaster-risk financing (DRF) instruments that are budgeted and controlled by the Government can be used to finance and expand anticipatory action activities under the framework parameters. These include, for example, Pacific Catastrophe Risk Insurance Company (PCRIC) parametric insurance, the World Bank Catastrophe Deferred Drawdown Option (CAT-DDO), and World Bank Contingency Emergency Response Components (CERCs) embedded in sector projects. Because these DRF instruments are financed and controlled by Government—and any payout or drawdown is received by Government—they constitute internal resources that can be used to finance and, where appropriate, expand line-ministry-led anticipatory activities under this Framework.

Complementary climate risk and recovery finance initiatives, such as the Global Shield may also be explored to finance and expand line-ministry-led anticipatory activities and leverage pre-arranged financing instruments (e.g., trigger-based financing and insurance), operating under the same AA Framework parameters (readiness/action triggers, SOPs, coordination and reporting).

Other Pooled/Bilateral Channels

Additional pooled or bilateral resources may be activated to complement the above and expand anticipatory activities, provided they operate under the parameters of this Framework. To formalize this, partners provide a short alignment note/side letter confirming adherence to the Framework.



8 The Learning

Learning is an integral part of the Fiji AA Framework. It ensures that anticipatory action is continuously improved, evidence is generated to demonstrate impact, and that national systems are strengthened for long-term use.

During the pilot phase (2023–2025), learning was prioritised from the outset. An independent Process Learning, conducted by the University of the South Pacific, confirmed that the Framework generated important lessons even in the absence of its activation. These findings directly informed the adjustments and priorities reflected in this revised version of the Framework.

In parallel, the Fiji AA Technical Working Group supported the design of a multi-stakeholder evaluation protocol,²⁵ funded by FAO and developed by Johns Hopkins University with technical support from OCHA and FAO. This protocol provides a shared methodology for assessing the effectiveness and value for money of anticipatory actions when the Framework is activated. It embeds an AA module into Fiji's national Initial Damage Assessments and applies both quantitative and qualitative methods to capture timeliness, equity, household impacts, and return on investment across all sectors.

Learning in Phase 2 (2025–2027) will therefore follow three complementary streams:

1. Agency monitoring and evaluation – Each agency will apply its own systems to track delivery, aligned to a harmonised set of indicators agreed through the Fiji AA TWG.
2. Collective evaluation – If activation occurs, the Johns Hopkins protocol will be applied under NDRMO leadership to evaluate the impact of the Framework. The evaluation will be carried out by an independent party hired by FAO with CERF funding.
3. Process learning – If no activation occurs in a season, lessons will continue to be captured through simulations, seasonal reviews, and community feedback, ensuring the Framework evolves even without a live trigger.

Across these streams, the Framework will prioritise answering key learning questions:

- Timeliness: Did anticipatory actions reach people before impact and allow more time for preparation?
- Effectiveness and impact: Did the actions reduce humanitarian consequences on lives, livelihoods, health, food security, education, and protection?
- Targeting and equity: Did the Framework reach the most at-risk groups, including women, children, persons with disabilities, and those in remote areas? Did joint targeting improve efficiency and reduce duplication?
- Early warning and risk communication: Were messages timely, trusted, accessible, and did they lead to protective behaviours?
- Inclusion and localisation: How were communities, sub-national authorities, and civil society organisations engaged? Did the Framework advance localisation and ownership?
- Partnership and governance: How did government leadership and cluster-based coordination support delivery and institutionalisation?

²⁵ Johns Hopkins University (2025), Anticipatory Action Framework for Tropical Cyclones in Fiji: Multi-stakeholder Evaluation Protocol, <https://reliefweb.int/report/fiji/anticipatory-action-framework-tropical-cyclones-fiji-multi-stakeholder-evaluation-protocol-march-2025>



- Value for money: What is the return on investment of anticipatory actions compared with traditional response, and how can financing strategies be strengthened for sustainability?

Learning is embedded as part of the Framework's design, not an afterthought. Findings will be shared with the government and partners through the Fiji and PHT AA TWG, and used to inform government decision-making. Evaluations are explicitly designed to feed into the national policy agenda on AA and to strengthen its integration within Fiji's wider disaster risk management system.

At the same time, Fiji's experience contributes directly to the global evidence base on AA. By demonstrating how a government-led framework can function even without activation, and by pioneering collective evaluation methods, Fiji provides lessons of global relevance—showing that AA is not only about faster response, but about system change. In this way, learning from Fiji supports both the development of AA worldwide and its institutionalisation as part of Fiji's national disaster risk governance.

Advocacy and Public Communication

Partners agree to coordinate, under the leadership of the NDRMO and the Resident Coordinator, key messages around the framework, including during the development, activation and learning phase. Partners' advocacy related to projects under this Framework should always reference it.

In case of an activation of the framework, close coordination facilitated by OCHA will facilitate as a minimum: a joint press release and mutual amplification of press released and social media stories.

To enhance common messaging and advocacy for anticipatory action, partners agree to share any visuals (photos, videos) and impact stories with the ad hoc committee as these become available.



Country Snapshot Brief: Fiji

Overview

Fiji is among the world's most climate-vulnerable nations, facing frequent tropical cyclones, sea level rise, and displacement that disproportionately impact women, adolescent girls, youth, people with disabilities (PWD), individuals of diverse sexual orientation, gender identities, expressions and sexual characteristics (SOGIESC) and other vulnerable groups. During crises, access to sexual and reproductive health (SRH) services is often disrupted while risks of gender-based violence (GBV) surge. Following Cyclone

Yasa (2020), protection actors reported increased demand for GBV services and significant barriers to SRH access in remote areas, highlighting the urgency of pre-positioned supplies and integrated early action systems¹. With over 64% of Fijian women experiencing intimate partner violence in their lifetime², embedding SRH and GBV into disaster risk reduction (DRR), anticipatory action (AA), and climate frameworks is essential to protect rights, reduce harm, and build resilient, inclusive systems that reach those most at risk.

SRH and GBV within Fiji's Policy Frameworks

SRH	GBV
Climate: Acknowledged in national climate policy and adaptation plans, but with no operational mechanisms, dedicated funding, or governance inclusion for SRHR. DRR: Some SRH elements (maternal health) appear in DRR plans such as HEADMAP and the DRM Bill, but they are inconsistently applied and lack scale or routine national resourcing. Anticipatory Action: A core priority in the updated AA Framework including Cash and Voucher Assistance for termed high-risk pregnant women, prepositioned clean delivery kits, and referral systems.	Climate: While referenced in gender-related frameworks, GBV is not routinely integrated into climate or adaptation planning or budgeting. DRR: Present in DRR documents like the DRM Bill and EAW NAP, but not systematically included in preparedness plans, simulations, or DRR funding mechanisms. Anticipatory Action: Within the revised AA framework (2025-2027), prepositioning and distribution of inclusive Pacific Customised Dignity Kits targeting women, adolescent girls and women with disabilities.

Promising Practices

Fiji has advanced promising practices by including SRH and GBV in the anticipatory action framework, by working to integrate gender, disability, and social inclusion (GEDSI) considerations into

disaster risk reduction frameworks, and by investing in capacity building on the Minimum Initial Service Package (MISP) and GBV response.

Key Frameworks and Legislation

Climate:

National Climate Change Policy (2018-2030), Climate National Adaptation Plan (2018), Climate Change Act (2021)

Disaster Risk Reduction:

National Disaster Risk Reduction Policy (2018-2030), Natural Disaster Management Act (1998)

Anticipatory Action Framework:

Fiji Anticipatory Action Framework (2023), Forecast-Based Financing SOPs

SRH/GBV/Youth:

Fiji National Youth Policy (2023-2027), National Gender Policy (2014), National Action Plan to Prevent Violence Against All Women and Girls (2023-2028), Fiji Sexual and Reproductive Health Policy (2011)

1. Gaddour, A., Tappis, H., Lazieh, S., Ward, A., & Spiegel, P. (2024). The humanitarian-development nexus and sexual and reproductive health interventions in fragile settings: A scoping review. *Johns Hopkins Bloomberg School of Public Health / Jhpiego. medRxiv.*

2. United Nations Office for Disaster Risk Reduction (UNDRR). (2023, July). Midterm review of the Sendai Framework for Disaster Risk Reduction 2015-2030: Thematic report on gender equality and social inclusion in disaster risk reduction in the Pacific. UNDRR / Institute for Sustainable Futures, University of Technology Sydney.

Key Gaps

- **Weak SRHR and GBV integration in climate planning:** Policies lack clear strategies for service continuity and risk mitigation, including in early warning and anticipatory action.
- **Limited data on climate impact:** There is a critical gap in data on how climate change affects SRHR and GBV, hindering evidence-based planning and resource allocation.
- **Youth perspectives underrepresented:** While youth are acknowledged in policies, their voices are not systematically included in SRHR and GBV strategies, and out-of-school youth remain underserved.
- **Limited protection for marginalized groups:** SOGIE-SC individuals face heightened risks in climate crises, with few inclusive strategies in current policies.

Recommendations

1. Review national and subnational DRR, climate, and AA policies and strategies to assess SRH and GBV integration and alignment with global and regional commitments (e.g., Sendai Framework, SDGs, CEDAW, Sendai GAP, FRDP, PRP). Identify gaps in services and protections and update policies and monitoring systems accordingly.
2. Allocate national budget lines and decentralized emergency funds to support pre-disaster SRH and GBV actions (e.g., stockpiling dignity kits, early GBV case management, contraceptive procurement) linked to forecast-based triggers and seasonal risk calendars.
3. Invest in tools such as parametric insurance, pre-approved contingency funds, or shock-responsive social protection schemes that activate when climate thresholds are reached. Ensure these mechanisms include SRH and GBV-specific funding lines and trigger actions that directly protect the health, rights, and safety of women, youth, adolescent girls, PWD, SOGIESC populations and other vulnerable populations.
4. Establish localized accountability systems, including anonymous feedback mechanisms, GBV safety audits, survivor-centered community monitoring tools, and data collection offers, ensuring responses inform national systems.
5. Reinforce institutional and operational structures and the national, divisional and sub-divisional levels to embed SRH and GBV into anticipatory action, DRR, and climate systems by assigning empowered focal points to coordination platforms, engaging in planning processes, establishing multi-stakeholder coalitions, and enhancing technical and inter-cluster mechanisms to deliver gender-responsive preparedness, early action, and risk mitigation.



Annex 2 – Overview of Stakeholders

Government

National Disaster Risk Management Office (NDRMO)
Fiji Meteorological Services (FMS)

Ministry of Health and Medical Services (MHMS)
Ministry of Women, Children and Poverty Alleviation (MWCPA)
Ministry of Agriculture (MoA)
Ministry of Education and Human Resource Development (MEHRD)
Ministry of Rural & Maritime Development and Disaster Management (MRMDDM)
Ministry of iTaukei Affairs (MTA)

Humanitarian Partners

United Nations Office for the Coordination of Humanitarian Affairs (OCHA)
United Nations Office for Disaster Risk Reduction (UNDRR)
United Nations Children's Fund (UNICEF)

United Nations Population Fund (UNFPA)

World Health Organization (WHO)
United Nations Program for Gender Equality and Empowerment of Women (UN Women)
Food and Agriculture Organization of the United Nations (FAO)
Fiji Red Cross Society (FRCS) &
International Federation of Red Cross and Red Crescent Societies (IFRC)
International Organization for Migration (IOM)

The Adventist Development and Relief Agency (ADRA)
Fiji Council of Social Services (FCOSS)
Habitat for Humanity



Annex 3 – Historical Analysis

The historical storms since 2000 that would have triggered this framework as shown in the table below. Only storms with more than 0 “Total Affected” from the EM-DAT database are shown.

Name	CERF	Pop. exposed to 64 knots	Pop. exp. trig.	Two-day rainfall	Rain trig.	Either trig.	Total Affected
Winston 2016	True	796,251	True	195	True	True	540,558
Mal 2024	False	0	False	45	False	False	230,000
Harold 2020	True	32,963	True	128	False	True	180,000
Josie 2018	False	0	False	140	False	False	89,950
Keni 2018	False	9,169	True	126	False	True	89,250
Ana 2021	False	0	False	275	True	True	82,751
Cody 2022	False	0	False	203	True	True	69,564
Tomas 2010	False	17,865	True	79	False	True	39,101
Ami 2003	False	32,472	True	188	False	True	30,000
Yasa 2021	True	123,899	True	199	True	True	22,000
Evan 2013	False	285,222	True	130	False	True	8,400
Sarai 2020	False	0	False	203	True	True	7,780
Zena 2016	False	0	False	174	False	False	5,000
Unnamed 2004	False	nan	False	nan	False	False	5,000
Mick 2010	False	0	False	118	False	False	3,845
Tino 2020	False	0	False	122	False	False	3,115
Jim 2006	False	0	False	nan	False	False	168
Daman 2008	False	167	False	81	False	False	69

Columns reference:

- *CERF*: whether the storm had a CERF allocation
- *Pop. exposed to 64 knots*: the population estimated to have been exposed to at least 64 knot wind speeds
- *Pop. exp. trig.*: whether the population exposure trigger condition was met
- *Two-day rainfall*: the maximum 2-day total rainfall for the storm, averaged over the whole country
- *Rain trig.*: whether the rainfall trigger condition was met
- *Either trig.*: whether either trigger condition was met (i.e. whether the framework was triggered)
- *Total Affected*: the total number of people affected by the storm, from the EM-DAT database

The overall trigger mechanism was developed through a simple optimization process:

1. All possible trigger thresholds for wind exposure (at 34-, 64-knot levels), and two-day rainfall were iterated over. For each trigger combination, the historical triggers were determined.
2. Trigger combinations that did not have the correct return period (3.1 years) were rejected.
3. Trigger combinations where the forecast-based trigger did not trigger for all historical CERF allocations (Winston 2016, Harold 2020, and Yasa 2021) were rejected.
4. Trigger combinations that were more likely to trigger with the observational trigger than with the forecast trigger were rejected.
5. The trigger combination whose historically triggered storms caused the most total impact (measured by “Total Affected”) was selected.



The accuracy metrics²⁶ of the triggers are shown in the table below. For this table, a “positive” is a storm with “Total Affected” of at least 22,000 people (i.e., storms at least as bad as Yasa 2021). This subset of storms was selected on the basis that theoretically a trigger could have activated for exactly this subset with a return period of 3.1 years (the return period specified for this framework).

Accuracy metrics			Analysis seasons: 2001-2024		
Trigger	Accuracy	Detection rate	False alarm rate	Precision	F1 score
Readiness	90%	60%	3%	86%	71%
Action	90%	60%	3%	86%	71%
Observational	86%	40%	3%	80%	53%
Overall	92%	80%	5%	80%	80%

²⁶ See here for definitions: https://en.wikipedia.org/wiki/Confusion_matrix



Annex 4 – Distribution Lists

Distribution list A: Official Trigger Email

Mailing list: trigger_FijiAA@pacifichumanitarian.org

Resident Coordinator	Dirk Wagener dirk.wagener@un.org ; Kesang Phuntsho kesang.phuntsho@un.org ; Fiona Schmid fiona.schmid@un.org ; Alumita Masitabua alumita.masitabua@un.org ; RCO Fiji rco.fiji@un.org
NDRMO	Napolioni Boseiwaqa napsboseiwaqa@gmail.com or Napolioni Boseiwaqa napsboseiwaqa@gmail.com ; Litiana Bainimarama lbainimarama@govnet.gov.fj or lnaidoleca@gmail.com ; Shaya Malini shayamalini2021@gmail.com ; National Emergency Operations Centre neocfiji@gmail.com
Cc	
Ministry of Health & Medical Services	Anaseini Maisema abmaisema@gmail.com ; Anaseini B. Maisema anaseini.maisema@health.gov.fj ; Ivatuvoka@gmail.com; Ivatuvoka@yahoo.com; Jese Vatukela jese.vatukela@health.gov.fj Vimal Deo vimal24deo@yahoo.com or vimal.deo@health.gov.fj ; Fiji WASH Cluster fijiwashcluster@gmail.com ; Toga Vosataki togavosataki@yahoo.com ;Kelera Sakumeni kbavsaku@gmail.com ;Dr Rachel Devi rachel.devi@health.gov.fj
Ministry of Women, Children and Social Protection	Selai Korovusere SelaiK@mwcpa.gov.fj ; Salote Biukoto salote.biukoto@mwcpa.gov.fj ; Rozia Bi rbi@mwcpa.gov.fj ; Laisani Petersen laisani.petersen@unwomen.org
Ministry of Agriculture	Titilia Wati titiliadavetanivalu3@gmail.com
Ministry of Education	Semisi Siga semisi.siga01@govnet.gov.fj ; Koroiwaqa koroiwaqa1989@gmail.com
Ministry of Rural & Maritime Development & Disaster Management	Arieta Dimuri ddsmrmd@gmail.com ; Kasalia Kororua kasakororua@gmail.com ; Keith Hornby keithhornby@gmail.com ;
OCHA	Olga Prorovskaya prorovskaya@un.org ; Katalaine Duaibe katalaine.duaibe@un.org ; Sara Manni sara.manni@un.org ; Tristan Downing tristan.downing@un.org ; Daniel Pfister pfisterd@un.org ; Yakubu Alhassan yakubu.alhassan@un.org ; Daniel Gilman gilmamd@un.org ; Julia Wittig wittigj@un.org ; OCHA-cerf cerf@un.org ; OCHA Office of the Pacific Islands ochafiji@un.org
NDRMO	Litiana Bainimarama lbainimarama@govnet.gov.fj or lnaidoleca@gmail.com ; Napolioni Boseiwaqa napsboseiwaqa@gmail.com ; Prishika Nadan prishinadan@gmail.com ; National Emergency Operations Centre neocfiji@gmail.com Bidisha Pillai pillai@unfpa.org ;Mateen Shaheen shaheen@unfpa.org ;
UNFPA	Rai Buenaventura buenaventura@unfpa.org ; Abdul Hussain abdussain@unfpa.org ;Olana Naigulevu naigulevu@unfpa.org ;Farida Tambun tambun@unfpa.org ; Komathi govindasamy@unfpa.org
IOM	BIDDER Matthew Aaron Mark mbidder@iom.int ; KANTHA Solomon skantha@iom.int ; DEVI Karishma kdevi@iom.int ; RO Bangkok - Emergency and Post-Crisis Team ROBangkokEPC@iom.int Jonathan Veitch jveitch@unicef.org ; Roshni Basu rbasu@unicef.org ; Diego Fernando Lopez dflopez@unicef.org ; Ali Safarnejad asafarnejad@unicef.org ; Halitesh Datt hdatt@unicef.org ; Semiti Temo stemo@unicef.org ; Ronesh Prasad rprasad@unicef.org ; Kencho Namgyal knamgyal@unicef.org ; Suranga De Silva sudesilva@unicef.org ; Aisling Falconer afalconer@unicef.org ; Johary Randimbivololona jrandimbivololona@unicef.org ; Aye Aye Than athan@unicef.org ; Diego Fernando Lopez dflopez@unicef.org ; Ro Iva Namela rmamela@unicef.org
UNICEF	JACOBS, Mark Andrew jacobsma@who.int ; GENAY-DILIAUTAS, Sophie genaydiliautass@who.int ; GILMORE, Chandra gilmorec@who.int ; CASEY, Sean scasey@who.int
WHO	



Pacific
Humanitarian
Team
ANTICIPATORY ACTION TWG

WFP	Emma Conlan emma.conlan@wfp.org ; Philippe Brewster philippe.brewster@wfp.org ; Saidamon Bodamaev saidamon.bodamaev@wfp.org ; Diego Flores diego.flores@wfp.org ; nitesh.chand@wfp.org
UNWOMEN	Naheed Ahme; Eri Taniguchi eri.taniguchi@unwomen.org Kolosa Matebalavu kolosa.matebalavu@unwomen.org Lanieta Tokalauvere lanieta.tokalauvere@unwomen.org
FAO	Qu, Guangzhou (FAOSAP) < Guangzhou.Qu@fao.org >; Talakai, Malia (FAOSAP) < Malia.Talakai@fao.org >; Young, Joann (FAOFJ) < Joann.Young@fao.org >; Jones, Catherine (FAORAP) < Catherine.Jones@fao.org >; Ji, Leeann (FAORAP) < Leeann.Ji@fao.org >; Riquet, Damien (FAORAP) < Damien.Riquet@fao.org >
UNDRR	Gabrielle EMERY gabrielle.emery@un.org ; Nazgul Borkosheva nazgul.borkosheva@un.org
IFRC	Finau Heuifanga LEVENI FINAU.LEVENI@ifrc.org ; Jen STEWART jennifer.stewart@ifrc.org ; Maciu Nokelevu maciu.nokelevu@ifrc.org ; Nete Tamanitoakula nete.tamanitoakula@ifrc.org
Fiji Red Cross	Ragigia Dawai < ragigia.dawai@redcross.com.fj >; Margaret Liebregts < margaret.liebregts@redcross.com.fj >; Unaisi Baro < unaisi.bar@redcross.com.fj >; Romit Maharaj romit.maharaj@redcross.com.fj ; Luta Teonea luta.teonea@redcross.com.fj ; Luisa Turaga luisa.turaga@redcross.com.fj ; Meresiana Moce meresiana.moce@redcross.com.fj
Australian Red Cross	Veronica Bell vbell@redcross.org.au
ADRA	Christine Lemau christinelemau@adra.org.fj ; Angelina Taufaga AngelinaTaufaga@adra.org.fj

Distribution list B: Complementary Trigger Information Email

Mailing list: triggerinfo_FijiAA@pacifichumanitarian.org

Resident Coordinator	Dirk Wagener dirk.wagener@un.org ; Kesang Phuntsho kesang.phuntsho@un.org ; Fiona Schmid fiona.schmid@un.org ; Alumita Masitabua alumita.masitabua@un.org ; RCO Fiji rco.fiji@un.org
NDRMO	Napolioni Boseiwaqa napsboseiwaqa@gmail.com or Napolioni Boseiwaqa napsboseiwaqa@gmail.com ; Litiana Bainimarama lbainimarama@govnet.gov.fj or Inaidoleca inaidoleca@gmail.com ; Shaya Malini shayamalini2021@gmail.com ; National Emergency Operations Centre neocfiji@gmail.com
Ministry of Health & Medical Services	Anaseini Maisema abmaisema@gmail.com ; Anaseini B. Maisema anaseini.maisema@health.gov.fj ; Ivatuvoka ivatuvoka@gmail.com ; Ivatuvoka ivatuvoka@yahoo.com ; Jese Vatukela jese.vatukela@health.gov.fj ; Vimal Deo vimal24deo@yahoo.com or vimal.deo@health.gov.fj ; Fiji WASH Cluster fijiwashcluster@gmail.com ; Toga Vosataki togavosataki@yahoo.com ; .Kelera Sakumeni kbavsaku@gmail.com
Ministry of Women, Children and Social Protection	Selai Korovusere SelaiK@mwcpa.gov.fj ; Salote Biukoto salote.biukoto@mwcpa.gov.fj ; Rozia Bi rbi@mwcpa.gov.fj ; Laisani Petersen laisani.petersen@unwomen.org
Ministry of Agriculture	Titilia Wati titiliadavetanivalu3@gmail.com
Ministry of Education	Semisi Siga semisi.siga01@govnet.gov.fj ; Koroiwaqa koroiswaqa1989@gmail.com
Ministry of Rural & Maritime Development & Disaster Management	Arieta Dimuri ddsmrmd@gmail.com ; Kasalia Kororua kasakororua@gmail.com ; Keith Hornby keithhornby@gmail.com
DSLOs	
OCHA	Olga Prorovskaya prorovskaya@un.org ; Katalaine Duaibe katalaine.duaibe@un.org ; Sara Manni sara.manni@un.org ; Tristan Downing tristan.downing@un.org ; Daniel Pfister pfisterd@un.org ; Yakubu Alhassan yakubu.alhassan@un.org ; Daniel Gilman gilmand@un.org ; Julia Wittig wittigj@un.org ; OCHA Office of the Pacific Islands ochafiji@un.org



NDRMO

Litiana Bainimarama lbainimarama@govnet.gov.fj or lnaidoleca@gmail.com;
 Napolioni Boseiwaqa napsboseiwaqa@gmail.com; Prishika Nadan
prishinadan@gmail.com ; National Emergency Operations Centre
neocfiji@gmail.com

UNFPA

Bidisha Pillai pillai@unfpa.org;
 Mateen Shaheen; shaheen@unfpa.org
 Rai Buenaventura buenaventura@unfpa.org;
 Abdul Hussain abdhussain@unfpa.org;
 Olana Naigulevu naigulevu@unfpa.org
 Farida Tambun tambun@unfpa.org

IOM

Komathi Govindasamy govindasamy@unfpa.org
 BIDDER Matthew Aaron Mark mbidder@iom.int; KANTHA Solomon
skantha@iom.int; DEVI Karishma kdevi@iom.int; RO Bangkok - Emergency and
 Post-Crisis Team ROBangkokEPC@iom.int

UNICEF

Jonathan Veitch jveitch@unicef.org; Roshni Basu rbasu@unicef.org; Diego Fernando
 Lopez dflopez@unicef.org; Halitesh Datt hdatt@unicef.org; Semiti Temo
stemo@unicef.org; Kencho Namgyal knamgyal@unicef.org; ; Aye Aye Than
athan@unicef.org; Suranga De Silva sudesilva@unicef.org; knamgyal@unicef.org;
 Aisling Falconer afalconer@unicef.org; Ro Iva Namela mamela@unicef.org
 WHO JACOBS, Mark Andrew jacobsma@who.int; GENAY-DILIAUTAS, Sophie
genaydiliautass@who.int; GILMORE, Chandra gilmorc@who.int; CASEY, Sean
scasey@who.int

WFP

Emma Conlan emma.conlan@wfp.org; Philippe Brewster philippe.brewster@wfp.org;
 Saidamon Bodamaev saidamon.bodamaev@wfp.org; Diego Flores
diego.flores@wfp.org; nitesh.chand@wfp.org

UNWOMEN

Naheed Ahmed Naheed.ahmed@unwomen.org; Eri Taniguchi
eri.taniguchi@unwomen.org; Kolosa Matebalavu kolosa.matebalavu@unwomen.org
 Lanieta Tokalauvere lanieta.tokalauvere@unwomen.org

FAO

Xiangjun Yao Xiangjun.Yao@fao.org ; Talakai, Malia (FAOSAP)
Malia.Talakai@fao.org; Young, Joann (FAOFJ) Joann.Young@fao.org; Vukialau
 Mere Mere.Vukialau@fao.org ; Jeffrey Kich Jeffrey.Kinch@fao.org ; Jones,
 Catherine (FAORAP) Catherine.Jones@fao.org; Inyoung Jang
Inyoung.Jang@fao.org; Riquet, Damien (FAORAP) Damien.Riquet@fao.org

UNDRR

Gabrielle EMERY gabrielle.emery@un.org; Nazgul Borkosheva
nazgul.borkosheva@un.org

IFRC

Finau Heuifanga LEVENI FINAU.LEVENI@ifrc.org; Jen STEWART
jennifer.stewart@ifrc.org; Maciu Nokelevu maciu.nokelevu@ifrc.org;
 Nete Tamanitoakula nete.tamanitoakula@ifrc.org

Fiji Red Cross

Aporosa Torotagi aporosa.torotagi@redcross.com.fj ; Unaisi Baro
unaisi.baro@redcross.com.fj ; Salote Maramaciriciri
salote.maramaciriciri@redcross.com.fj ; Ksanita Temo
kasanita.temo@redcross.com.fj ; Sainimili Lagilagi sainimili.lagilagi@redcross.com.fj ;
 Livai Mocolutu livai.mocolutu@redcross.com.fj ; Salote Tupou
salote.tupou@redcross.com.fj ; Seru Tabakece seru.tabakece@redcross.com.fj ;
 Mitieli Duvuloco mitieli.duvuloco@redcross.com.fj ; Sagaitu Josaia
sagaitu.josaia@redcross.com.fj

ADRA

Christine Lemau christinelemau@adra.org.fj ; Angelina Taufaga
AngelinaTaufaga@adra.org.fj



Pacific
Humanitarian
Team
ANTICIPATORY ACTION TWG



Annex 5 – DRAFT Trigger Messages

From: data.science@humdata.org

To: trigger_FijiAA@pacifichumanitarian.org

SUBJECT: Anticipatory action Fiji – Readiness trigger reached

Readiness trigger

This is an automated message.

Dear Resident Coordinator, dear colleagues,

The readiness trigger of the coordinated anticipatory action pilot for tropical cyclones in Fiji has been reached in line with the 120-hour forecast shared by the Fiji Meteorological Service, operators of Regional Specialized Meteorological Centre (RSMC) Nadi.

Readiness activities in line with the framework document [link] should now commence. CERF funding to UN agencies is being released. OCHA may convene a meeting of the participating partners.

Best wishes and good luck,

OCHA Center for Humanitarian Data

Action trigger

SUBJECT: Anticipatory Action Fiji – Action trigger reached

This is an automated message.

Dear Resident Coordinator, dear colleagues,

The action trigger of the coordinated anticipatory action pilot for tropical cyclones in Fiji has been reached in line with the 72-hour official forecast shared by the Fiji Meteorological Service, operators of Regional Specialized Meteorological Centre (RSMC) Nadi.

All activities in line with the framework document [link] should now commence. OCHA may convene a meeting of the participating partners.

Best wishes and good luck,


OCHA Center for Humanitarian Data

PS: Please remember that the impact of this pilot will be evaluated and we encourage all partners to document decisions and lessons learned as best as possible during this activation. Finally, please also ensure any visuals, stories, social media is shared with the group.






Below is a sample complementary cyclone forecast information message. The forecast in this sample was fabricated purely for the sample and is not valid.



Wind swaths

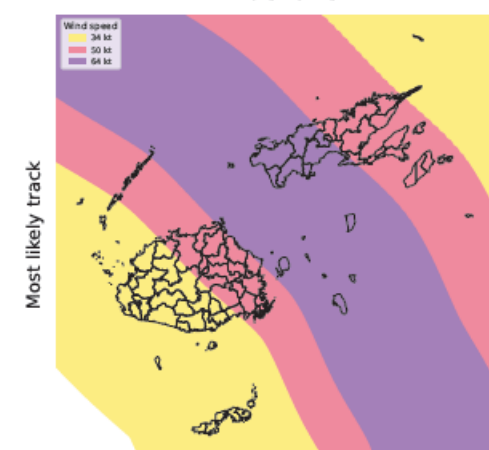

Population exposure

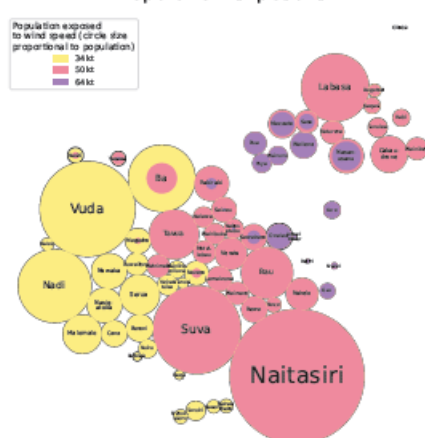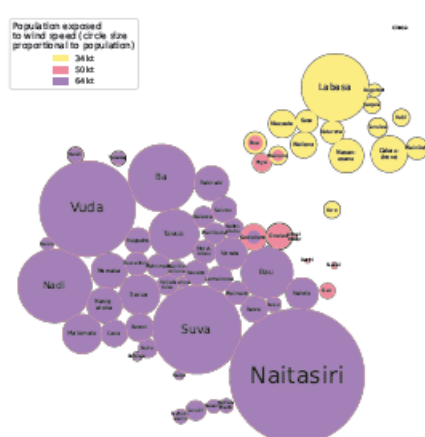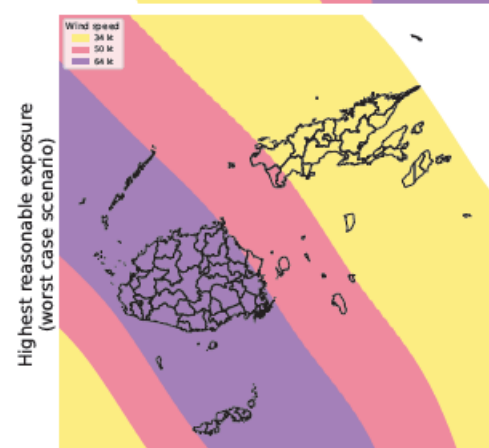Highest reasonable exposure
(worst case scenario)

Lowest reasonable exposure
(best case scenario)

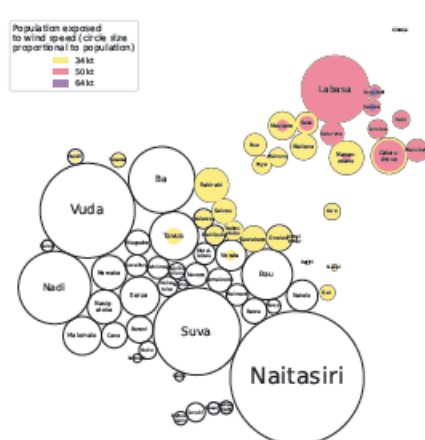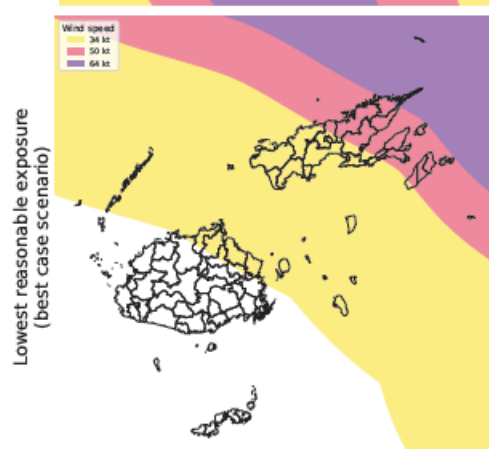



Anticipatory action Fiji – Cyclone Yasa observational information (ACTIVATED)

This is an automated message produced by the OCHA Centre for Humanitarian Data.

This email is purely advisory, and does not serve as an official notice for the anticipatory action framework. Official notices of activation are sent by a separate email. This email also does not constitute an official forecast. Under the World Meteorological Organization's Tropical Cyclone Programme, RSMC Nadi is responsible for monitoring tropical cyclones in the region; the forecast track map published on their website should be treated as authoritative.

Dear colleagues,


The IMERG precipitation data for Cyclone Yasa has been issued by NASA.

Observational trigger: **ACTIVATED**

The plot below shows the 2-day precipitation caused by Yasa. The average precipitation over the whole country is **199 mm**. The trigger threshold is 190 mm, so the observational trigger is **ACTIVATED**.



Cyclone Yasa: 2-day rainfall
Average over whole country: 199 mm

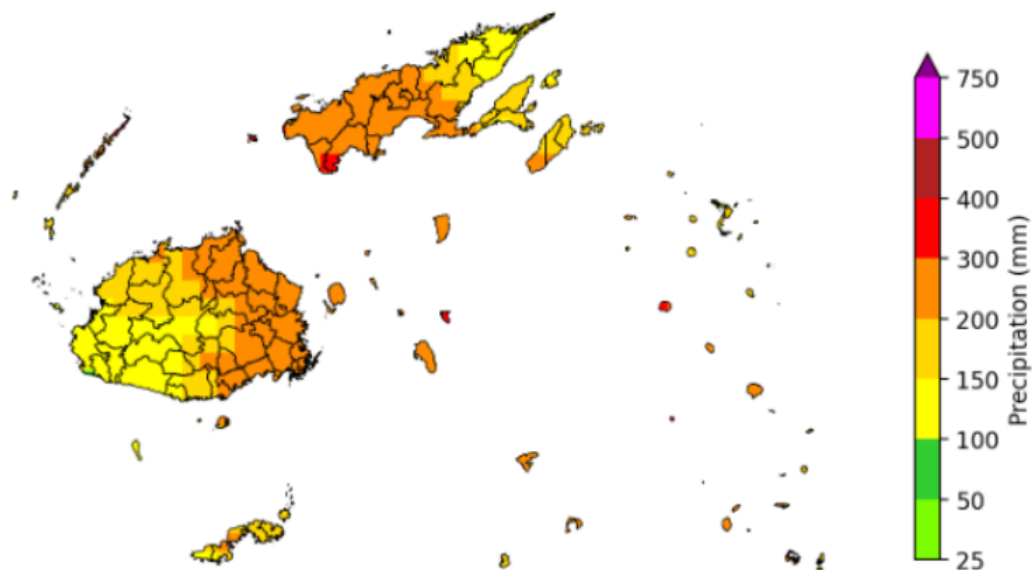

Best wishes,

OCHA Centre for Humanitarian Data

Contact

Contact the OCHA Centre for Humanitarian Data at ocha-datascience@un.org with any questions or feedback.



Annex 7 – Overview of Activities

UN-funded Activities

CERF Chapeau and project proposals can be accessed at cerf.un.org

The most vulnerable households are able to meet their essential needs	Multi-purpose cash	WFP	Ministry of Women, Children and Social Protection; Ministry of Finance	MPC distribution through DSW	<i>75,000 People</i>
Ensure emergency water, sanitation and hygiene supplies to tropical cyclone affected populations	Non-food items (WASH)		Ministry of Health and Medical Services	- Distribution of emergency WASH/Hygiene kits and tarpaulins - Distribution of sanitary pads	
Ensure that children return to safe learning environments and are provided with relevant learning resources to continue their education.	Non-food items (Education)	UNICEF	Ministry of Education	- Distribution and installation of temporary learning centres - Distribution and sensitisation of emergency learning materials	<i>20,000 People</i>
The affected community has access to critical information	Services (Community engagement)		NDRMO/ Ministry of Communication	- Mass Media messages distribution - SMS Blasts	
Women and Girls, women with disabilities have access to essential hygiene items	Non-food items (protection)		Ministry of Women, Children & Poverty Alleviation	Women with Disability Dignity Kits – Prepositioned supplies with DPO, to be distributed as preparedness as soon as disaster path is defined	
Pregnant women have access to clean delivery kits through health facilities	Multipurpose cash (Health)	UNFPA	Ministry of Health & Medical Services	Unconditional Cash for term High-risk pregnant women	<i>2,700 People</i>
Dignity Kit for women & Menstrual	Non-food items (protection)		Ministry of Women, Children & Poverty Alleviation	Distribution of Dignity kits usually intended for one per women aged (18-49) and menstrual health	



hygiene kits for Young Girls

Decreased damage and loss to crops, tools and fishing gears of farmers and fisherfolk

Non-food items

Ministry of Agriculture and Waterways

- Distribution of watertight drums

Decreased damage and loss to boats of fisherfolk

Non-food items

FAO

Ministry of Agriculture and Waterways

- Distribution of Small boat strengthening kits

2,400 People

Farmers and fisherfolk are informed that can take locally led actions

Services (Early warning messages)

NDRMO/ Ministry of Communication/ Ministry of Agriculture and Waterways

- EWM on potential locally led actions

Decreased damage and loss to shelters

Non-food items

Ministry of Rural & Maritime Development and Disaster Management

- Distribution of tie-down kits and tarpaulins, including basic tools and materials for minor works

2,760 People

Evacuation centres management is boosted

Services (Evacuation centre coordination)

IOM/IFRC

Ministry of Rural & Maritime Development and Disaster Management

- Coordination, monitoring and support to Evacuation Centre management in support of NDRMO

Services (Gender and Protection)

UN Women

Ministry of Women, Children and Social Protection

- Gender and protection support and analysis
- Deployment of DSW's Community Services Teams

Cluster coordination

Services (Health)

WHO

Ministry of Health and Medical Services

- Cross-cutting support to the health cluster



Pacific Humanitarian Team
ANTICIPATORY ACTION TWG

Management kits one per young girl aged (10-17)

Fiji Red Cross Early Action Protocol

The Fiji Red Cross Early Action Protocol can be accessed at <https://www.anticipation-hub.org/download/file-5011>



Annex 8 – MoU MWCSP-MoF-WFP

MEMORANDUM OF UNDERSTANDING

BETWEEN

THE UNITED NATIONS WORLD FOOD PROGRAMME (WFP)

AND

THE GOVERNMENT OF THE REPUBLIC OF FIJI

FOR

**TECHNICAL SUPPORT TO THE GOVERNMENT OF FIJI SOCIAL PROTECTION SCHEME FOR THE DELIVERY OF
ANTICIPATORY CASH TRANSFERS TO HOUSEHOLDS AFFECTED BY TROPICAL CYCLONES.**

PREAMBLE

This Memorandum of Understanding (together with all Annexes hereto, this **“MoU”**) is entered into between the Government of the Republic of Fiji by and through its Ministry of Finance and Ministry of Women, Children and Social Protection (MWCSP) (together as **“Government”**), and the World Food Programme of the United Nations (**“WFP”**), having its headquarters in Rome, Italy, acting through its Pacific Multi-Country Office in Fiji (together with Government, the **“Parties”** and each a **“Party”**).

WHEREAS WFP operates in Fiji under the framework of a Basic Agreement entered between the Government of the Republic of Fiji and WFP on 21 August 2018 (the **“Basic Agreement”**).

WHEREAS this MoU shall be read as complementary to the Basic Agreement and the provisions of the Basic Agreement shall apply in their entirety and without exception to this MoU.

WHEREAS the Government and WFP (the **“Parties”**) have entered into this MoU fully accepting and agreeing to abide by the provisions of the Convention on Privileges and Immunities of the United Nations, adopted by the United Nations General Assembly on 13 February 1946 and the Convention on the Privileges and Immunities of the Specialized Agencies and its Annex II, concerning the Food and Agriculture Organization of the United Nations, adopted by the United Nations General Assembly on 21 November 1947, both of which are applicable to WFP.

WHEREAS the Government recognizes WFP’s dual mandate of: (i) saving lives in emergencies and implementing food assistance activities to ensure access to adequate and nutritious food to the most vulnerable worldwide; and (ii) building resilience of vulnerable populations to withstand future shocks. In the context of WFP’s Pacific Multi-Country Office, these mandates are to be realized through strengthening the capacity of the Government of Fiji to prepare for and respond to emergencies, especially using data to better understand and respond to the differentiated impacts of shocks (including climatic shocks) on the food security and nutrition of those most at risk of being left behind.

WHEREAS the parties recognize the importance and value of cooperating with each other towards effective collaborative mechanism. The Parties desire to strengthen their relationship by entering into this MoU with a purpose of providing a coherent and structured framework for collaboration to strengthen government social protection policies, systems and programmes to be shock responsive.



THEREFORE, the Parties have agreed to fully cooperate and act in consultation with each other during this cooperation the manner and accordance with implementation procedures and responsibilities more particularly described in Annexes 1 (the “**Project Document**”) and 2 (the “**Standard Operating Procedures**” or “**SOP**”) for each of the technical areas. Annexes form integral part of this MoU.

The activities described herein for this anticipatory cash transfers through national **Social Protection Schemes and technical support to the Government (the “Operation”)** shall **commence** upon the Government's countersignature and by return of this MoU to WFP.

ARTICLE I

PURPOSE

- 1.1 This MoU establishes the framework for the cooperation between WFP and the Government aimed at ensuring that vulnerable populations have access to multi-purpose cash through anticipatory cash transfers which aim to reduce suffering and losses and protect lives by acting ahead of the shock (the “**Outcomes**”). The multi-purpose cash contributes to ensuring adequate access to food and preventing the deterioration of the nutritional status of affected populations.
- 1.2 Through this MoU, WFP will provide:
- a) technical assistance for rapid cash transfers preparedness of the government social protection transfer mechanisms;
 - b) funds to the Government to cover the Benefits (as defined below) for one tropical cyclone or flooding event which may occur during the Term,

and the Government shall be responsible for:

- c) preparing and enhancing its social transfer mechanism; and
- d) distributing funds provided by WFP with OCHA/CERF funding through anticipatory cash transfers (the “**Benefits**”) to the persons who have been assessed as being eligible to receive Benefits and at risk of a forecasted cyclone which selection criteria are described more particularly in Annexes (the “**Beneficiaries**”) through the Government social protection platform.

ARTICLE II

TERM, AMENDMENT, TERMINATION

- 2.1 This MoU shall commence on the date the last of the Parties signs this MoU (the “**Effective Date**”) and shall continue in full force and effect until **30 June 2027** unless terminated earlier in accordance with Articles 2.3 or 2.4 below. The term of this MoU may be extended, on the same terms and conditions set forth herein, by a formal written agreement signed by duly authorized representative of each Party prior to the expiration of the term.
- 2.2 This MoU may be supplemented or otherwise amended by a formal written agreement signed by duly authorized representatives of each Party.
- 2.3 In the event of the failure by one Party to fulfil any of its obligations under this MoU, the other Party may either (i) suspend the discharge of its own obligations by giving written notice to that effect to the defaulting Party



and/or (ii) terminate the MoU by providing to the defaulting Party thirty (30) days' prior written notice. Notwithstanding the foregoing, WFP shall have the right to terminate the MoU forthwith in accordance with Article 2.4 and, in the event of a material breach of the provisions in Article XII. Article 12.5

- 2.4 WFP or Government of Fiji may terminate this MoU upon provision of ninety (90) days' prior written notice, without having to provide any justification therefor. Notwithstanding the foregoing, WFP may terminate this MoU immediately by providing written notice to the Government in the event that (i) WFP's mandate or the resources available to WFP for the implementation of the Project is curtailed or terminated, in whole or in part, for any reason, including, but not limited to, the non-receipt by WFP of expected funding for the Project or (ii) a material breach of the provisions of Article XII occurs, as further described in Article 12.5.
- 2.5 In the event of the termination of this MoU for any reason, both Parties shall use reasonable efforts and good faith to bring their cooperation herein to a prompt and orderly conclusion. Furthermore, upon termination of this MoU for any reason, any balance of funds received by the Government from WFP and uncommitted as of the date of (i) transmission of the notice of termination by the Government; or (ii) receipt by the Government of the notice of termination by WFP, as applicable, as well as any funds not spent in accordance with the terms of this MoU, including, without limitation, any amounts recoverable by WFP in accordance with Article XII, shall be promptly returned to WFP.

ARTICLE III

JOINT RESPONSIBILITIES OF THE PARTIES

- 3.1 The Parties will cooperate proactively and constructively in all the covered areas of cooperation with respect to:
- e) Joint work planning and identification of the potential risks and mitigation measures throughout the process of planning and implementation of the anticipatory action framework.
 - f) Coordination among Parties, as well as with potential other actors that carry out relevant interventions.
 - g) Joint reviews of the progress, identification of bottlenecks and finding solutions to address them.
- 3.2 The Parties will participate in regular joint Management and Monitoring Team (MMT) meetings which will oversee the implementation of this MoU and address any issues arising. The MMT consists of the Minister of Women, Children and Social Protection or his/her designate and the WFP Representative and Country Director or his/her designate. The meetings will be convened by the Government every two (2) weeks or as necessary after the signing of the MoU.

ARTICLE IV

OBLIGATIONS OF THE GOVERNMENT

- 4.1 The Government:
- a) hereby designate the Ministry of Women, Children and Social Protection as the executing agency for this Operation generally (the "**Executing Agency**") and to act as the channel of communication between the Government and WFP for the purpose of this MoU;
 - b) shall provide resources for the implementation of the Operation for the duration of the MoU in the areas of its responsibilities generally, and in particular, through the Ministry of Finance, make funds available and ready for distribution within and by the Executing Agency in a timely manner upon the Activation Trigger Event (as defined below);



- c) determine the readiness and activation triggers for anticipatory cash transfers with United Nations Office for the Coordination of Humanitarian Affairs (“**OCHA**”) and declare and communicate to others, including WFP, when the triggers are met in accordance with the Project Plan and the “Trigger Statement” section of the SOP (the “**Readiness Trigger Event**” and “**Activation Trigger Event**” respectively). For the purpose hereof the Government will be represented through its National Disaster Management Office and Fiji Meteorological Services and OCHA, through its Centre for Humanitarian Data; and
- d) shall deliver the anticipatory cash transfers to the Beneficiaries using the existing mechanisms and financial services providers of the social protection programmes (the “**FSPs**”) within the agreed timelines, in accordance with the “**Project Document**” (Annex 1) upon the Activation Trigger Event.

4.2 In particular, without prejudice to any other obligations set forth elsewhere in this MoU, the Government shall:

- a) Designate a Ministry of Finance Fijian Dollar bank account, approved by WFP, to deposit and maintain the funds received from WFP earmarked as Benefits until such funds are utilized (the “**Programme Account**”). The Government shall not create or permit to subsist any mortgage, lien, charge, hypothecation, encumbrance or security interest or any other agreement or arrangement having the effect of conferring security over the Programme Account. The Government shall be responsible for any losses, financial or otherwise, and for ensuring that the funds provided by WFP are properly received, accounted for and transferred to the Beneficiaries or returned to WFP, as the case may be;
- b) apply the funds provided by WFP hereunder exclusively for distribution to the Beneficiaries as Benefits and transfer fees to FSPs as indicated in Estimate Budget (as defined below) and shall take measures to prevent the unauthorized use of funds by those persons and parties Government is responsible under this MoU.
- c) Facilitate joint planning, supervision, monitoring and evaluation and provide overall oversight of the activities under its responsibility as agreed upon in this MoU.
- d) Capture and register complaints and feedback from Beneficiaries and third parties using its Community Feedback Mechanisms (the “**CFM**”) and ensure timely response to the registered complaints and feedback;
- e) Identify overall implementation issues, risks, and gaps likely to impact the implementation of activities under this MoU and work towards achieving the Outcomes while mitigating identified risks to the extent possible;
- f) Coordinate the availability of complementary interventions and quality coverage of the activities implemented under this MoU to maximize the Outcomes;
- g) Promote the active participation of and coordination with relevant district and lower-level decentralised authorities in the activities under this cooperation, as well as, where relevant, local communities;



- h) Provide suitably qualified personnel and the adequate means necessary for the implementation and supervision of the activities under the Government's responsibility as agreed upon in this MoU;
- i) Provide its social benefits transfer framework to deliver the Benefits to the Beneficiaries, including using and managing its FSPs and any other services required for project preparation, implementation and management, including but not limited to, needs assessments, capacity building activities, monitoring, and evaluation;
- j) Carry out roles and implement activities assigned to it under this MoU and such other activities as needed to deliver upon the outputs under its responsibilities,
- k) Ensure visibility of WFP's support through this Operation as well as that of any donor to WFP to be communicated to the Government. This should include, at a minimum, the use of regular Government communication channels for the implementation of its social assistance programmes;
- l) Ensure that tasks are carried out in accordance with the principles and objectives underlying the WFP Gender Policy (Annex 7);
- m) Provide anticipatory cash transfers to all targeted Beneficiaries with complete impartiality regardless of race, religion, nationality, political opinion, or gender, and acknowledge that projects supported by WFP do not include any activities intended to promote a specific religious or political faith or persuasion; and
- n) Carry out its obligations in accordance with humanitarian principles, including the principles of humanitarian protection set forth in WFP Humanitarian Protection Policy (Annex 8).

4.3 Notwithstanding any other provision, the Government shall be fully responsible for its acts and omissions and its employees. For the avoidance of doubt, all activities assigned to the Government, be it to any of its ministries, departments, offices and services named in this MoU, shall be deemed responsibilities, acts and omission of the Government and WFP may rely on any notice (as defined in Article XI), instructions and agreements from, by and with any such entity as those of the Government. Unless otherwise specified in this MoU, all activities and responsibilities of the Governments are designated to the Executing Agency. Further, activities assigned to or implemented by the Government's contractors (such as FSPs) and other third parties on behalf of the Government ("**Government Contractors**") shall be considered activities and parties under the responsibility of the Government. The personnel of WFP do not have the status of staff members or employees of the Government;

ARTICLE V

OBLIGATIONS OF UNITED NATIONS WORLD FOOD PROGRAMME

Without prejudice to any other obligations set forth elsewhere in this MoU, and subject to availability of resources, WFP shall:

- 5.1 Make funds available in the estimated budget set out in Annex 3 hereto (the "**Estimated Budget**") but in any event up to the maximum of **USD 1,385,000** (one million, three hundred and eighty five thousand United States



Dollars) or its equivalent in Fiji Dollars (FJD) using prevailing the UN Operational Rate of Exchange applicable at the time of transfer and transfer the same into the Programme Account for the purpose of providing funding to the Government for its anticipatory cash transfer to the Beneficiaries upon the Activation Trigger Event in accordance with Clause 7.1.

- 5.2 Inform the Government of any known or anticipated problems in the availability of funds; where appropriate, assist the Government in minimizing risks resulting from such an event.
- 5.3 Provide suitably qualified personnel and the adequate means necessary for the implementation and technical support of the activities under its responsibilities agreed upon in this MoU.
- 5.4 As applicable, cooperate with the Government and any other parties involved in the implementation of the activities under this MoU, and coordinate, together with the Government, the activities implemented by any parties involved in the activities under this MoU to maximise outcomes.
- 5.5 Provide technical assistance and guidance on anticipatory action cash transfers preparedness of the existing social protection mechanisms, including training, where necessary, for Government staff on the planning, development, and implementation of the anticipatory action framework designed and agreed by the Government of Fiji, WFP, and other humanitarian partners.

ARTICLE VI

REPORTING, MONITORING EVALUATION AND AUDIT

- 6.1 The Government shall maintain separate and proper records and accounts of all resources provided by WFP under this MoU including:
 - a) the funds earmarked as Benefits received from WFP and disbursed in accordance with the accounting procedures and financial guidelines set out in the Project Document;
 - b) any funds not disbursed; and
 - c) any costs incurred,in each case, in a manner that shall enable the Government to substantiate its utilization of resources in accordance with the terms of this MoU.
- 6.2 The Government shall provide to WFP accurate and timely cash assistance transfer and financial reconciliation reports and in the form set forth in Annexes 4 and 5 to be submitted within thirty (30) days after (i) completion of the anticipatory cash transfers or (ii) the Activation Trigger Event date. The part of such reports covering the cash transfers shall include:
 - a) the number of Beneficiaries to whom Benefits were disbursed, disaggregated by gender, age and geographic location, including the value of Benefits provided to each Beneficiary; and
 - b) narrative information highlighting cash assistance transfers arrangements, timeliness of distribution, any challenges and measures taken to overcome them, successes and/or recommendations related to the implementation of the activities under this MoU.
- 6.3 The Government shall provide WFP with copies of all relevant records, documents, statements, and other information as WFP may request in relation to the fulfilment by the Government of its responsibilities under this MoU. The Government shall retain all such records, documents, statements, and other relevant information for a period of five (5) years from the termination or expiration of this MoU. The Government shall fully cooperate and shall ensure that its officers, employees, agents, contractors, and subcontractors fully cooperate with WFP



by complying with all reasonable requests from WFP to gain access to and review any such records, documents, statements, and other relevant information.

- 6.3 WFP may undertake, with the cooperation of the Government and as appropriate in collaboration with other United Nations agencies, including OCHA, evaluation, management, or technical review missions in order to assist in monitoring the progress of the Operation. The Government shall afford authorized representatives and agents of WFP the opportunity at all reasonable times to make field visits related to the activities undertaken by the Government hereunder. The Government shall ensure that its officers, employees, agents, contractors, and sub-contractors fully cooperate with the execution of any evaluation of the Operation conducted by or on behalf of WFP.
- 6.4 Subject to WFP's internal rules and regulations, WFP and the Government may jointly undertake, as necessary, the preparation of baseline data, assessment and monitoring as well as evaluation reports concerning areas where the Government operates under this MoU. Notwithstanding the foregoing, WFP may, in its sole discretion and subject to its internal rules, provide the Government with baseline data, assessment and monitoring as well as evaluation reports concerning areas where the Government operates under this MoU.

ARTICLE VII

PAYMENTS

- 7.1 Following the satisfaction of the following conditions precedent, WFP shall transfer the funds, in a single instalment, in the amount stated in Article 5.1 in accordance with the timeline set out in the SOP:
- a) the Effective Date has occurred;
 - b) the Government has delivered original copy of the MoU signed by it to WFP;
 - c) The Activation Trigger Event has been declared and communicated, in accordance with Article 4.1(c).
- 7.2 All disbursements of funds from WFP to the Government shall be made in the Fijian Dollars specified in the Estimated Budget into the Programme Account, detailed of which are as follows:
- Account Name: Government Central Account
Bank Name: Reserve Bank of Fiji
Bank Address: Pratt Street, Suva
Account Number: 31501
Swift Code: RBFJFJF
- 7.3 The Government shall proceed to disburse the anticipatory cash transfers to the targeted Beneficiaries following the Activation Trigger Event within the timeline specified in the SOP. The Government's obligation hereunder is notwithstanding whether WFP's funds have been credited to the Programme Account.
- 7.4 No later than sixty (60) days following the transfers of Benefits to Beneficiaries are made or the Activation Trigger Event, the Government shall refund to WFP in the same currency as it has received from WFP any and all undistributed Benefits and associated withdrawal fees, as well as any other unused funds provided by WFP under this MoU. The Government shall, as necessary, put in place adequate contractual requirements with other relevant parties to ensure satisfaction of this obligation.
- 7.5 Without prejudice to article 7.4, immediately upon the expiration, termination or suspension of this MoU, and in any event, no later than thirty (30) days following the occurrence of any such event, the Government shall



return to WFP any portion of payment received from WFP hereunder not spent or spent but not in accordance with the terms of this MoU, including, without limitation, any amounts recoverable by WFP in accordance with Article XIII. The Government shall refund in the same currency as it has received from WFP.

- 7.6 The Government acknowledges and agrees that all payments hereunder are financed with the resources of donor governments or organizations and that, notwithstanding any other provision of this MoU, WFP's financial commitments, including its payment obligations, under this MoU shall not exceed the amounts specified in the Estimated Budget and is subject to WFP having received funds from such donors and organisations for the purpose of this Operation.
- 7.7 In the event that WFP is unable to, as a result of the unavailability of funds, provide the Government with resources in the full amount specified in this MoU, WFP shall provide written notice of such event to the Government without undue delay.
- 7.8 Any payments to WFP from the Government hereunder shall be made into the WFP bank account with the following specifications:

Account Name:	WORLD FOOD PROGRAMME FIJI IMPREST FJD
Account Type:	Business Cheque Account
Bank Name:	WESTPAC BANK
Branch Name:	WESTPAC Suva, 1 Thompson Street Suva
Account Number:	9808124573
Swift Code:	WPACFJFX

ARTICLE VIII

LIABILITY AND INDEMNIFICATION

- 8.1 The Parties shall work together to prevent any losses associated with the activities envisaged in this MoU. The Government shall make good any loss directly attributable to the Government (including to the Government Contractors), including any losses incurred under Article XIII, and shall reimburse such losses to WFP, whether in kind or in the equivalent monetary value prevailing at the time of the loss, in either case, as WFP shall be entitled to select in its sole discretion.
- 8.2 The Government shall be responsible for dealing with all claims in Fiji arising from or directly attributable to the activities under this MoU, or any other supplemental agreement, that may be brought by third parties against WFP, its officers, employees, agents, contractors and sub-contractors and shall pay compensation in accordance with its national law, in respect of such claims and shall indemnify and hold harmless WFP, its officers, employees, agents, contractors and sub-contractors, except where the Parties agree that the particular claim or liability was caused by gross negligence or willful misconduct on the part of WFP.
- 8.3 Without prejudice to Article 8.1 and 8.2, the Government shall assume full legal responsibility for the safekeeping, handling and management of the funds provided to it by WFP under this MoU, whether such funds are held by the Government or any Government Contractor. The Government shall assume sole liability for any losses occurring at any stage from the time at which funds are deposited by WFP into the Programme Account until such time as such funds are disbursed to the Beneficiaries in accordance with the terms of this MoU, including any losses resulting from any breach of any provision in this MoU, as well as any acts, omissions or negligence attributable to the Government, its officials, employees, agents, contractors and sub-contractors.



The Government shall be responsible for reimbursing any loss to WFP subject to WFP's request. For the purpose hereof, the funds are deemed disbursed to the Beneficiaries, upon crediting of Benefits to Beneficiaries' own accounts for cash transfer using mobile money wallets and bank accounts, and actual receipt of Benefits in cash by the relevant beneficiaries for cash transfer using the postal service.

- 8.4 WFP shall not assume responsibility or liability for any loss or damage, including any indirect or consequential loss or damage, arising out of this MoU or any agreement entered pursuant hereto unless such loss or damage is attributable to gross negligence or willful misconduct on the part of WFP.

ARTICLE IX

COMMUNICATIONS, CONFIDENTIALITY AND DATA PROTECTION

- 9.1 WFP may provide its donors as well as other third parties as required under its internal rules and regulations with relevant information relating to this MoU, its contents and its implementation, as well as copies of reports and financial statements received from the Government hereunder.
- 9.2 In all other cases, the Parties shall communicate each other's role to the general public as agreed in each case by the Parties. This may include, without limitation, the display by the Government of WFP visibility and/or communication materials as requested by WFP from time to time.
- 9.3 Notwithstanding Article 9.2, neither Party shall make or issue any public statements, press releases, or communications regarding the collaboration of the Parties or any of the activities governed by this MoU without consultation with, and the prior written consent of, the other Party, as regards the contents of such public statement, press release or communication.
- 9.4 Without prejudice to WFP's right under Article 9.1, each Party shall maintain the confidentiality of any non-public information pertaining to or provided by the other Party hereunder, including information relating to any activities governed by this MoU. Each Party shall use such information only for purposes of this MoU and not for any commercial or private advantage. Notwithstanding the foregoing, the Government may disclose select information to contractors solely to the extent necessary for the purposes of the implementation of the activities envisaged under this MoU and the distribution of the Benefits, provided that such contractors are subject to a duty of confidentiality no less restrictive than those referred to in this Article 9.4. These obligations shall survive any suspension, termination or expiration of this MoU.
- 9.5 The Parties shall ensure that any personal data of Beneficiaries of the Project will be processed in accordance with the Data Processing Conditions set out in Annex 6.

ARTICLE X

FORCE MAJEURE



- 10.1 The term force majeure as employed herein shall mean any unforeseen event beyond the control of the Parties, which makes the performance of obligations under this MoU impossible in whole or in part, and which reasonably justifies the suspension or termination of this MoU, in whole or in part.
- 10.2 Neither Party shall be considered to be in breach of this MoU to the extent that performance of an obligation under it is prevented by a *force majeure* event, which shall be notified to the other Party no later than fourteen (14) days from the date of the beginning of the occurrence of such event. The Party to which notice of the *force majeure* event has been provided shall be relieved of the corresponding reciprocal obligations, it being understood by the Parties that the existence and/or applicability of the claimed *force majeure* event may be disputed under the procedure set forth in Article XV hereof. For the avoidance of doubt, occurrence of a tropical cyclone, is not a force majeure event.

ARTICLE XI

NOTICES

- 11.1 Unless otherwise agreed, any correspondence, notification, report, request or other communication (each a “notice”) to be provided by one Party to the other in connection with this MoU shall be made in writing. Any notice required to be given herein shall be deemed to have been provided if served by personal delivery, courier, recorded delivery, registered post, facsimile or e-mail, at the address, e-mail address or facsimile number of the focal point of the recipient Party, as applicable, as specified in Article 11.2.
- 11.2 The focal point for each Party for purposes of this MoU shall be as set forth below. Any changes in connection with the focal point designation of either Party shall be promptly notified to the other Party no later than three (3) days following the date on which such change shall have occurred.

For the Government

Name: Eseta Nadakuitavuki

Title: Permanent Secretary

Address: Civic Tower, Level 5, Victoria Parade
Suva

E-mail: eseta.nadakuitavuki@mwcs.gov.fj

For WFP

Name: Emma Conlan

Title: Deputy Country Director and
Representative

Address: WFP Pacific, Level 2, Ra Marama
House, Gordon Street, Suva, Fiji

E-mail address: emma.conlan@wfp.org

ARTICLE XII

ANTI-FRAUD AND ANTI-CORRUPTION

- 12.1 Each Party hereby affirms that it is highly risk averse towards fraud; corruption; theft; collusive, coercive and obstructive practices; money laundering; and financing of terrorism as such terms are defined in WFP’s Anti-



Fraud and Anti-Corruption Policy (collectively, the “Prohibited Practices”) in its activities and operations and has zero tolerance for inaction. Each Party has the duty to act honestly and with integrity in the course of implementation of this MoU. It is understood that the Government agrees to maintain standards of conduct governing the performance of its officers, employees, contractors, sub-contractors, agents and affiliates, including the prohibition of Prohibited Practices in connection with the granting and administration of any resources provided pursuant to this MoU.

- 12.2 The Government affirms its knowledge and acceptance of the general principles and objectives underlying WFP’s Anti-Fraud and Anti-Corruption Policy, as amended from time to time and undertakes to communicate such principles to its officers, employees, contractors and sub-contractors, agents and affiliates and shall take all reasonable measures to ensure that such persons or entities do not engage in Prohibited Practices. The Government shall include appropriate anti-fraud and anti-corruption provisions in any sub-contract or sub-agreement entered into by the Government pursuant to this MoU.
- 12.3 The Government will act on all reasonably suspected cases of any Prohibited Practice. In particular, it shall promptly disclose to WFP any reasonably suspected Prohibited Practice or any attempt thereof.
- 12.4 WFP shall have the right to conduct its own investigation of any reasonably suspected Prohibited Practice. In such event, the Government shall fully cooperate with WFP or its agents and shall take all necessary measures to ensure that its officers, employees, agents and affiliates, contractors and sub-contractors fully cooperate with any such investigation conducted by WFP or its agents, including by providing WFP or its agents all relevant information, records, documentation and premises.
- 12.5 The Parties hereby expressly acknowledge and agree that in the event that the Parties were to determine, through an investigation conducted in accordance with Article 12.3, Article 12.4 or otherwise, that a Prohibited Practice has occurred, such event shall constitute a material breach of this Article XII. In all such cases, WFP shall be entitled to immediately terminate this MoU in accordance with Article 2.4 and recover all losses, financial or otherwise, suffered by WFP in connection with such Prohibited Practice, including by withholding relevant amounts from any subsequent disbursements, and take any other actions in accordance with WFP internal rules and regulations as may be deemed necessary or appropriate.

ARTICLE XIII

ANTI-TERRORISM

- 13.1. Consistent with numerous United Nations Security Council resolutions relating to terrorism and in particular, the financing of terrorism, WFP and the Government shall seek to ensure that none of the resources received under this MoU, whether in cash or in kind, is used, directly or indirectly, to provide support to terrorist entities or individuals.
- 13.2. In accordance with this policy, the Government agrees to employ all reasonable efforts to ensure that none of such resources (a) is knowingly transferred directly or indirectly or otherwise used to provide support to any individual or entity associated with terrorism as designated on the list maintained by the Security Council Committee established pursuant to Security Council Resolution 1267 (1999) and 1989 (2011) (available at <http://www.un.org/Docs/sc/committees/1267/1267ListEng.htm> or any other similar lists that may be established by the United Nations Security Council, including the list of individuals and entities maintained by the Security Council Committee established pursuant to resolutions 751 (1992) and 1907 (2009) concerning Somalia and Eritrea; and/or (b) is used in any other manner that is prohibited by a resolution of the United Nations Security Council adopted under Chapter VII of the Charter of the United Nations.



ARTICLE XIV

PREVENTION OF SEXUAL EXPLOITATION AND ABUSE

- 14.1 The United Nations and WFP are committed to the protection of vulnerable populations in humanitarian crises, including from sexual exploitation and abuse. By entering into an MoU with WFP, the Government undertakes to adhere to: (i) the standards set out in the Secretary-General's Bulletin Special measures for protection from sexual exploitation and sexual abuse (ST/SGB/2003/13); (ii) any minimum operating standards adopted as a result of the Statement of Commitment on Eliminating Sexual Abuse and Abuse by UN and Non-UN Personnel of 4 December 2006; and (iii) any other Protection from Sexual Exploitation and Abuse (PSEA) policy or guidelines as may be adopted by WFP, as notified to the Government by WFP from time to time.
- 14.2. The Government shall ensure that its personnel, agents, contractors and subcontractors conform to the highest standards of moral and ethical conduct. Any failure by the Government to take preventive measures against sexual exploitation or abuse, to investigate allegations thereof or to take corrective action, shall constitute grounds for termination of the MoU.

ARTICLE XV

PRIVILEGES AND IMMUNITIES

- 15.1. Nothing in this MoU or any agreement and/or document entered into in connection with this MoU shall (i) imply a waiver, express or implied, by WFP, the United Nations and the Food and Agriculture Organization of the United Nations of any privileges or immunities enjoyed by them pursuant to the 1946 Convention on the Privileges and Immunities of the United Nations, the 1947 Convention on the Privileges and Immunities of the Specialized Agencies, customary international law, other relevant international or national agreements, or under domestic law or (ii) confer any such privileges or immunities on the Government or any of its officers, employees, agents, contractors or sub-contractors.

ARTICLE XVI

SUBCONTRACTING; PROCUREMENT

- 16.1 In the event that the procurement of goods and/or services are required to be made by the Government pursuant to this MoU, all necessary procurement actions to be taken in connection therewith shall be carried out in accordance with the Government's applicable procurement policies and procedures and in a manner consistent with internationally accepted procurement standards.
- 16.2 In the event that the Government requires the services of contractors or sub-contractors to perform any obligations under this MoU, the Government shall obtain written approval from WFP prior to entering into any sub-contracts or sub-agreements. WFP shall be entitled, in its sole discretion, to review and approve, where appropriate, the qualifications of any prospective contractor or sub-contractor for purposes of this MoU.
- 16.3 The terms and conditions of any sub-contract or sub-agreement entered into by the Government pursuant to this MoU shall be fully consistent with the terms and conditions of this MoU. The Government shall ensure that provisions analogous to those contained in this MoU, including, without limitation, the provisions of Articles VI, IX, XII and XIII hereof, are included in any such sub-contract or sub-agreement.

ARTICLE XVII

APPLICABLE LAW AND SETTLEMENT OF DISPUTES



- 17.1. The interpretation, construction and performance of this MoU, including any agreements and/or documents entered into in connection with this MoU, and any claims, controversies or disputes arising hereunder or there under shall be exclusively governed by general principles of international commercial law and the terms and conditions of this MoU, to the exclusion of national law.
- 17.2. Any claims, controversies or disputes between the Parties arising out of or relating to this MoU or under any agreements and/pr documents entered into in connection with this MoU, shall be settled in accordance with the provisions of the Basic Agreement.

ARTICLE XVIII

OTHER PROVISIONS

- 18.1 The Parties shall carry out all their respective responsibilities in relation to this MoU in a proper, faithful, diligent, timely, efficient and professional manner.
- 18.2 The Parties are committed to ensuring that their personnel and the personnel of any third parties appointed in the framework of the activities contemplated under this MoU adhere to their respective codes of conduct and/or to other internationally accepted principles of accountability.
- 18.3 The collaboration between the Parties envisaged hereunder is non-exclusive and shall not preclude either Party from engaging in, or collaborating with third parties on, other activities such as those covered in this MoU.
- 18.4 This MoU shall not constitute a legal partnership, representation, alliance, joint venture, association or company of any sort between WFP and the Government or any other person, and shall not impose any obligations and/or responsibilities on the Parties except such obligations and responsibilities as are expressly stipulated herein.
- 18.5 Nothing contained in or relating to this MoU shall be construed as creating or establishing between the Parties the relationship of employer and employee or of principal and agent. The officers, employees, agents, representatives, contractors or sub-contractors of each of the Parties shall not be considered in any respect as being the employees or agents of the other Party.
- 18.6 This MoU comprises the main body of this MoU as well as all the Annexes attached hereto, which together constitute the entire agreement between the Parties in respect of the Project. Each of the documents comprising this MoU is an essential part of the agreement between the Parties, and a requirement occurring in one is as binding as though occurring in all. The documents comprising this MoU are intended to be complementary to each other and to describe and provide for a complete agreement. In the event of any conflict among the documents comprising this MoU, the order of precedence shall be as set forth below.
- (a) the main body of this MoU;
 - (b) the Project Document (Annex 1);
 - (c) the Plan of Operations and Standard Operating Procedures (Annex 2)
 - (c) the Estimated Budget (Annex 3); and
 - (d) all other Annexes.
- 18.7 Each provision under this MoU is severable and distinct. In the event that any provision in this MoU is held to be invalid, illegal or unenforceable, such invalidity, illegality or unenforceability shall not affect the validity, legality and enforceability of any other provision in this MoU.



- 18.8 Any provision of this MoU, including, without limitation, the provisions of Articles VI, IX, XV and XVII, which contemplate performance or observance subsequent to any suspension, termination or expiration of this MoU shall survive any suspension, termination or expiration of this MoU and shall continue in full force and effect.

IN WITNESS WHEREOF the undersigned, being duly appointed representatives of the Parties, have on behalf of the Parties signed this MoU as confirmation of the terms and conditions contained herein.

Signed at Suva, Fiji on 2026

For the Government:

For WFP:

MINISTRY OF FINANCE

Name:

Name:.....

Designation:

Designation:

Signature:

Signature:

MINISTRY OF WOMEN, CHILDREN



AND SOCIAL PROTECTION

Name:

Designation:

Signature:



ANNEX 1:
Project Document

**WFP TECHNICAL SUPPORT ON ANTICIPATORY CASH TRANSFERS USING THE GOVERNMENT OF FIJI SOCIAL
PROTECTION SCHEME DELIVERY MECHANISM**

**A CERF funded Anticipatory Action project with technical support from the United Nations World
Food Programme**

December 2025



Pacific
Humanitarian
Team
ANTICIPATORY ACTION TWG



Table of Contents

List of abbreviations	71
Background.....	72
Project Summary	72
Life-Saving Justification	73
Objectives and Expected Outcome	73
Implementation arrangements	73
Project Activities.....	74
Anticipatory cash transfers.....	74
Flow of funds	74
Transfer value.....	74
Cash assurance	74
Geographical targeting and beneficiary selection.....	75
Capacity strengthening.....	75
Communication with communities	75
Emergency preparedness and system strengthening	75
Monitoring and learning.....	75
Partnerships and coordination	76
Roles and Responsibilities	76
National Disaster Management Office	76
Ministry of Finance	76
Ministry of Women, Children and Social Protection.....	76
United Nations World Food Programme.....	77
Cross Cutting Issues	77
Accountability to Affected Populations.....	77
Gender	77
Gender-based violence.....	77
Disability Inclusion.....	77
Project Timeframe	78
Operational Presence and Access	79



List of abbreviations

AA	Anticipatory Action
AAR	After-action-review
BNPL	Basic Needs Poverty Line
CERF	United Nations Central Emergency Response Fund
CFM	Community Feedback Mechanisms
DRR	Disaster Risk Reduction
DSW	Department of Social Welfare, MWCSP
FAO	Food and Agriculture Organization of the United Nations
FCWG	Fiji Cash Working Group
FJD	Fijian Dollars
FMS	Fiji Meteorological Services
G2P	Government-to-Person
MWCSP	Ministry of Women, Children and Social Protection
OCHA	Office for Coordination of Humanitarian Affairs
NDMO	National Disaster Management Office
FMS	Fiji Meteorological Services
PAAW	Pacific Anticipatory Action Week
SMS	Short Message Service
UN	United Nations
UNFPA	United Nations Population Fund
UNICEF	United Nations Children's Fund
WFP	United Nations World Food Programme



Background

Tropical cyclones have disproportional impacts on small island states like Fiji. In its National Adaptation Plan, Fiji underscored its vulnerability to tropical cyclones which due to climate change are expected to increase in intensity. However, thanks to the advances in forecasting and early warning systems, the likelihood, intensity and impacts of tropical cyclones have become increasingly predictable. Following lessons learned and recommendations from the Tropical Cyclone Winston response in 2016, the Government of Fiji has been committed to the development of shock responsive social protection policies, systems and programmes, through review of existing and development of new disaster management policies. With assistance from the World Bank, the Government is in the process of developing an adaptive social protection policy that will guide the implementation of shock responsive social protection initiatives.

Over the past years, the global humanitarian community has developed a concept of Anticipatory Action (AA)²⁷ that builds on existing Disaster Risk Reduction (DRR) frameworks to enable actions and financing to be triggered based on forecast of impending climate-induced shocks rather than reacting to their impact. There is growing evidence that providing assistance prior to the onset of a predictable shock is lifesaving, dignified and more cost-effective than reacting to loss and damages post shock. In addition, an anticipatory approach can also protect development gains. There are three key building blocks of AA: (i) forecasting, (ii) pre-agreed actions and (iii) pre-arranged financing. It is important that governments and its partners agree on thresholds, triggers, actions, and financing modalities to ensure that AAs are timely, effective and reduce vulnerabilities of the affected population. This agreement – outlined in the Anticipatory Action Plan – forms the basis of commitments to fund disbursement from OCHA/CERF to WFP and the Government of Fiji and is reflected below in the flow of funds.

The Pacific Anticipatory Action Week (PAAW) (28 to 30 March 2023) brought together 15 governments represented by National Disaster Management Office of Fiji (NDMO), Fiji Meteorological Services (FMS) and partners to advance AA in the Pacific. During this meeting, the Government of Fiji and operational partners showed great interest to pilot a collective AA framework for tropical cyclones. Following the PAAW, the United Nations (UN) Resident Coordinator in May 2023 requested the Under-Secretary-General for Humanitarian Affairs and Emergency Relief Coordinator to provide support for piloting AA in Fiji. OCHA confirmed this support, including pre-arranged financing from the United Nations Central Emergency Response Fund (CERF) of up to US\$1 million should pre-agreed triggers for tropical cyclones be met for the first two years 2023-2025. The pilot was reviewed and has now been agreed to be extended for another two years 2025-2027.

The establishment of a pilot AA framework for tropical cyclones in Fiji takes place within a broader effort for disaster risk management, including the United Nations Secretary-General's Early Warning for All Initiative for which Fiji is a priority country. Efforts will also be undertaken to include especially vulnerable communities in the design of the framework. In addition to ensuring adequate access to food and preventing the deterioration of the nutritional status of affected populations through anticipatory cash transfers, the purpose of this pilot is to test AA viability in the Pacific Region with the aim of establishing it as a regular operational approach for social protection assistance in shock-prone states and islands in the region.

Project Summary

The Government, in partnership with WFP, will support at-risk communities by vertically expanding social protection benefits with unconditional anticipatory cash transfers as a measure to help people to mitigate the impact of tropical cyclones. To ensure fast and efficient assistance before the tropical cyclone strikes, the cash transfers will use Government's existing social protection programmes payment systems and reinforce national and local capacities to prepare for, respond to and withstand future shocks through social protection systems. In consultation with the Government, its existing transfer mechanisms that include mobile money, bank transfers and post office cash vouchers will be assessed to identify any assurance risks and potential challenges for rapid cash transfers to the right people with the right amount, and to the extent possible, risk mitigation measures will be put in place to ensure preparedness and assurance of these instruments.

With funding from CERF, the Government and WFP will support existing Department of Social Welfare (DSW) beneficiaries of the Government's national social protection programmes, as more particularly described under the section headed "Project Activities" (Beneficiaries) through AA cash transfers. Beneficiaries will receive an unconditional and unrestricted cash assistance before cyclones hit to ensure that their immediate food and other essential needs can be met in local markets and emergency

²⁷ Anticipatory Action (AA) refers to actions triggered before a crisis to mitigate the worst effects of the crisis, or even avoid crisis altogether. It is a rapidly growing concept used in humanitarian aid, climate change and disaster, and climate finance.



preparedness actions such as evacuation, and reinforcement of their dwellings before the tropical cyclone strikes.

Life-Saving Justification

The proposed anticipatory cash transfers will save lives by helping people to prepare for and mitigate the impact of tropical cyclones. The anticipatory cash transfer will also support the long-term recovery of the affected populations by stabilizing their livelihoods, preventing them from turning to negative coping strategies such as selling of productive assets, and by stimulating local markets and economies.

The proposed anticipatory cash transfers fall within the life-saving mandate of the CERF as follows:

- a) The anticipatory cash transfers helps to meet immediate food security needs and other essential needs at the onset of tropical cyclones, such as covering costs of evacuation or reinforcement of recipients' dwelling.
- b) The anticipatory cash transfers will be provided in a manner that is consistent with humanitarian principles of humanity, neutrality, impartiality, and independence.

Cash will be transferred to people at risk of the tropical cyclones at confirmation of activations triggers and before the forecasted landfall. The Government of Fiji and WFP recognise the potential that a forecasted storm landfall might not actually occur – as weather-related hazards can never be predicted with full certainty. However, given the low likelihood of this due to predictability of the hazards to be addressed and the high impact on lives and livelihoods – this recognised risk is considered to be mitigated by sound Anticipatory Action Plan design and the prioritisation of life saving assistance.

Objectives and Expected Outcome

The primary objective of the project is to achieve food security outcomes and emergency preparedness for the forecasted affected population. The proposed approach also supports the national Government's leadership and commitment in anticipating the emergency, as well as the national social protection systems to become more shock responsive, and while also strengthening existing Government social protection programme.

In view of Fiji's resilient markets, and the existence of effective nationwide social protection schemes, WFP's food security intervention through this Project, by supporting the Government in its anticipatory cash transfers, as the best approach to achieve national objectives and in so doing:

- (i) address the immediate food and other essential needs of some of the poorest and most vulnerable members of society;
- (ii) limit their adoption of negative coping strategies such as selling of productive assets;
- (iii) enable them to purchase food of their choice locally, and in so doing, help strengthen local markets;
- (iv) prepare for the cyclone by evacuating from their house to evacuation center, moving their livestock to safer place, or reinforcing their dwellings.
- (v) strengthen the Government's emergency response capacity and national social protection systems; and
- (vi) generate evidence to inform future AA in Fiji and the Pacific region.

Implementation arrangements

Through the DSW under the Ministry of Women, Children and Social Protection (MWCSPP), the Government will provide leadership for the development and implementation of the Project and shall be responsible for ensuring that the funds provided by WFP are properly received, transferred to beneficiaries in timely manner, and thoroughly accounted for. The Government's responsibility for the Project will include the provision of suitably qualified personnel and the adequate means necessary for the implementation and supervision of the activities under the Government's responsibility throughout the project. The government social protection programme payment system to be used for the transfer of WFP funds shall continue to be managed by the Government.

WFP, through its Pacific Office, Regional Bureau for Asia and the Pacific and Headquarters, will leverage its human resources and technical expertise in social protection, cash-based transfers, and research, assessment and monitoring to ensure provision of quality advisory to the Government for the Project. WFP will provide support for optimization of processes and functions for the same payment systems to ensure assurance and readiness for anticipatory cash transfers during the upcoming cyclone season. Furthermore, WFP will provide technical, analytical, and capacity strengthening support to the development of PDM tools, data collection and reporting. The Post Distribution Monitoring (PDM) will be complemented by an after-action review (AAR) session that will be conducted by the Government of Fiji and WFP in collaboration with the DSW, NDMO, other relevant departments of the Government, humanitarian and development partners, and beneficiary communities. The AAR will seek to review the overall



AA process and identify best practices and areas of improvement to make recommendations for improvements in the design of future AA in Fiji and the Pacific region.

Project Activities

Anticipatory cash transfers

The Government of Fiji, in partnership with WFP, will support a projected **15,000** households (75,000 people) with anticipatory cash transfers. With CERF funding, WFP will provide funds to the Government so that the Government will, through its social protection programme payment system, provide cash assistance to the existing beneficiaries of social protection schemes identified by the Government under four parts of the national social protection scheme namely: 1) the Poverty Benefit Scheme, 2) the Care and Protection Allowance, 3) the Disability Allowance and 4) the Social Pension Scheme. The government in consultation with WFP proposed transfer value of FJD200²⁸ to be provided to targeted households. Confirmation of the transfer value will be carried out in consultation with the Fiji Cash Working Group (FCWG) and the Department of Social Welfare (DSW).

Flow of funds

WFP will receive CERF funds from OCHA immediately after the activation of preparedness triggers, set out in the Plan of Operation (annex 2). Below is the process flow for each of the transfer modalities:

- 1) OCHA communicates to WFP that a trigger has been reached, which immediately activates the transfer of funds from OCHA to WFP – and subsequently from WFP to the Government of Fiji. OCHA will transfer the funds as per the agreement set out in the Anticipatory Action Plan, which details triggers agreed by all parties.
- 2) Upon internal approval processes with the Government that should take place within 24 hours, DSW will disburse the funds to the accounts of the Government Payment Agents together with a beneficiary list and their payment details
- 3) WFP will transfer funds from its Imprest account to the Government's Programme Account to cover for the transfer value, including the relevant withdrawal fee amount, within 24 hours after receiving the request from the Government.
- 4) Once the funds have been transferred, WFP will share a transfer notification with DSW to notify them of the transaction, within 24 hours of processing the transfer to DSW.
- 5) Upon confirmation of receipt of funds, DSW will issue an acknowledgement letter and a receipt to WFP.

Transfer value

Targeted households will receive a one-off, unconditional, and multi-purpose cash of **FJD200** to support their households purchase items for their essential needs and necessary services before the shock. In the absence of an established minimum expenditure basket (MEB)²⁹ in Fiji, the proposed transfer value considers the national poverty line, the existing monthly transfer values of the Basic Needs Poverty Line, the Family Assistance Programme transfer values of DSW/MWCSP, and the payout amount of the parametric insurance. Impact of tropical cyclones can compound vulnerabilities and increase financial needs on existing household vulnerability and financial gaps. The AA intervention will match the current level of transfer value (FJD200) for the social protection programme cash transfers. This is also to harmonize anticipatory cash transfers with regular cash assistance leveraging the Government's social protection system.

Cash assurance

As appropriate, the Government and WFP will put in place a set of standards and priority risk-mitigation measures to ensure the right people receive the right amount of money at the right time, while mitigating the risks of human error or other divergence of benefits to the extent possible. These priority risk mitigation measures include sound programme design; adequate capacity of financial service providers; segregation of duties of staff; data protection; reliable data to pay people; verification of beneficiaries; transfer reconciliation; effective CFM; and regular monitoring.

²⁸ The transfer value is proposed by the Department of Social Welfare and final determination will be done in collaboration with the national cash working group.

²⁹ Minimum expenditure basket is defined as what a household requires to meet their essential needs and its average cost.



Geographical targeting and beneficiary selection

The Government and WFP will jointly identify and target populations in priority areas, as per targeting procedures agreed with stakeholders, expecting to reach an estimated 15,000 households through the joint implementation of targeted anticipatory cash transfers. Geographical targeting of the priority areas will be determined upon the monitoring of the cyclone path/rainfall pattern depending on the pre-agreed triggers. The most vulnerable of the existing beneficiaries of social protection schemes, namely: 1) the Poverty Benefit Scheme, 2) the Care and Protection Allowance, 3) the Disability Allowance and 4) the Social Pension Scheme, will be selected for the assistance. Due to limited funding, the project will prioritize 15,000 most vulnerable and at-risk individuals and their households using criteria set by the Government in consultation with stakeholders including the communities. Older persons, people living with disabilities, women and people living below the poverty line are considered the most vulnerable in the four social protection schemes and will be prioritized as direct beneficiaries of the anticipatory cash transfers. The Government shall select the Beneficiaries in accordance with the criteria described in this Project Plan and following the procedure set out in the SOP.

Capacity strengthening

The Government and WFP will collaborate to support the capacity strengthening activities for district governments' social protection focal points through a set of trainings. The trainings will include topics to ensure smooth implementation of the Project, such as Anticipatory Action fundamentals, cash assurance, transfer mechanisms, monitoring, accountability to affected populations, and early warning messages. The training will bring together approximately 50 district government social protection focal points for a one and half day session in October 2023, before the cyclone season starts.

Communication with communities

During the preparedness phase, WFP, UNICEF, and other UN agencies will support DSW to design and implement sensitization and outreach activities to ensure beneficiaries and their communities fully understand the scope of the project (consent, eligibility criteria, transfer value, payment process, project duration), the community feedback mechanisms in place, the early warning system, what to do before the impact of cyclones, and early warning dissemination channels (SMS, community radios and announcements at religious sites). WFP and UNICEF will also provide trainings to relevant government officials at national and district level and personnel at distribution points.

Once the activation triggers are met, messaging will be distributed by the Government in Fijian, Hindi, and English language to ensure that communities are adequately informed to prepare for the forecasted cyclone. To the extent possible, the Government's community feedback mechanism will be supported by WFP and UNICEF to absorb increased demand for rapid case management.

Emergency preparedness and system strengthening

The Government and WFP will provide strengthen existing government social protection systems to generate evidence to further strengthen the DSW's capacity to anticipate, prepare for, and respond to future climate-induced shocks and return to normal programming after the response. Critically, the pilot will provide the opportunity to review the current social protection cash delivery systems to identify risks and risk mitigation measures to ensure rapid and assured cash transfers once activation triggers are met.

Monitoring and learning

The Government and WFP will jointly design and implement monitoring and reporting activities. National systems will be leveraged to undertake monitoring activities during and after the implementation of the anticipatory cash transfers. The post distribution monitoring³⁰ will assess the impact of the intervention on beneficiaries and how the anticipatory cash transfers helped to mitigate the impact, which will help DSW and WFP to develop any corrective measures on the social protection schemes in the future. In addition, WFP in collaboration with the Government will organize a joint lesson learned and best practices event to document the overall experience in this project. This approach will ensure accountability to stakeholders through information sharing and also provide learning to inform future anticipatory action design and decisions of the Government, as well as other governments within the Pacific region.

³⁰ Information of persons indirectly benefiting from this project apart from the household members of the targeted 5,000 recipients will be collected through post distribution monitoring



Partnerships and coordination

The overall project coordination is led by the Government's National Disaster Management Office with technical support and collaboration with OCHA's Regional Office for Pacific Islands in Fiji. UN agencies including WFP, UNICEF, FAO, UNFPA and UN Women will jointly provide coordinated support for the anticipatory cash transfer processes using each agencies' comparative advantages to maximize efficiency and effectiveness of the Project. The FCWG³¹ will provide a platform for operational coordination, standardization, harmonization, and learning related to multi-sector cash and voucher assistance in emergency preparedness and response activities in Fiji. In addition to the collaboration with UN agencies, WFP will work closely with relevant government departments that will provide leadership throughout the design and implementation of the project. The overall joint responsibilities of the government are also provided in Article IV of the contract. The implementation of the project will be done in coordination with and under the leadership of Department of Social Protection lead in Fiji and National Disaster Management Office (NDMO). These partnerships between line ministries, UN agencies, local NGOs and community-based organizations will ensure a coordinated humanitarian response, strengthen national capacity, and help steer future anticipatory action based on evidence and learning generated.

Roles and Responsibilities

National Disaster Risk Management Office

- Provide overall leadership of the design and implementation of the project through coordination of key stakeholder consultations and communications between governmental and other stakeholders.
- Determine the readiness and activation triggers for anticipatory cash transfers together with Fiji Meteorological Service and OCHA and declare when the triggers are met.
- Coordinate the development of the Post Distribution Monitoring operational plan with the Ministry of Women, Children and Social Protection (MWCSP), WFP and other stakeholders.
- Provide staff to participate in and support joint monitoring with MWCSP and WFP at least once during the project implementation period.

Ministry of Finance

- Receive funds from WFP through the Government's Consolidated Account on behalf of the Government of Fiji.
- Transfer funds to the MWCSP upon request from MWCSP. The request to Ministry of Finance will be sent through a Request for Release of Ad Hoc Donor Funds Checklist which will be completed by MWCSP and submitted to Ministry of Finance when the funds are allocated.
- Disburse funds to MWCSP through the small grant allocation process within 24 hours of fund transfer request receipt.
- Create an internal transfer fund allocation number for WFP for accountability purposes. This specific allocation will record all transactions from WFP funds in the Government's Financial Management Information System.
- Receive reconciliation of funds by MWCSP with supporting documents and using the information to support the preparation of an end of project accountability report for WFP within three months after the end of the project.
- Attend coordination meetings as per invitations from NDMO.

Ministry of Women, Children and Social Protection

- Develop and maintain updated beneficiary lists with minimum information needed to make the cash transfers for programme planning purposes.
- Collaborate with WFP and other UN agencies to provide an effective communication to beneficiaries, their communities, and relevant MWCSP staff at the field level during the project period. Messaging to beneficiaries should include but not all relevant project information such as entitlements, eligibility criteria and duration of project.
- Through the Poverty Monitoring Unit of MWCSP, lead and support the WFP and NDMO for monitoring purposes (post-distribution monitoring exercise) through provision of staff to participate in and support joint monitoring with NDMO and WFP within three months after cyclone hits, at least once during the project implementation period.
- Request funds from the Ministry of Finance by filling in the Request for Release of Ad Hoc Donor Funds Checklist and submitting it to the Ministry of Finance immediately after the readiness triggers are declared.
- Transfer funds to the agreed target beneficiaries under the Poverty Benefit Scheme, Care and Protection Allowance

³¹ The FCWG is composed of the cash and voucher assistance community of practice that includes, but not limited to, NGOs, UN agencies, community-based organizations of people's organizations, financial service providers, micro-finance institutions, rural and commercial banks, remittance centres, and government line ministries.



Scheme, Disability Allowance Scheme, and Social Pension Scheme in priority areas projected to be impacted by the forecasted cyclone.

- Manage partnerships with financial service providers for the project. This will include orientation on the anticipatory action approach, coordination to ensure timely cash transfers within the defined timeframe.
- Facilitate reconciliation of funds provided by WFP with supporting documents and submitting this information to Ministry of Finance.
- Use the reconciliation information to support the preparation of an end of project accountability report for WFP within three months after the end of the project.
- Jointly organize with WFP a workshop after project completion to facilitate internal and external discussions on lessons learnt for continuous learning and recommendations for improvements in the future.
- Prepare and submit a final project report to WFP.

United Nations World Food Programme

- Disburse funds to the Government's Programme Account to cover both transfer value for the Beneficiaries and the withdrawal fees of the FSP and the Government. Disbursement of funds will be made in accordance with the MoU.
- Support review existing set up of the Community Feedback Mechanism for management the complaints and feedback from beneficiaries and their communities.
- Provide technical support for rapid cash transfers preparedness of existing government social protection delivery mechanisms to ensure timely cash transfer by Department of Social Welfare
- Support the government in the design and implementation of the process and output monitoring of the anticipatory cash transfers including post distribution monitoring.

Cross Cutting Issues

Accountability to Affected Populations

The Government, in collaboration with WFP, will ensure that the targeted communities, including vulnerable population groups such as households headed by women, older persons, children and people with disabilities will be provided with appropriate, accessible, and timely information on the proposed anticipatory cash transfer, such as transfer amount, project duration, and other related aspects. To reach all people in the project area, the information will be provided in local languages during the community level meetings, and this will be facilitated through the DSW field level teams. Given that this is a vertical expansion of the Government social protection system, WFP will not set up a separate CFM. Instead, WFP will support DSW and NDMO in the management of its own CFM and process, to ensure any irregularities are addressed.

Gender

The government will implement anticipatory cash transfer taking account of gender sensitivity. Gender considerations, including contribution to greater gender equality and women's economic empowerment, will be at the core of WFP's technical support to the Government. The anticipatory cash transfers will be implemented in coordination with MWCSPP, an active partner of UN agencies currently working on gender-sensitive programming, and the lead of the Fiji Safety and Protection Cluster. By using Government Social Safety Net platforms for anticipatory cash transfers, the Government and WFP will be able to leverage existing systems to strengthen the Government's efforts on gender, help make social protection systems become more gender-sensitive and improve vulnerable women's immediate access to food.

Gender-based violence

Given that this Project is for a one-off emergency assistance with limited timeframe, WFP will not be able to support the Government to respond to gender-based violence in a comprehensive manner, however, to the extent possible WFP will support the Government to ensure that risks of gender-based violence are identified and mitigated, and any instance of gender-based violence encountered is reported and responded to during the Project.

Disability Inclusion

This Project is designed to address the preparedness of the persons with disabilities who are beneficiaries of the Disability Allowance scheme and live in the priority response area. The Government and WFP will ensure meaningful access to communication channels including CFMs, sensitization materials, and field monitors for all persons with disabilities during the Project to identify their barriers, and their unique needs are adequately met with reasonable accommodations.




Project Timeframe

The project activities are estimated to be completed within a three-month period from when the readiness and activation triggers are met. The table below provides critical actions that will take place should the triggers be met in the event of cyclones.

Activities	Responsible Agency(ies)	Timeline
Preparation Phase		
Revised MoU and project document preparation	WFP	December 2025
MoU signing	WFP/DSW	January 2026
Implementation Phase³²		
On going monitoring of tropical cyclones	NDMO/OCHA/FMS	Jan '26 – Apr '27
Declaration of triggers	FMS/NDMO	Jan '26 – Apr '27
OCHA transfers funds to WFP	OCHA	Jan '26 – Apr '27
WFP transfers funds to the Government	WFP	Jan '26 – Apr '27
Early warning messaging and beneficiary sensitization to all locations on cyclones path	WFP/UN AGENCIES/DSW	Jan '26 – Apr '27
Government transfers funds to FSP	MoF/DSW	Jan '26 – Apr '27
Anticipatory cash transfers to people at risk of the cyclone	DSW	Jan '26 – Apr '27
Monitoring and CFM follow ups	DSW/WFP	Jan '26 – Apr '27
Review Phase		
After Action Review	OCHA/UN AGENCIES	3 to 4 weeks after TC/Flood AA transfers
Post Distribution Monitoring and documentation	WFP/DSW	2 to 4 weeks after TC/Flood AA transfers

Figure 1: Flow of actions upon triggers

³² The implementation phase activities and timelines are dependent on when the tropical cycles may happen which can be between November 2023 and March 2024. The detailed sequence of events upon declaration of triggers is in the SOP.

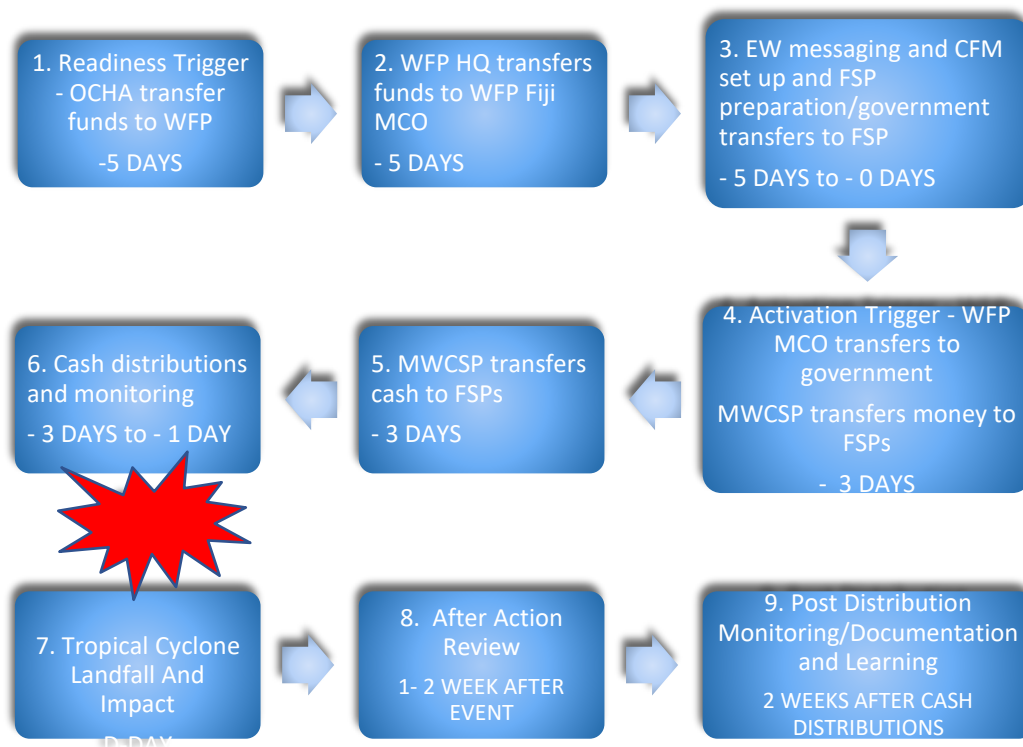

Operational Presence and Access

The WFP Pacific Multi-Country Office is located in Suva, Fiji. In close collaboration with the DSW and NDMO field level offices, WFP will provide remote monitoring support to ensure the quality and smooth implementation of the project.

ANNEX 2:

Plan of Operation and Standard Operating Procedures (Document attached separately)

ANNEX 3:



Estimated Budget

	Number of households	FJD*	USD
Transfer value	15,000	2,970,000.00	1,320,000.00
Transfer Cost and Withdraw fees	15,000	101,250.00	45,000.00
MWCSP Administration costs		45,000.00	20,000.00
Total Estimated Budget		3,116,250.00	1,385,000.00

*FJD amount may vary based on foreign currency exchange rate at time of transfer



ANNEX 4:

Distribution/Financial Reconciliation Report

			Transfer Details		
Region/District	Number of planned households (HHs)	Total entitlement (FJD)	Number of HHs Assisted - Successful transfers	Number of HHs Assisted - Unsuccessful transfers	Cash balance (FJD)
Bank Transfers					
Subtotal					
Mobile Money					
Subtotal					
Post Office					
Subtotal					
Grand Total					

I, the..... *[title of the person]* of the Department of Social Welfare, Ministry of Women, Children and Social Protection hereby certify that the this report contains, true, complete and accurate information and accounts of funds received from WFP and used to distribute benefits to beneficiaries for the Operation pursuant to the MoU between the Government of Fiji and World Food Programme dated.....20.....

Department of Social Welfare

Certified by (DSW):

Name:

Title:

Date:

Received by (WFP):

Name:

Title:

Date:

ANNEX 5



Final Consolidated Distribution/Financial Reconciliation Report

Region/District	Number of planned households (HHs)	Planned Cash Distributions (FJD)	Actual Cash Distributions (FJD)				Cash Balance (FJD)	Remarks
			Day 1	Day 2	Day 3	Post-shock		
Bank Transfers								
Subtotal								
Mobile Money								
Subtotal								
Post Office								
Subtotal								
Grand Total								

I, the..... *[title of the person]* of the Department of Social Welfare, Ministry of Women, Children and Social Protection hereby certify that the this report contains, true, complete and accurate information, financial statements and accounts of funds received from WFO and used to distribute benefits to beneficiaries for the Operation pursuant to the MoU between the Government of Fiji and World Food Programme dated..... 20.....

Certified by (DSW):

Name:

Title:

Date:

Received by (WFP):

Name:

Title:

Date:

ANNEX 6



DATA PROCESSING TERMS

According to the MoU WFP will provide technical assistance for rapid cash transfers preparedness of the government social protection transfer mechanisms (Article 1.2.a). In particular, WFP shall provide to the Government technical assistance and guidance on anticipatory action cash transfers preparedness of the existing social protection mechanisms (Article 5.5). The Government has designated the Ministry of Women, Children and Social Protection (the “Executing Agency”) as the executing agency for this Operation (article 4.1). In order to execute this Operation, the Executing Agency will process personal data. To the extent that WFP’s assistance and guidance entails the processing of the Executing Agency’s personal data by WFP, the following data processing terms shall apply to both Parties. Any terms not defined herein shall have the meanings set out in other parts of the MoU.

1. DEFINITIONS

- 1.1 “Controller”** means the natural or legal person which, alone or jointly with others, determines the purposes and means of the processing of Personal Data. For the purposes of this Annex, the Executing Agency acts as the Controller of the Beneficiaries’ personal data.
- 1.2 “Data Subject”** means the individual or individuals to whom the personal data processed under this MoU relates.
- 1.3 “Personal Data”** means any information relating to a Data Subject, in particular by reference to an identifier such as a name, an identification number, location data, an online identifier or to one or more factors specific to the physical, physiological, genetic, mental, economic, cultural or social identity of that natural person. Personal Data covers digital as well as non-digital information that is provided to the Processor (as defined below) by or on behalf of the Controller or is obtained by the Processor in connection with Processor’s activities under Articles 1.2.a) and 5.5 of the MoU.
- 1.4 “Process” or “processing”** (or any variation thereof) means any operation or set of operations that is performed on Personal Data, whether or not by automatic means, such as viewing, accessing, collection, recording, organization, storage, adaptation or alteration, retrieval, consultation, use, disclosure by transmission, anonymization, dissemination or otherwise making available, alignment, combination, blocking, erasure or destruction.
- 1.5 “Privacy Rules”** means, regarding WFP, its applicable data protection rules, principles and guidelines and regarding the Executing Agency, its applicable data protection laws.
- 1.6 “Processor”** means a natural or legal person (including public authority, agency, NGO or other body) which processes Personal Data on behalf of the Controller. WFP acts as the Processor of the Personal Data provided by the Controller within the context of Articles 1.2.a) and 5.5 of the MoU for the provision of the agreed technical assistance and guidance.

2. DATA PROCESSING TERMS

The Controller accepts to provide the Processor access to Personal Data for the purposes described in Articles 1.2.a) and 5.5 of the MoU. The Processor undertakes to process such Personal Data on behalf of the Controller and according to the following terms:

- The Processor shall act solely in accordance with the Controller’s written instructions, to the extent the Processor can do so in accordance with its rules and regulations, including Processor’s Privacy Rules; in case that the Controller’s instructions contravene the Processor’s rules and regulations, the Processor will immediately inform the Controller, in writing.
- The Processor shall only process the Personal Data for the purposes of performing its obligations under Articles 1.2. a) and 5.5 of the MoU as well as its obligations under the Processor’s Privacy Rules;
- The Processor shall inform the Controller in the event of a breach of its obligations under this Annex.
- The Processor shall only disclose, give access to or share the Personal Data with subcontractors contractually engaged by the Processor to provide the technical assistance and guidance set out in Articles 1.2.a) and 5.5 of the MoU. Any other disclosure of Personal Data will be subject to the Controller’s authorization.
- The Processor shall keep confidential the Personal Data, even after the expiry or termination of the MoU.
- The Processor shall implement and maintain all the appropriate technical and organizational measures necessary to ensure the security of the Personal Data.



- The Processor shall inform the Controller promptly by email, after the Processor has discovered or become aware of a data security breach involving the Personal Data processed on behalf of the Controller.
- The Processor shall cooperate with the Controller in providing the relevant information related to any requests received from Data Subjects who exercise their data protection rights vis-à-vis the Controller. The Processor shall not be responsible for responding these data protection requests.
- Upon the termination of the MoU, the Processor shall either return to the Controller or destroy the Personal Data. The Processor shall be entitled to keep the Personal Data until the end of its applicable data retention periods according to the Processor's rules and regulations.

ANNEX 7
WFP GENDER POLICY 2022

(printed copy to be attached)

ANNEX 8
WFP HUMANITARIAN PROTECTION POLICY

Printed Copy to be attached

ANNEX 9
ANTI FRAUD ANTI CORRUPTION POLICY

Printed Copy to be attached

ANNEX 10
SG BULLETIN ON SPECIAL MEASURES ON PSEA

printed copy to be attached



Annex 9 - Common Early Warning Messages

Early Warning Messages	Target audience	Communication channel	Language	Readiness trigger (up to 120 hours)	Activation trigger (up to 72 hours)
CATEGORY 1: MOVEMENT					
In case of flooding, do not cross or swim in rivers, streams, drains, roads and walkways where water is above your ankles. Supervise your children, do not let them swim or cross flooded rivers, streams, drains, and roads.	The public, Parents, caretakers	Radio, TV, SMS Blast, Social media	English, iTaukei, Hindi	v	v
The weather conditions over the next days could cause poor visibility and traffic disruptions. Do not drive before you read the advisories on the Fiji NDRMO website https://www.ndmo.gov.fj/or Facebook https://www.facebook.com/FijiNDRMO .	Drivers, Public Transport Operators	Radio, TV, SMS Blast, Social media	English, iTaukei, Hindi	v	v
Move to safety while it is daylight or while it is safe to do so. Should you need any assistance, contact the Fiji Police Force on 917, the National Fire Authority (NFA) on 910, or the Fiji Roads Authority on 5720. Assist the elderly or persons with disabilities, pregnant women while moving to safety.	The public, Caregivers, PWD Organisations and PWDs.	Radio, TV, SMS Blast, Social media	English, iTaukei, Hindi	v	v
Move to higher grounds while it is safe to do so. Should you need any assistance, contact the Fiji Police Force on 917, the National Fire Authority (NFA) on 910, or Fiji Roads Authority on 5720 NB: Merge this message with Move while it is daylight.	The public (consider adding further instructions for people with disabilities)	Radio, TV, SMS Blast, Social media	English, iTaukei, Hindi	v	v
Look after your pets and move livestock to higher and safe grounds or shelter).	Pet owners and farmers	Radio and SMS Blasts, Social Media	English, iTaukei, Hindi	v	v



CATEGORY 2: ACCESS TO INFORMATION					
Follow the latest weather and public advisories on radio and TV or visit the Fiji NDRMO website https://www.ndmo.gov.fj/ or Facebook https://www.facebook.com/FijiNDRMO . Be ready to evacuate if needed.	The public	Radio, TV, SMS Blast, Social media	English, iTaukei, Hindi	v	v
Know your emergency contacts: 910 for National Fire Authority, 913 for Energy Fiji Limited, 911 for Ambulance, 5720 for Fiji Roads Authority, 917 for Police, 5777 for Water Authority of Fiji.	The public	Radio, TV, SMS Blast, Social media	English, iTaukei, Hindi	v	v
As we get ready for power outages, prepare power banks and a battery-powered radio to tune into public advisories from government. Keep your phone with emergency contacts charged at all times.	The public	Radio, TV, SMS Blast, Social media	English, iTaukei, Hindi	v	v
CATEGORY 3: HEALTH AND PERSONAL SAFETY					
Prepare your emergency kit with: first-aid kit with essential medicines important documents candles bottled or boiled drinking water canned food battery powered radio torch spare batteries	The public	Radio, TV, SMS Blast, Social media	English, itaukei, Hindi	v	



Prepare your first aid kit with band-aids, bandage, antiseptic wipes, antibiotic ointment, thermometer, essential medicine such as pain relievers, cough and cold medicine, anti-diarrhea medication, and antihistamine. Have sufficient prescription medications on hand.	The public, elderly, sickly	Radio, TV, SMS Blast, Social media	English, itaukei, Hindi	v	
Store copies of your medical records , allergies, and important health information in a waterproof container.	The public (parents, the elderly)	Radio, TV, SMS Blast, Social media	English, itaukei, Hindi	v	v
Ensure you have contact information for nearby medical facilities, emergency services, and local hospitals in case of emergency.	The public (parents, the elderly)	Radio, TV, SMS Blast, Social media	English, itaukei, Hindi	v	v
If you or your family members have special medical needs such as using of special medical equipment, contact your doctor now or arrange for alternate care location during power outages.	The public (parents, the elderly, disabled, caretakers)	Radio, TV, SMS Blast, Social media	English, itaukei, Hindi	v	
During prolonged power outages and floodings, follow these steps not to get sick: Do not eat spoiled food and dispose it immediately. Wash raw fruits and vegetables before consumption. Boil, filter or chlorinate untreated drinking water and store it properly. Wash your hands with soap before eating and after going to the toilet or touching animals	The public (community leaders, parents)	Radio, TV, SMS Blast, Social media	English, itaukei, Hindi	v	v
Continue breastfeeding your baby.	Mothers	Radio, TV, SMS Blast, Social media	English, itaukei, Hindi	v	v



Prepare enough food and water . Boil, filter or chlorinate all untreated drinking water and store it properly.	The public (parents, caretakers)	Radio, TV, SMS Blast, Social media	English, itaukei, Hindi	v	
Ensure that you and your family practice good hygiene at all times .	The public (parents, caretakers)	Radio, TV, SMS Blast, Social media	English, itaukei, Hindi	v	v
Check on the elderly, neighbours and persons with disabilities . Keep children indoors.	The public (community leaders, parents)	Radio, TV, SMS Blast, Social media	English, itaukei, Hindi	v	v
Severe weather events can be accompanied with stress and anxiety. As we prepare for the upcoming cyclone, check on people around, especially children, persons with disabilities and the elderly. Try to address their concerns and fears .	The public (community leaders, parents)	Radio, TV, SMS Blast, Social media	English, itaukei, Hindi	v	
CATEGORY 4: ASSET AND LIVELIHOODS PROTECTION					
Secure your important external home appliances such as solar panels, tv antennas that can be damaged during disasters.	Homeowners	Radio, Tv, SMS Blast, Social media	English, itaukei, Hindi	v	v
Ensure that your water sources are well secured. water tank is filled with clean water, secure the tanks, disconnect the guttering.	Homeowners (parents, caretakers)	Radio, Tv, SMS Blast, Social media	English, itaukei, Hindi	v	v
Coastal dwellers are advised to secure boats and items that may float and damage property. Stay informed on the weather updates for flood alerts and warnings through Fiji Met Services and NDRMO. take note of high and low tides to be better prepared. Avoid going out to seas during bad weather conditions. (Fiji Met/NDMO Web/FB Link)	The public living close to the coast/boat owners	Radio, Tv, SMS Blast, Social media	English, itaukei, Hindi	v	v



Harvest mature crops , fruits and vegetables and store in safe spaces or water-tight containers.	Farmers	Radio, Tv, SMS Blast, Social media	English, itaukei, Hindi	v	v
Store farming tools and machineries in safe spaces.	Farmers	Radio, Tv, SMS Blast, Social media	English, itaukei, Hindi	v	v



Annex 10 - Common Early Warning Messages Testing Results

In November 2023 WHO led the testing of the EWMs in Annex 10. The results of the testing are outlined below.

Methodology

The research was conducted on the Stickybeak platform to understand which messages were most motivating to take action before a cyclone


- Survey audiences were recruited via Facebook, Messenger and Instagram from 3-5 November 2023
- Total respondents were segmented by:
 - Gender: Male (n=85) Female (n=115)
 - Age: 18-34 (n=79) 35-54 (n=74) 55+ (n=47)
 - Geography: Fiji ◦ Parent or caregiver (n=166)
 - Live with people with a disability (n=38)

Note: Segment sample sizes are small and should be treated with caution.

Key Findings

58% of those surveyed feel prepared for a cyclone, with 28% feeling unprepared

- All three messages are motivating, and the instructional message about 'securing your home etc' was the most motivating
- The message option that including a timeframe in relation to getting an emergency kit ready was slightly more motivating overall, but even more motivating with those who are feeling unprepared (rated 1 or 2 in Ques 1)
- 'Staying tuned...' vs 'Follow the latest' was more motivating in relation messaging encouraging respondents to listen to media updates
- English is preferred by over 80% of respondents (note survey was run in English only)
- The most trusted source of information is the NDRMO office.
- Radio is the main communication channel for keeping updated regarding cyclone information Based on these findings, messages that are more concise / singular with a greater sense of urgency appear to be more motivating for people to take action.






We expect severe weather conditions.

Ensure you have contacts for nearby medical facilities, emergency services, and local hospitals in case of emergency.

On a scale from 1 to 5, how motivating to take action is this message?



n=200




Secure your homes, cut overhanging branches, stow objects that can be blown or washed away.

On a scale from 1 to 5, how motivating to take action is this message?



Insight: 95% of those feeling unprepared for a cyclone rated this message a 4 or 5



n=200



A

Cyclone is expected to hit your area in around 5 days. Get your emergency kit ready – it should contain:

- first aid kit with essential medicines
- important documents
- candles
- bottled or boiled drinking water
- canned food
- battery powered radio torch
- spare batteries

B


In anticipation of an upcoming cyclone, prepare your emergency kit with:

- first aid kit with essential medicines
- important documents
- candles
- bottled or boiled drinking water
- canned food
- battery powered radio torch
- spare batteries

Which of these messages is the MOST motivating to take action?





Insight: 65% of those feeling unprepared for a cyclone prefer Message A




n=200



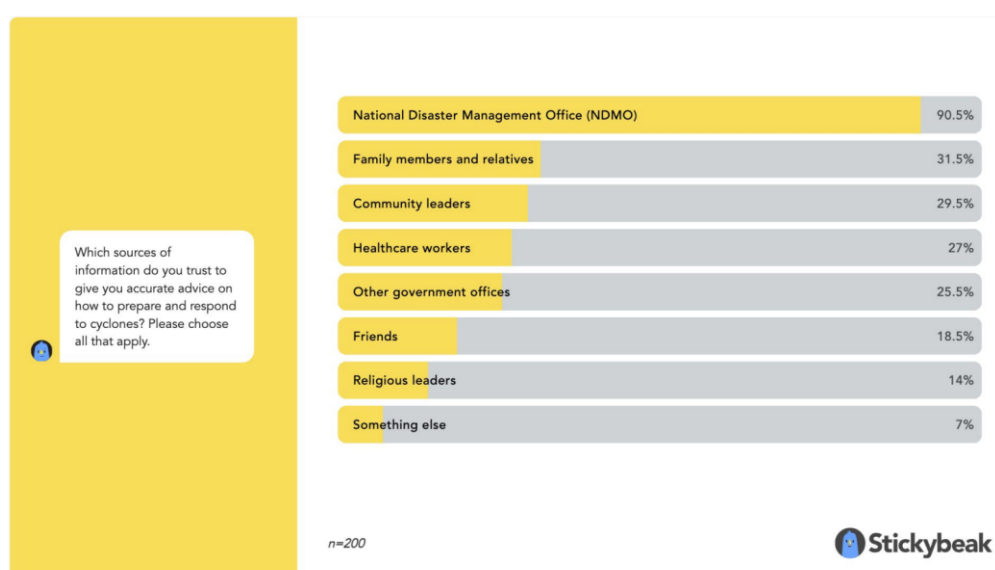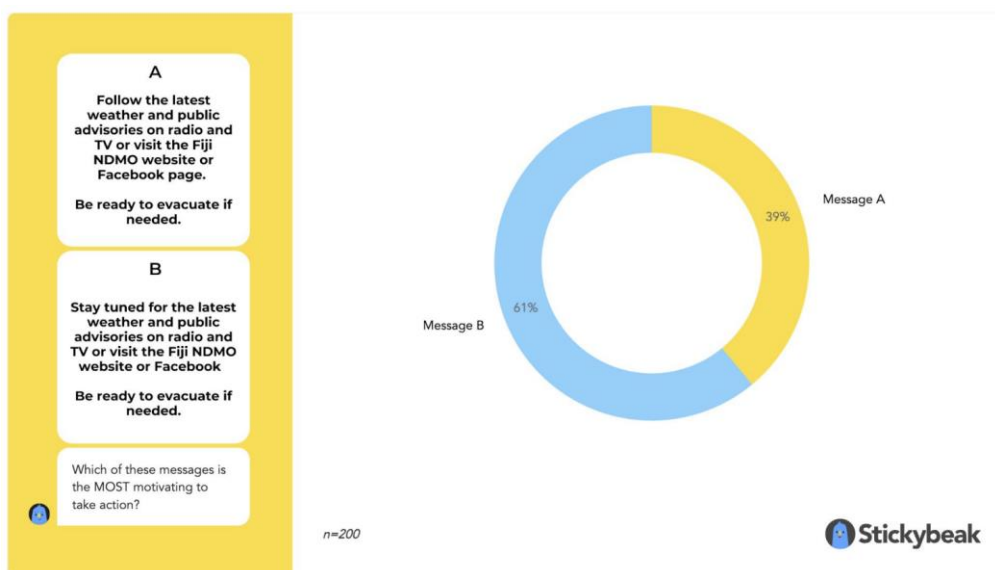



Which communication channels do you use for getting latest updates on cyclones? Select up to 3

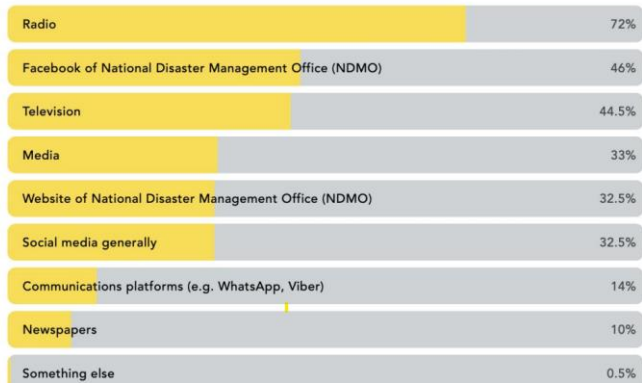

n=200





Annex 11 – Coordination Standard Operating Procedure

OCHA	NDRMO	AA Partners Agencies	Line Ministries	Divisional Commissioners	Provincial Administrators/ District Officers
Trigger Monitoring Period					
- Convenes AA Group meetings to ensure operational readiness - Keeps monitoring Fiji Met Services and NDRMO website	- Briefs Inter-Cluster Group (ICG) and Commissionaires to ensure operational readiness.	- Works with Line Ministries to ensure AA activities are ready to be implemented.	- Works with AA partners and the clusters to ensure AA activities are ready to be implemented.	- Attends briefing session. - Briefs District Officers (DOs) on the Anticipatory Action Pilot.	- Attend briefing session by Divisional Commissionaires. - Brief Community Leaders on Anticipatory Action Pilot.
Readiness Trigger					
- OCHA Centre for Humanitarian Data releases automated Official Readiness Trigger Notification to AA Partners, Line Ministries, Divisional Commissionaires, UN Resident Coordinator and NDRMO.	- NDRMO informs the Permanent Secretary about the readiness trigger. - Inform the Divisional Commissionaires about readiness triggers. - NDRMO re-shares community sensitisation	- Activates communication with line ministers. - Implements readiness activities. - Updates 5Ws (if anything is being implemented). - Shares targeting decisions with OCHA.	- Supports AA readiness activities implementation. - Updates relevant Commissionaires on targeting decisions. - Keep informed Disaster Service Liaison Officers (DSLOs).	- Reinforces EWMs and awareness video with DOs. - Shares community information sheet with DOs.	- Reinforces EWMs and awareness video with Community Leaders. - Shares community information sheet with Community Leaders.



- OCHA Centre for Humanitarian Data releases automated readiness trigger information emails to AA partners, NDRMO, Line Ministries and Commissioners.
 - CERF releases funds to AA partner agencies (up to 15% only can be spent for readiness activities)
 - OCHA activates AA Viber group for informal information sharing.
 - OCHA convenes daily AA coordination meetings and shares consolidated updates with NDRMO and PHT.
- sheet and video with commissionaires and sectors via Viber groups.
 - EWMs and community awareness videos are shared on social media, radio and TV through Get Ready (UNICEF-NDRMO).
 - NEOC is put on standby.
 - NDRMO issues advisory



Activation Trigger

- | | | | | | |
|---|---|--|--|--|---|
| <ul style="list-style-type: none"> - OCHA Centre for Humanitarian Data releases automated Official Activation Trigger Notification to AA partners, NDRMO, Line Ministries and Commissioners. - OCHA Centre for Humanitarian Data releases automated activation trigger information emails to AA partners, NDRMO, Line Ministries and Commissioners. - CERF funds can be spent by agencies. - OCHA shares impact model map issued by NDMRO with AA partners. | <ul style="list-style-type: none"> - NDRMO officially the PS about the activation trigger [forwards official trigger email]. - NEOC is activated. ECs are activated if needed. - NDRMO shares AA updates (received by OCHA) to ICG if convened. - Joint UN-Fiji Gov Press Release is finalized and issued | <ul style="list-style-type: none"> - Confirms geographical targeting decision with OCHA and Line Ministries (based on 1st activation path received and NDRMO impact model) - Jointly with Line Ministry, inform via official email the Divisional Commissioners responsible for the implementation area. - Once in the Division, report in person to Divisional EOC. - Implements AA activation in communication with line ministries and clusters. - Reports on implementation to line ministries. - Shares targeting decision and implementation | <ul style="list-style-type: none"> - Jointly with implementing agency, inform via official email the Divisional Commissioners responsible for the implementation area. - Report in person to Divisional EOC. - Supports AA activities implementation. - Shares implementation updates with the clusters. - Reports on implementation to Commissioners, DOs and PAs. - Keep informed Disaster Service Liaison Officers (DSLOs). | <ul style="list-style-type: none"> - Activate provincial and District EOCs. - Ensures PAs and DOs are aware about the AA activation if their division is being targeted. - Ensures widespread dissemination of EWMs with community leaders. - Guide geographic targeting based on collected information. - Shares SitReps based on inputs from line ministries. | <ul style="list-style-type: none"> - Ensure Community-based Disaster Risk Management Committees are aware of AA activation if their district is targeted. - Ensures Community-based Disaster Risk Management Committees actively engaging with EWMs and Advisory. - Guide geographic targeting based on collected information. |
|---|---|--|--|--|---|



- OCHA convenes daily AA coordination meetings and shares consolidated updates to NDRMO and PHT.
 - OCHA finalises draft joint UN-Fiji Gov press release.
- updates with OCHA and in Viber group and at AA coordination meetings and through live template.
 - Updates 5Ws

Post Landfall – Response Phase

- | | | | | | |
|---|---|---|---|--|--|
| <ul style="list-style-type: none"> - Shares consolidated 5Ws platform with NDRMO and PHT. - Updates PHT on the Cyclone? and AA completed activities. - Supports agencies in reprogramming AA to RR (if needed) | <ul style="list-style-type: none"> - Shares consolidated information on completed AA activities with ICG. - Creates impact model with landfall cyclone path. - Starts assessment with IDA form (with AA questions included). | <ul style="list-style-type: none"> - Shares updates on completed AA activities with OCHA and line Ministries. - Updates 5Ws - Reprogrammes activities to RR if needed. | <ul style="list-style-type: none"> - Shares updated on completed AA activities with the Commissionaires, the clusters, DSLOs, PAs and DOs. | <ul style="list-style-type: none"> - Updates SitReps - Rollout assessments with IDAs (with AA question included) | <ul style="list-style-type: none"> - Provide SitReps information to Divisional Commissionaires. |
|---|---|---|---|--|--|

Post-Crisis

- | | | | | | |
|---|--|--|--|--|---|
| <ul style="list-style-type: none"> - Organizes LLW/AAR with NDRMO. | <ul style="list-style-type: none"> - Attends/organizes LLW/AAR. | <ul style="list-style-type: none"> - Participates in the LLW/AAR. | <ul style="list-style-type: none"> - Participates in the LLW/AAR. | <ul style="list-style-type: none"> - Participates in the LLW/AAR. | <ul style="list-style-type: none"> - |
|---|--|--|--|--|---|



- Supports coordination of data collection for the multi-stakeholder evaluation
- Supports multi-stakeholder evaluation data collection
- Conducts activity-specific evaluation.
- Participates in multistakeholder evaluation data collection
- Participates in multistakeholder evaluation data collection.



Annex 12 – IDA Forms

Anticipatory Action Evaluation Questions to be added to the community level data collection form of the Initial Disaster Assessment

1. Did this community or any households in the community receive any of the following types of support within the week before the cyclone? [Multiple-Choice](#) [Read Responses](#)

_____ [1] Water and sanitation kit (water treatment/storage supplies)

_____ [2] Shelter kit (items to reinforce house)

_____ [3] Boat strengthening kit

_____ [4] Hermetic bag (for dry storage)

_____ [5] Hygiene items or dignity kit

_____ [6] Menstrual hygiene supplies / kit

_____ [7] Multi-purpose cash transfer

_____ [8] Temporary learning space

_____ [9] Health facility support

_____ [10] Evacuation center

_____ [11] Early warning messaging

_____ [99] Other (Specify ^(If 99): _____)

_____ [0] None

2. Did this community or any households in the community receive any of the following types of support within the week after the cyclone? [Multiple-Choice](#) [Read Responses](#)

_____ [1] Water and sanitation kit (water treatment/storage supplies)

_____ [2] Shelter kit (items to reinforce house)

_____ [3] Boat strengthening kit

_____ [4] Hermetic bag (for dry storage)

_____ [5] Hygiene items or dignity kit

_____ [6] Menstrual hygiene supplies / kit

_____ [7] Multi-purpose cash transfer

_____ [8] Temporary learning space

_____ [9] Health facility support

_____ [10] Evacuation center

_____ [11] Early warning messaging



Pacific
Humanitarian
Team
ANTICIPATORY ACTION TWG

_____ [99] Other (Specify ^(If 99): _____)

_____ [0] None



Annex 13 – Awareness Sheet for Community Leaders

Anticipatory Action Pilot for Tropical Cyclones in Fiji

Testing a New Way to Prepare for Cyclones

Acting early saves lives and keeps your community safe. Anticipatory action is a pilot project, which introduces a new way of providing communities with humanitarian aid before the cyclone hits. This aid is given in the time between the forecast and the cyclone's landfall, allowing communities to act early and protect their lives and livelihoods. Use it before the disaster to become more resilient and keep themselves safe.

Here's what's happening:

What's a Trigger?

A trigger works like an early warning that alerts us about an approaching tropical cyclone. It relies on weather forecasts from the Fiji Meteorological Services. If there's a severe cyclone expected and/or heavy rainfall that meets the pre-agreed conditions, we will activate our plan.

Getting Ready Before the Cyclone:

Communities within the direct forecasted path of the cyclone may receive assistance before its arrival. This support is designed to enhance safety as the cyclone approaches. It's a safety initiative we're testing, focusing on areas where the cyclone might hit the hardest.

How Does it Work?

Different kinds of help have been planned, and they will be given to different groups of people in the forecasted cyclone path based on their vulnerabilities. This happens before the cyclone hits, so families can prepare and stay safe. Items on this list will be distributed by various partners:

- **Cash Aid:** To assist the most vulnerable families in getting what they need urgently. Selected households on the Department of Social Welfare's Family Assistance Scheme, Care and Protection Allowance, Disability Allowance and Social Pension Scheme may receive a top-up of FJD 200 to prepare for the cyclone. Money could be spent on items such as evacuation, food, medicines, communications, batteries etc.
- **Watery, Hygiene and Sanitation Kits:** Supplies for staying clean and safe during the cyclone.
- **Special Kits for Women:** Helping pregnant women and women with disabilities stay comfortable and safe.
- **Education Materials:** Materials to help children continue with their education even during the cyclone.
- **Tools to Strengthen Shelters:** Equipment to make homes stronger against the storm.
- **Farmers' Supplies:** Tools to protect farmers' resources.
- **Fishing Support:** Tools to help fishermen protect their boats.
- Alongside this aid, communities will receive early warning messages with instructions on how to prepare for the cyclone.

How We Decide Who Gets Help:



It's crucial to note that not everyone will receive every type of aid. Each specific item will go to those who need it the most. We aim to assist communities located where the storm is predicted to be most severe. However, forecasting isn't 100% precise. Sometimes, we may unintentionally provide more help to areas less impacted by the cyclone. We're learning from this process to improve our strategies for future events.

Your Role in Helping:

Help us explain this new plan to everyone in your community! Together, we can ensure everyone understands the reasons behind receiving or not receiving support, how to use it before the cyclone arrives, and how to stay safer when cyclones hit.

