

1. Executive Summary

This document presents the framework for anticipatory action (AA) in Mozambique, including the trigger, the pre-agreed action plan and the pre-arranged financing.

The context: Mozambique is regularly impacted by cyclones, especially in the low-lying coastal areas that are home to a majority of the population. Since 2017 alone, some 5 million people have been affected, mostly in the provinces of Zambezia, Nampula and Sofala. Moreover, cyclones are the natural hazard with the greatest attributable economic losses. Since 2000, Mozambique has been impacted by a major tropical cyclone every other year on average. The cyclones that hit the Mozambican coast are increasing in number and intensity¹.

The objective: This framework seeks to provide coordinated anticipatory action to people at risk of or affected by cyclones in Mozambique. The initiative provides life-saving assistance to people across all coastal provinces: Cabo Delgado, Nampula, Zambezia, Sofala, Inhambane, Gaza, Maputo and Maputo City.

The development process: The framework was developed through a participatory process led by the Resident and Humanitarian Coordinator and coordinated by OCHA Mozambique in collaboration with the government-led national technical working group on anticipatory action.

The trigger

The financing and activities included in this framework will be triggered by either the following readiness trigger, action trigger or observational trigger.

- **Readiness trigger (lead time up to 120 hours before landfall, monitored by OCHA/CHD):**
 - The readiness trigger is using the same conditions defined for the action trigger (see below), but is considering forecasts with lead times between 96 and 120 hours
- **Action trigger (lead time between 96 and 6 hours before landfall, monitored by INAM):**
 - The exposed area corresponding to a tropical cyclone of at least 119km/h overlaps with at least one of the coastal provinces: Cabo Delgado, Nampula, Zambezia, Sofala, Inhambane, Gaza, Maputo and Maputo City
- **Observational trigger (last forecast before or at landfall up to 48 hours after landfall, monitored by OCHA/CHD):**
 - Forecasts issued around landfall indicate that landfall will be within the selected provinces and the intensity at landfall will be at least a tropical cyclone of 119km/h OR
 - The sum of rainfall within a given province the days before, of and after landfall (sum of rainfall over 3 days) around the landfall location exceeds 120 mm.
 - If the observational rainfall trigger is reached only, either the HC or the CERF secretariat can stop an activation within 48 hours of landfall, should they determine that available information indicates that the humanitarian impact is not severe to an extent that justifies a CERF allocation.

Partners also agreed to conform with the government-mandated *cut-off time of 6 hours* before landfall for the action trigger to protect humanitarian personnel and people targeted. The observational trigger for windspeed is assessed around the time of landfall and may lead to the activation of the framework. If a trigger is reached at any time during the 6 hours before expected landfall, no anticipatory activities will begin or be carried out during this window.

¹ <https://africanclimatefoundation.org/wp-content/uploads/2023/11/800834-AFC-Mozambique-country-note-05A.pdf>

The action plan

The framework will enable agencies to implement anticipatory activities in a coordinated manner. The pre-agreed actions will focus on the following core objectives:

- **Communicating risks, engaging with communities, and early warning messaging:** Partners will collaborate to disseminate joint early warning signals as well as sector-specific messaging, including on people's rights to safe and free assistance. All partners will harmonize their messages through national government platforms in addition to agency-specific channels.
- **Supporting people in temporary accommodation centers (TACs):** Partners will ensure TACs are prepared, and people receive food, water, sanitation and hygiene (WASH) and other assistance.
- **Providing in-kind assistance:** A set of in-kind assistance activities such as the provision of shelter kits, dignity kits and hygiene and water treatment products.
- **Facilitating access to services:** The framework supports access to health, protection, (including gender-based violence (GBV)), and WASH services.

Activities were designed to be applicable for both anticipatory action and early response in case of an observational trigger being met.

The financing

The Emergency Relief Coordinator (ERC) has pre-arranged up to \$4.5 million from the Central Emergency Response Fund (CERF) to support the present framework. The funding will allow partners to provide assistance in the Food Security (\$1.3M), Shelter (\$819k), WASH (\$750k), Health (\$450k), Protection (\$300k), Sexual and Reproductive Health (\$300k), GBV (\$300k), CCCM (\$231k), and Logistics (\$50k) sectors and areas of responsibilities. In addition, agencies will provide funding through their internal mechanisms to increase the scale of the assistance provided.

The learning

The present framework has incorporated several lessons learned from previous activations. In case of an activation, an after-action review will be conducted to gather further lessons learned from the implementation of the framework. Partners also commit to engage in more comprehensive learning efforts in the future.

Contents

1.	Executive Summary.....	1
2.	Introduction	4
	Objectives of anticipatory action	4
	Exposure to and humanitarian impact of cyclones in Mozambique	4
	Framework improvements	5
3.	Coordination arrangements	6
	Core group	6
	National Technical Working Group on Anticipatory Action	6
	Synergies with other initiatives.....	6
	Alignment with Government Policies	6
4.	Forecast and Trigger	8
	Forecasts	8
	Triggers and thresholds	8
	Roles and responsibilities in monitoring the trigger.....	9
	Activation protocol	9
5.	Anticipatory Action Plan.....	12
	Selection criteria.....	12
	Priority interventions	12
	Climate adaptation.....	12
	Geographical prioritization	13
	Targeting.....	13
	Beneficiary identification and registration	14
	Ensuring preparedness for a timely implementation	15
	Activities - Summary table	17
6.	Pre-agreed Financing	20
	CERF	20
	Complementarity with other donors.....	22
	Considerations	22
7.	Learning	23
	Monitoring and evaluation.....	23
8.	Validity and future of the framework.....	24
9.	Annex.....	25
	Core principles	25
	Evaluation of trigger performance	26
	Trigger Monitoring Methodology	28
	Draft activation messages.....	29
	Membership of the national technical working group on anticipatory action	31

2. Introduction

Objectives of anticipatory action

There is broad agreement for the international humanitarian sector to scale up anticipatory action. An anticipatory approach leads to a more effective, efficient and dignified response. It also protects hard-won development gains.

Today, we can predict with increasing confidence the occurrence and humanitarian impact of certain climate-related shocks and infectious disease outbreaks. By combining different analytical approaches, out-of-the-ordinary weather events can not only be predicted, but their projected impact can proactively be mitigated based on pre-identified anticipatory actions. Building on growing evidence that acting prior to the onset of a predictable hazard enables more (cost-)effective humanitarian response, OCHA facilitates anticipatory action globally, including through the setup of Anticipatory Action frameworks.

Each framework comprises 3 core elements, all of which are underpinned by a clear learning, monitoring and evaluation plan:

- Robust forecasting embedded in a clear decision-making process (the **trigger**).
- Pre-agreed activities that can fundamentally alter the trajectory of the crisis (the **action plan**).
- Pre-arranged funding (the **financing**).

In addition to the 3 core elements, OCHA and partners invest in documenting evidence and learning from each framework to inform the improvement and scale-up of anticipatory action.

Each anticipatory action framework is tailored to the local context. Additional core principles that apply to the framework in Mozambique can be found in the annex.



Figure 1. Building blocks of anticipatory action

Exposure to and humanitarian impact of cyclones in Mozambique

Mozambique is regularly impacted by cyclones, especially in the low-lying coastal areas that are home to a majority of the population. Since 2017, some 5 million people have been affected, mostly in the provinces of Zambezia, Nampula and Sofala. Moreover, cyclones are the natural hazard with the greatest attributable economic losses. For instance, tropical

Cyclone Idai, which hit Mozambique in 2019, was one of the two most costly events (estimated loss of US\$ 1.96 billion) in Africa over the past 50 years. **The annual cyclone season in Mozambique usually lasts from November until March.** However, events may also occur outside of this period. Historical data from the National Institute for Disaster Management and Risk Reduction (Instituto Nacional de Gestão e Redução do Risco de Desastres, INGD) shows that the impact of cyclones in Mozambique has varied, affecting between 73,000 people (Cyclone Chalane in 2020) and 1.5 million people (Cyclone Idai in 2019). All cyclones have led to increased protection needs including loss of civil documentation, heightened vulnerability of persons with specific needs including elderly people and persons with disabilities, family separation, and increased gender-based violence (GBV) risks. Women and girls have been among the most vulnerable groups during and after the disasters. They face increased risks of GBV, displacement, and loss of livelihoods. Women, particularly in rural areas, are also heavily affected due to challenges in accessing relief and recovery resources. In 2023, Tropical Cyclone Freddy hit Mozambique twice, causing destructive winds, extreme rainfall, and widespread flooding. Despite accurate early warnings and coordinated disaster management, significant damage occurred, affecting infrastructure, displacing populations, and disrupting essential services. Roads were cut off, hindering social services, trade and provision of healthcare thus worsening the cholera outbreak that had started in September 2022. During the 2024/2025 cyclone season, three consecutive tropical systems, Chido, Dikeledi and Jude, made landfall between December and March, collectively affecting 1.3 million people across multiple provinces in Mozambique but particularly Cabo Delgado and Nampula. Cyclone Chido caused extensive damage in conflict-affected districts in Cabo Delgado, including Ancuabe, Chiure, Mecúfi, Metuge, and Pemba, compounding displacement and protection concerns. Heavy rains linked to Cyclones Dikeledi and Jude triggered flash floods in Sofala, Zambézia and Manica that destroyed roads, bridges and schools, and isolated communities for days. The cyclones that hit the Mozambican coast are increasing in number and intensity². Between 2000 and 2022, Mozambique has been impacted by a major tropical cyclone every other year on average (see figure below).

Return period:
2.3 years

based on 23 years with
cyclone data, since 2000

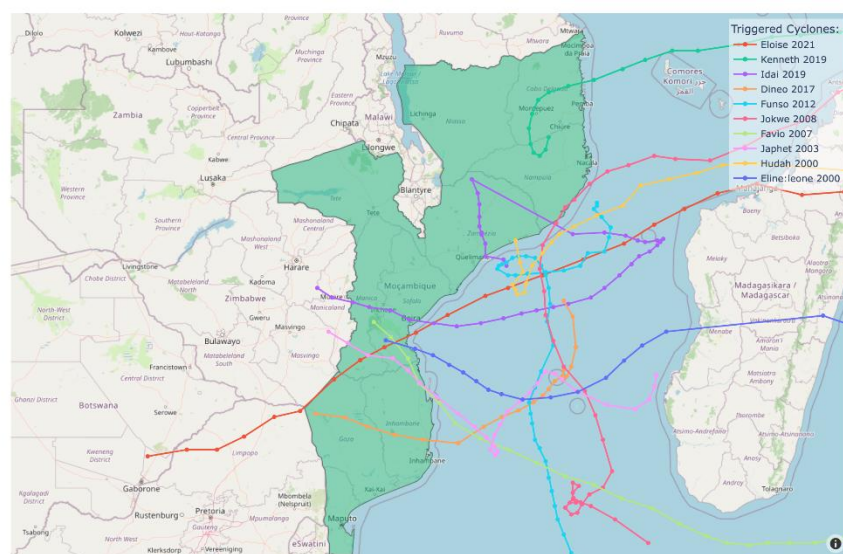


Figure 2. Historical tracks of cyclones in Mozambique 2000-2022

Framework improvements

In addition to generating learning for future frameworks, this revised framework has applied lessons learned from previous activations in Mozambique. Among others, these include:

- Simplification of the action trigger from two to a single threshold
- Disbursement of the entire CERF funding envelope after either the action or observational trigger
- Expansion of the geographical scope, enabling AA in all 8 coastal provinces
- Improved agency preparedness to ensure immediate action once triggers are met

² <https://africanclimatefoundation.org/wp-content/uploads/2023/11/800834-AFC-Mozambique-country-note-05A.pdf>

3. Coordination arrangements

Core group

This framework was developed under the leadership of the Resident and Humanitarian Coordinator by a core group comprised of IOM, UNFPA, UNHCR, UNICEF, and WFP. Relevant coordination fora, such as the Humanitarian Country Team (HCT) and the Inter-Cluster Coordination Group (ICCG) were consulted. The group closely collaborated with the wider National Technical Working Group on Anticipatory Action.

National Technical Working Group on Anticipatory Action

The National Technical Working Group on Anticipatory Action (NTWG-AA) in Mozambique is a multisectoral coordination body led by the National Institute for Disaster Risk Management and Reduction (INGD) that brings together government agencies, UN organizations, international and national NGOs, Red Cross/Red Crescent partners, donors and academia to coordinate anticipatory action across multiple hazards. The working group is structured into three sub-groups: one focused on forecasting and early warning to define risk thresholds, another providing guidance on selecting impactful interventions for anticipatory action protocols, and a third dedicated to coordinating financing mechanisms. Under government leadership, the TWG has successfully coordinated activations during the 2024/25 cyclone season and represents a leading example of institutionalizing anticipatory action within national disaster risk management systems. Collective lessons collated by the NTWG-AA from the 2024/25 cyclone season AA activation have informed the revisions in this framework.

Synergies with other initiatives

Under the leadership of the Government, this framework is aligned with and complements the efforts of other anticipatory action initiatives for cyclones, including those by WFP and the Mozambique Red Cross. Details can be found in Table 1.

Moreover, the framework contributes to the Government's vision of reducing the vulnerability of its population to predictable shocks through a multi-hazard approach. It thus complements AA initiatives for drought, floods and cholera led by the Government and supported by WFP, FAO, WHO, UNICEF, the Mozambique Red Cross, Save the Children, and others.

Table 1. Anticipatory action initiatives

Implementing organizations	IOM, UNFPA, UNHCR, UNICEF, WFP	Mozambique Red Cross, German Red Cross, IFRC	WFP
Financing Source	CERF, UN agencies	IFRC Disaster Response Emergency Fund (DREF)	WFP Global Anticipatory Action Trust Fund
Amount	\$4,500,000 from CERF + co-funding by agencies ³	500,000 CHF (approx. US\$ 630,000)	\$1,000,000
Forecast source	Météo France La Réunion, NASA	Météo France La Réunion	Météo France La Réunion
Action trigger threshold	119km/h (windspeed)	119km/h (windspeed)	119km/h (windspeed)
Lead time for action	96 hours	96 hours	96 hours
Return period	1 in 3	1 in 3	1 in 3

Alignment with Government Policies

The NTWG-AA has developed a Manual of Standard Operating Procedures for Anticipatory Action to Floods and Cyclones building on the country's experience with developing a similar manual for [anticipatory action for drought](#) in 2022. The manual was revised in 2025 based on joint after-action reviews. The present framework is in alignment with the revised manual. Specifically, this applies to the following elements:

³ Approximately up to \$1.2 million.

- The action trigger and activation protocol
- The anticipatory action plan
- The geographical prioritization

The readiness and observational triggers, which have become standard in OCHA-facilitated frameworks for cyclones, do not formally constitute a part of the national manual for AA.

Furthermore, Mozambique's National Adaptation Plan (NAP) to the United Nations Framework Convention on Climate Change (UNFCCC) identifies the increased frequency and intensity of tropical cyclones as a significant threat. Anticipatory action, including through this coordinated framework, aims to also reduce vulnerability and enhance the adaptive capacity of its communities in the face of climate change.

4. Forecast and Trigger

Forecasts

Under the World Meteorological Organization's Tropical Cyclone Programme, the Regional Specialized Meteorological Centre (RSMC) in La Réunion has the responsibility for detecting and forecasting tropical cyclones (TCs) in its zone of responsibility, which includes the South-West Indian Ocean basin, encompassing Mozambique. As such, RSMC La Réunion's TC forecasts are the internationally recognized authoritative source for TCs in this region. RSMC La Réunion is operated by Météo-France.

RSMC La Réunion issues official TC track forecasts with a 120-hour lead time. These forecasts include the TC's forecasted category and position and 5-day TC formation risk outlooks. This framework includes an observational component that uses the forecasts issued around landfall and rainfall data from NASA's Integrated Multi-satellite Retrievals for GPM (IMERG)⁴ on the days before, of and after landfall.

Triggers and thresholds

The financing and activities included in this framework will be triggered by either the readiness trigger, action trigger or the observational trigger. The activation thresholds and data sources have been selected to ensure full integration with the government-led AA activities and to capture most of the historical rapid response allocations made by CERF while maintaining a return period for activation of around 1-in-3 years. The framework relies on the following triggers to release pre-arranged financing and implement activities.

- **Readiness trigger (lead time up to 120 hours before landfall, monitored by OCHA/Center for Humanitarian Data):**
 - The readiness trigger is using the same conditions defined for the action trigger (see below), but is considering forecasts with lead times between 96 and 120 hours
- **Action trigger (lead time between 96 and 6 hours before landfall, monitored by INAM):**
 - The exposed area corresponding to a tropical cyclone of at least 119km/h overlaps with at least one of the coastal provinces: Cabo Delgado, Nampula, Zambezia, Sofala, Inhambane, Gaza, Maputo and Maputo City
- **Observational trigger (last forecast before or at landfall up to 48 hours after landfall, monitored by OCHA/CHD):**
 - Forecasts issued around landfall indicate that landfall will be within the selected provinces and the intensity at landfall will be at least a tropical cyclone of 119km/h OR
 - The sum of rainfall within a given province the days before, of and after landfall (sum of rainfall over 3 days) around the landfall location exceeds 120 mm.
 - If the observational rainfall trigger is reached only, either the HC or the CERF secretariat can stop an activation within 48 hours of landfall, should they determine that available information indicates that the humanitarian impact is not severe to an extent that justifies a CERF allocation.

	Readiness	Action	Observation
Threshold	119km/h*	119km/h*	119km/h** OR 120mm of rainfall over 3 days
Lead time	120 - 96 hours before landfall	96 - 6 hours before landfall	none (immediately prior, day of or after landfall)

*forecast windspeed when making landfall in any of the 8 coastal provinces

** forecast or observed windspeed when making landfall in any of the 8 coastal provinces

⁴ This data source has been chosen because it offers granular data encompassing the entire target area with a short latency period of approximately 24 hours. For more details, visit [IMERG](https://IMERG.nasa.gov/) on NASA's website.

Partners also agreed to conform with the government-mandated *cut-off time of 6 hours* before landfall for the action trigger to protect humanitarian personnel and people targeted. The observational trigger for windspeed is assessed around the time of landfall and may lead to the activation of the framework. If a trigger is reached at any time during the 6 hours before expected landfall, no anticipatory activities will begin or be carried out during this window.

In collaboration with technical partners, the analysis of the forecast has been standardized to consider both the cyclone track uncertainty and the expected extent of the wind buffers for the 119km/h threshold in the calculation of the projected cyclone impact area. This analysis code is publicly available in a repository⁵.

Roles and responsibilities in monitoring the trigger

The monitoring of the action triggers is done using PRISM⁶, INAM's system developed in close collaboration with WFP, which sends out a notification to a pre-determined mailing list that includes INAM, WFP and OCHA.

During the monitoring period, every 6 hours, the forecast released by RSMC in La Réunion is evaluated to determine whether the trigger has been reached. The process is outlined below:

- The forecast, containing up to 120-hour lead time, is produced by the RSMC Centre.
- It is automatically added to an FTP server⁷ managed by the RSMC. The next steps are then carried out automatically using PRISM. From the FTP server:
 - Forecast files are automatically downloaded and processed
 - The forecast is analyzed for wind speeds against the threshold where they overlap with predefined geographic zones.
 - Data is validated against thresholds for tropical cyclones (at least 119 km/h) for the 8 selected provinces..
 - If a trigger threshold is met, the system automatically sends an email to INAM, WFP's and OCHA's monitoring team to notify them that the threshold has been reached.
 - OCHA Centre for Humanitarian Data/ OCHA Mozambique emails the relevant parties under the activation protocol (draft activation messages can be found in the Annex)
 - If no trigger is reached, the system monitors the next forecast cycle.

While the action trigger will be monitored using the tools and analyses provided by INAM, the readiness as well as observational windspeed and rainfall triggers, specific to this framework, will be monitored by the Data Science team at the UN OCHA Centre for Humanitarian Data.

Monitoring will take place from 1 October to 30 April. If seasonal forecasts indicate a significant risk of events outside of these months, the monitoring period may be extended.

Activation protocol

Pre-defining this activation protocol is critical in order to avoid delays, miscommunication, uncertainty or errors once a trigger threshold is reached. Activation of the action triggers will be formally decided by the government's Technical Council on Disaster Management (Conselho Técnico de Gestão e Redução do Risco de Desastres, CTGD). The readiness and observational triggers, which are not currently included in the national AA manual, will be monitored and communicated by OCHA. Additionally, informal communication channels will be maintained to ensure effective information sharing.

⁵ [Mozambique Anticipatory Action for Cyclones GitHub Repository](#) managed by the Centre for Humanitarian Data

⁶ PRISM is the cyclone monitoring tool used to track and analyse tropical cyclone forecasts.

⁷ A File Transfer Protocol server is a secure system that facilitates the transfer of large files over a network.

Who	What
During Mozambique's cyclone season	
INAM (PRISM), OCHA's Centre for Humanitarian Data	Monitor cyclone forecasts and triggers
OCHA's Centre for Humanitarian Data	Keeps partners informed of storms that could potentially reach trigger levels.
If a readiness trigger is reached	
OCHA's Centre for Humanitarian Data	Confirms that the readiness trigger has been reached and informs the RC/HC, HCT, ICCG, UN agencies, OCHA Mozambique, relevant OCHA sections (CIS, CERF, CRD, ROSEA), via email (see draft email in annex)
CERF Secretariat	Sends approval letters to UN agencies via email, with RC/HC and OCHA Mozambique in copy
UN agencies and partners	Begin implementing <i>readiness activities</i> as soon as activation has been confirmed
If an action trigger is reached⁸	
INAM (PRISM)	Sends out a notification via email that the action trigger is reached and informs INGD and OCHA
OCHA's Centre for Humanitarian Data	Confirms that the action trigger is reached and informs the RC/HC, UN agencies, OCHA Mozambique, relevant OCHA sections (CIS, CERF, CRD, ROSEA) via email that trigger threshold is reached <u>but activation not yet confirmed</u> (see draft email in annex)
INGD	Convenes Technical Committee on Disaster Management (CTGD) virtually, which confirms activation. OCHA Mozambique informs OCHA's CHD via email of decision.
OCHA's Centre for Humanitarian Data	If CTGD confirms activation: Informs the RC/HC, the HCT, UN agencies, relevant OCHA sections (CIS, CERF, CRD, ROSEA), and the ICCG via email that <u>framework is activated</u> (see draft email in annex)
CERF Secretariat	<u>If activation confirmed:</u> If action trigger is reached without previous readiness trigger: Sends approval letters to UN agencies via email, with RC/HC and OCHA Mozambique in copy If action trigger is reached after previous readiness trigger: Confirms to agencies via email that they are authorized to use the entire funding envelope, with RC/HC and OCHA Mozambique in copy <u>If activation not confirmed:</u> No action
UN agencies and partners	Begin implementing anticipatory activities as soon as activation has been confirmed
If no action trigger but an observational trigger is reached based on windspeed	
OCHA's Centre for Humanitarian Data	Informs the RC/HC, the HCT, UN agencies, OCHA Mozambique, relevant OCHA sections (CIS, CERF, CRD, ROSEA), the ICCG via email
CERF Secretariat	If observational trigger is reached without previous readiness trigger: Sends approval letters to UN agencies with RC/HC and OCHA Mozambique in copy If observational trigger is reached after previous readiness trigger:

⁸ The exact timing of these steps depends on many factors. All stakeholders are committed to avoiding any delays in the decision-making process.

	Confirms to agencies that they are authorized to use the entire funding envelope, with RC/HC and OCHA Mozambique in copy
UN agencies and partners	Begin implementing early response activities as soon as activation has been confirmed
If no action trigger but an observational trigger is reached based on rainfall⁹	
OCHA's Centre for Humanitarian Data	Informs the RC/HC, OCHA Mozambique, CERF
RC/HC and/or CERF	Can object to an activation within 48 hours after information from CHD that trigger is reached. If no objection:
OCHA's Centre for Humanitarian Data	Informs the RC/HC, the HCT, UN agencies, OCHA Mozambique, relevant OCHA sections (CIS, CERF, CRD, ROSEA), the ICCG via email
CERF Secretariat	If observational trigger is reached without previous readiness trigger: Sends approval letters to UN agencies with RC/HC and OCHA Mozambique in copy If observational trigger is reached after previous readiness trigger: Confirms to agencies that they are authorized to use the entire funding envelope, with RC/HC and OCHA Mozambique in copy
UN agencies and partners	Begin implementing early response activities as soon as activation has been confirmed
In agreement with national technical working group on AA	
RC/HC	Announces end of trigger monitoring at the end of the cyclone monitoring season

⁹ In case of the observational trigger based on rainfall, the RC/HC and/or CERF may object to an activation. The Centre for Humanitarian Data will provide information on the extent of rainfall 24-48 after landfall to the RC/HC, OCHA Mozambique and the CERF secretariat along with historical comparisons to assess the potential impact.

5. Anticipatory Action Plan

Selection criteria

Anticipatory actions aim to protect populations most at risk of being impacted by a shock. The following criteria were applied to select actions:

1. **Anticipatory character:** Is the action effective in preventing or reducing the humanitarian impact of the shock?
2. **Ability to deliver within the window of opportunity:** Is it possible to carry out the action effectively with the available forecast lead time, i.e. in the window of opportunity between the trigger and the cyclone making landfall?
3. **Operational capacity:** Do the agency and its implementing partners have the demonstrated institutional capacity (thematic, logistic, administrative, financial, human resources) to implement the action effectively given the lead time and scale?
4. **No regrets approach:** In the case of a false alarm, will the proposed actions benefit rather than negatively affect the targeted population?

Activities were designed to be applicable for both anticipatory action and early response. Complete implementation of early response activities – in the case of an observational trigger – should not exceed 2 weeks after landfall.

Priority interventions

The pre-agreed actions, identified in collaboration with the national technical working group on anticipatory action, will focus on the following core objectives:

- **Communicating risks, engaging with communities, and early warning messaging:** Partners will collaborate to disseminate joint early warning signals as well as sector-specific messaging, including on people's rights to safe and free assistance. All partners will harmonize their messages through national government platforms in addition to agency-specific channels.
- **Supporting people in temporary accommodation centers (TACs):** Partners will ensure TACs are prepared, and people receive food, WASH and other assistance.
- **Providing in-kind assistance:** A set of in-kind assistance activities such as the provision of shelter kits, dignity kits and hygiene and water treatment products.
- **Facilitating access to services:** The framework supports access to health, protection, (including gender-based violence (GBV)), and water, sanitation and hygiene (WASH) services.

The summary table below (Table 2) provides a snapshot of each agency's planned activities. Further details can be found in CERF project documents.

Climate adaptation

In addition to their life-saving nature, many of the activities in this framework have been selected due to their ability to strengthen communities' resilience to the effects of climate change. Examples include: the dissemination of early warning messages; promotion of safe hygiene and sanitation practices; protection of WASH infrastructures in public institutions and communities; strengthening and protection of public infrastructures and roads (e.g. quick drainage cleaning, leveling and sand bags in critical points, improving road accessibility); distribution of water treatment products; cash and in-kind assistance for shelter reinforcement; reinforcing preparedness of the Local Disaster Risk Committees and health facility support.

Geographical prioritization

In line with the national standard operating procedures, the framework will be implemented in the following provinces covering the entire coast of Mozambique: Cabo Delgado, Nampula, Zambezia, Sofala, Inhambane, Gaza, Maputo and Maputo City (see map below). The RC/HC may decide to expand the geographical scope of early response activities based on the observed impact, including cyclone-induced flooding. All partners have confirmed their operational response capacity¹⁰.



Targeting

Partners will jointly target temporary accommodation centers identified in coordination with the government. Agencies will collaborate to identify households, including women-headed households, households with vulnerable older people, and households with a people with disabilities receiving joint assistance as a preparedness activity. After cyclone landfall, partners will coordinate their activities, including targeting and identification and referral of people with protection risks, with relevant stakeholders, including the government, civil society organizations and through OCHA-facilitated coordination mechanisms.

¹⁰ UNFPA has implementation capacity in Cabo Delgado, Nampula, Zambezia, Maputo and Maputo City. , Consequently, if a trigger is reached in Sofala, Inhambane or Gaza province only, CERF will not release funds for UNFPA.

Beneficiary identification and registration

While a significant portion of the in-kind assistance and services will be provided in temporary accommodation centers, the only way of ensuring that sector-specific cash and certain in-kind assistance can be distributed to those in need in the very short window of opportunity prior to cyclone landfall is by pre-registering households and individuals in advance. Registration processes must be inclusive and accessible to women and girls and other vulnerable groups, including people with disabilities and older people and those in rural or hard-to-reach areas.

IOM

While the Government conducts registration, IOM through displacement tracking matrix (DTM) and camp coordination and camp management (CCCM) provides technical assistance, tools, and resources to enhance efficiency, inclusiveness and coverage.

UNFPA

While working closely with its national partners, as well as with the government, UNFPA will identify and register vulnerable women and girls in high-risk areas who might require support during or after a cyclone. Pre-crisis vulnerability data, including information on pregnant women, and displaced people, will also be utilized. Additionally, GBV Safety Audits will be conducted to further assess risks and identify vulnerable women and girls. Besides, the Mobile sexual and reproductive health (SRH) Team will conduct real-time registration of target groups in need of SRH support.

UNHCR

UNHCR conducts rapid protection assessments to identify those at heightened protection risk and assess immediate needs, risks, and gaps within affected communities. A key protection component of the project is the identification and referral of persons with specific needs—including people with disabilities, older persons, unaccompanied children, and GBV survivors—to appropriate services. Mobile protection desks provide basic psychological support, raise awareness of available services, and ensure inclusive feedback and complaint mechanisms for all, especially vulnerable groups.

UNICEF

UNICEF's services are a mix of community and household level beneficiaries. For community services, for example, deployment of mobile health teams, or provision of health kits to the district authorities, no beneficiary registration is required ahead of time. The Ministry of Health records user data so UNICEF can understand the number of users, visit purposes, etc. Similarly, water trucking, water and sanitation in institutions and water infrastructure do not require beneficiary registration; services are available for those who need them. For distribution of health kits and WASH hygiene kits, this will be prioritized for those staying in accommodation centers. Registration will be coordinated with the government and center officials. Lastly, messaging will be done through community radios, mobile teams or other means and do not require registration.

WFP

The successful implementation of WFP's anticipatory action activities does not require pre-registration of beneficiaries since there is no provision of sector-specific cash or commodities outside of temporary accommodation centers. Early warning information will be disseminated for all populations in high-risk areas, while food assistance will be provided to populations evacuated to temporary accommodation centers.

For the case of early response where populations outside of TACs might be assisted, targeting and registration of beneficiaries will be conducted in coordination with the government and other humanitarian organizations.

Ensuring preparedness for a timely implementation

Anticipatory action requires a significant level of preparedness to be able to respond quickly and effectively before a shock occurs and during its early stages. This is especially true for sudden-onset shocks. As a result, partners have made investments to enhance their operational readiness and be able to implement their activities without delay.

IOM

Displacement Tracking Matrix (DTM)

DTM enables decision makers and responders to provide populations with better context specific assistance. As part of this framework, IOM will pre-deploy planning, pre-position data collection tools, and deploy enumerators as early response. Deployment planning includes pre-identifying enumerators and data collection teams for immediate deployment and establishing clear communication and reporting structures with the government, internally, and among partners to enable rapid data flow and analysis. Pre-positioning efforts involve updating data collection tools tailored to anticipated disaster impacts, providing these tools and resources to enumerators and partners in targeted areas, and offering training to enumerators and government counterparts. During early response, enumerators are deployed to affected areas to collect preliminary data on population counts and urgent needs. This data is promptly shared with the government, partners, and sectors to inform early response decision-making.

Camp Coordination and Camp Management (CCCM)

CCCM ensures effective coordination and support through information dissemination, deployment of teams, site/ accommodation center improvement, and early response activities. Information, education, and communication (IEC) materials are produced and distributed ahead of cyclone landfall, and early warning messages are disseminated through established communication channels, including community focal points, local authorities, megaphones, and public address systems, alongside the establishment of information points to keep communities informed. CCCM teams are deployed, prioritizing experienced field staff, to conduct site visits and joint assessments with government authorities, including assessments of accommodation and evacuation centers, provide referrals, assist affected populations, and support authorities with registration and documentation. Communities are equipped with pre-positioned site improvement tools for preparedness and initial response activities, such as cleaning and organizing. Cash-based interventions, including cash-for-work programs, are implemented to support affected populations, particularly for site/ accommodation center/ road cleaning and improvement activities. In the early response phase, CCCM teams maintain an on-site presence to assess needs, facilitate multi-sectoral responses, and strengthen Accountability to Affected Populations (AAP) and PSEA. Referral and complaints/feedback mechanisms are also established to enhance responsiveness and community engagement, ensuring activities are implemented immediately once early warning and response triggers are reached through close coordination with government counterparts.

Shelter

The Shelter/NFI component ensures targeted, needs-based assistance through rapid household assessments and coordination with Cluster partners to inform and deduplicate the distribution of Non-Food Items (NFIs). Beneficiary eligibility will be validated in close collaboration with local authorities and communities, with particular attention to vulnerable groups, including older persons, people with disabilities, and female-headed households. Implementation will be closely coordinated with the Shelter Cluster, which leads needs assessments, gap analysis, and pipeline stock management, to prevent duplication and ensure complementarity with other partners.

As part of readiness effort, Shelter/NFI procured and Pre-positioned NFIs, such as tarpaulins and shelter repair kits, will be mobilized to high-risk districts. Accessible distribution points will be established to ensure equitable access. **Following action trigger, NFIs will be distributed to households**, accompanied by awareness sessions and demonstrations on the correct use of items to maximize effectiveness and durability of assistance.

UNFPA

To ensure rapid action within trigger thresholds, UNFPA prepositions emergency supplies in high-risk coastal provinces (mainly in Cabo Delgado, Nampula and Maputo), including SRH tents, Inter Agency Reproductive Health (IARH) kits, and dignity kits, to maintain continuity of services. UNFPA's strong operational presence in the aforementioned provinces is supported by fully equipped teams ready for immediate deployment and to support the humanitarian response in the districts.

Established partnerships with national NGOs with technical capacity and local presence, as well as government stakeholders, further strengthen UNFPA's SRH and GBV response capacity. As the lead agency of the SRH Technical Working Group and GBV Coordination, as well as a strong actor on GBV-related issues, UNFPA coordinates closely with government agencies, local partners, and humanitarian clusters to ensure alignment of priorities, coordination, and avoid duplication of efforts.

Additionally, fast-track procedures under UNFPA's Emergency Policy and Procedures (EPP) and LTAs will be applied to expedite all logistical and administrative processes related to readiness, anticipatory action, and early response.

UNHCR

UNHCR maintains operational readiness through partnerships with government and local actors, enabling a rapid and timely response to sudden-onset shocks. Pre-existing coordination and communication mechanisms, including community-based early warning and information-sharing systems, allow UNHCR to disseminate timely alerts and engage immediately with affected populations and partners when risks escalate or a crisis occurs. In addition, UNHCR maintains core relief item stockpiles that can be quickly mobilized to support persons with specific needs and complement protection interventions.

As the Lead Agency of the Protection Cluster, UNHCR ensures that protection analysis and community feedback inform multi-sectoral response planning, particularly for evacuation processes, temporary accommodation centers, and service delivery modalities. UNHCR works closely with cluster members to support protection mainstreaming across sectors and to promote consistent application of protection principles and to ensure that results in effective outcomes.

Accountability to affected populations is integrated from the outset through the establishment of accessible feedback and complaint mechanisms, supporting informed and safe decision-making, early identification of emerging risks, and adaptive response measures during both the anticipatory and early response phases.

UNICEF

UNICEF maintains partnerships with a variety of government and NGO (both local and international) partners and has long term agreements (LTAs) for procurement and transport of goods. Through these agreements, UNICEF is able to quickly jump-start activities to allow for anticipatory actions to be completed. Moreover, UNICEF has stocks of emergency supplies prepositioned in four locations across the country, namely Maputo, Beira, Nacala and Pemba that can be deployed ahead of the storm to ensure timely response.

WFP

For the dissemination of early warning messages, WFP has worked with CENOE to ensure operational readiness of the INGD-led early warning platform. This includes the preparation of message templates and pre-registration of phone numbers of relevant focal points in each province. Furthermore, INGD has established contracts with radios to ensure early warnings can also be disseminated through different radio providers.

For evacuation, WFP has supported INGD to map potential temporary accommodation centers, safe evacuation routes and do community-level evacuation simulations ahead of the cyclone season.

For anticipatory food assistance, WFP has worked with INGD to map the capacity and prioritization of temporary accommodation centers in relevant locations. Furthermore, WFP has mapped and identified retailers that could provide commodity vouchers for early response phase..

Activities - Summary table

Table 2. Anticipatory actions by sector and agency

Objective	Sector	Agency	Outcome	Activity
Provide early warning messaging	Cross-cutting	IOM, UNFPA, UNICEF, WFP, UNHCR	Communities are aware of appropriate behaviors and available services to protect their lives and livelihoods	Dissemination of general and sector-specific early warning messages to at-risk communities through national government platforms
		IOM, UNICEF		Deployment of community teams to disseminate early warning messages
	Food security – Food assistance	WFP	Avoid a deterioration of food consumption by people in temporary accommodation centers	Provision of food assistance in temporary accommodation centers to meet food security needs
	WASH	UNICEF	Ensure adequate WASH services and prevent disease outbreaks	Set up of emergency WASH services (e.g. emergency latrines, solid waste management) and quick refresher training of community hygiene volunteers
	CCCM	IOM	Ensure adequate conditions for people in evacuation centers	Preparation of communal accommodation, including the quick maintenance of the temporary accommodation centers and pre-positioning of large-size communal tents, solar lights, information desks, and essential site management materials
Provide in-kind assistance	Protection - GBV	UNFPA	Ensure women and girls can maintain their personal hygiene and provide protection from gender-based violence (GBV) including Sexual Exploitation and Abuse (SEA)	Distribution of dignity kits and information on GBV ¹¹
	WASH	UNICEF	Ensure adequate WASH services and prevent disease outbreaks	Distribution of hygiene and water treatment products ¹²
	Shelter	IOM	Ensure people have access to safe shelter	Distribution of emergency NFI kits to affected households ¹³

¹¹ To be distributed to vulnerable women and girls at the household level after the action trigger and in accommodation centers as early response.

¹² To be distributed in accommodation centers at the household level after the action trigger and to affected households as early response.

¹³ Outside of CERF funding, UNHCR also prepositions and distributed core relief items (CRIs) to complement its protection response, targeting those with specific needs.

				Distribution of emergency shelter kits and/or tools for shelter reinforcement and/or repairs
Facilitate access to services	Protection - GBV	UNFPA	Ensure partners can effectively support prevention and case management of GBV	Provide orientations on SRH and the prevention and management of GBV for implementing partners
	Sexual and Reproductive Health		Ensure continuity of SRH and GBV response services	Set up of emergency SRH tents
				Delivery of inter-agency reproductive health kits and other SRH supplies to health facilities
				Deployment of mobile SRH/GBV teams
	CCCM	IOM	Protect at-risk infrastructures at displacement sites	Deployment of CCCM teams to support provision of tools and materials to the communities to strengthen key infrastructures and roads
	Health	UNICEF	Ensure continued access to health services	Deployment of mobile health teams
	Prepositioning and set up of emergency health kits and tents			
	WASH		Ensure adequate WASH services and prevent disease outbreaks	Protect and/or rehabilitate WASH infrastructure in public institutions and at community-level
	Protection	UNHCR	Communities and individuals at risk are informed and can access protection services to reduce harm and safeguard rights.	Awareness raising on PSEA, protection principles, human rights, GBV prevention and response among community leaders, activists, and community members
Rapid protection assessments and referral of people with specific needs. Carry out rapid protection assessments to identify groups at				

				heightened protection risk and assess immediate needs, risks, and gaps within affected communities.
				Protection desks: Establish mobile protection desks in cyclone-affected areas (including AAP and CFMs) to raise awareness of available protection services, complaint channels, and reporting procedures, and to provide basic psychological first aid.
	Logistics	WFP	At-risk communities are safely evacuated	Evacuation of people to temporary accommodation centers

6.Pre-agreed Financing

CERF

For this anticipatory action framework in Mozambique, the ERC has pre-agreed to allocate *up to* USD 4.5 million from the Central Emergency Response Fund (CERF) if triggers are reached. Further details can be found in the CERF application documents.

CERF will disburse funds once three conditions are met:

- Endorsement by the Resident and Humanitarian Coordinator of the framework and the CERF application package; and
- Endorsement by the Emergency Relief Coordinator of the finalized framework as well as the CERF agency project proposals and budgets; and
- Activation of the pre-agreed triggers once the framework is fully approved and operational for 2025/26 or 2026/27 cyclone season

CERF will disburse funds on a no-regrets basis as soon as the readiness, action or observational trigger is reached. Disbursement will take place only once during the period of validity of the framework. Upon activation of the first of any trigger, CERF will send out approval letters to the relevant agencies and subsequently will disburse all the funds. While a small portion of the fund can be used immediately upon disbursement for readiness activities, the portion of the funding for anticipatory action or early response can only be used if and when an action or observational trigger is reached. The amount of funding for readiness vs action/early response activities will be clearly defined in the pre-approved project proposals and budgets and communicated in the CERF approval letters. Distinguishing between these cost categories in advance is important given the different potential scenarios:

- If the readiness trigger is activated, agencies are authorized to use the funding allocated for readiness activities
- If the action trigger is activated, agencies are authorized to use all the allocated funding.
- If an observational trigger is activated without a prior action trigger, agencies are authorized to use all the funds.
- In case of a readiness trigger without subsequent action or observational trigger, the remaining funding will remain with agencies until the project end date. OCHA will convene partners to discuss options for the use of the remaining pre-arranged funding in future activations. If no additional trigger is reached by the end of the project period, the remaining funds will be reimbursed to CERF.
- If an action or observational trigger is reached without a prior readiness trigger, agencies are authorized to use all allocated funds, including those for readiness activities.

While approval letters will be sent out immediately following an activation, the administrative transfer of funds to agencies may be delayed by a few days. To avoid a delay in project implementation, agencies confirm their ability to frontload the resources required to initiate their response until the funding has been received.

Further details can be found in the CERF project documents and CERF communications. Any changes to the projects and budgets have to be approved by the CERF Secretariat as per usual practice.

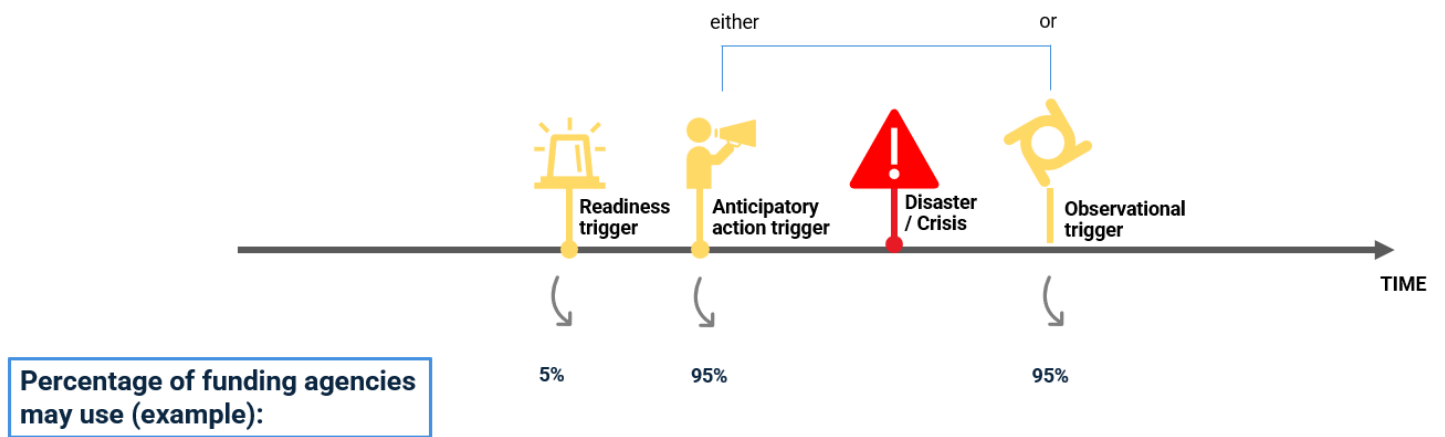


Figure 3. Overview of financing model with examples

Complementarity with other donors

This framework for anticipatory action is not limited to CERF-funded activities. UN agencies will provide internal funding in complementarity to increase the scale of this plan. Moreover, the Mozambique Red Cross has an Early Action Protocol in place backed by \$500,000 in funding from the DREF. Other donors are encouraged to pre-arrange funding to expand the scope of the framework.

The table below summarizes the funding available for this framework, including committed co-financing by agencies.

Table 3. Pre-arranged funding per sector

Agency	Sector	Number of people targeted	CERF funding	Agency co-funding	Total funding per agency
IOM	Shelter/NFI	50,000	\$819,000	0	\$1,050,000
	CCCM	70,000	\$231,000	0	
UNFPA	GBV	10,000	\$300,000	0	\$600,000
	SRH	30,500	\$300,000	0	
UNICEF	WASH	20,000	\$750,000	\$62,500	\$1,300,000
	Health	60,000	\$450,000	\$37,500	
UNHCR	Protection	58,000	\$300,000	\$35,000	\$335,000
WFP	Food Security	194,910	\$1,300,000	Up to \$864,664	\$2,387,074
	Logistics	194,910	\$50,000	Up to \$172,410	
TOTAL		194,910	\$4,500,000	\$1,172,074	\$5,672,074

Considerations

Both the geographical scope and the impact of cyclones are inherently difficult to predict despite the use of the best available scientific data. As a result, it is possible that an event causes or exacerbates existing humanitarian needs despite not formally reaching the thresholds required to utilize the pre-arranged funding. In this case, the RC/HC may request the ERC to make an allocation through CERF's Rapid Response window and use the projects already developed for the present framework, thus reducing the administrative burden for all partners and expediting the release of life-saving funds. This would not affect the amount of funding pre-arranged for this framework.

In general, having an anticipatory action framework supported by CERF neither precludes (nor guarantees) additional CERF Rapid Response funding to a country for the same or other shocks.

7. Learning

This framework offers significant opportunities to both generate and apply learning, thus contributing to the overall improvement of anticipatory action for sudden-onset shocks.

Monitoring and evaluation

Each agency will use its existing monitoring & evaluation systems to collect and track data on implementation progress and outputs achieved. All findings will be shared. Partners will also explore the possibility of collaborating on a quantitative impact evaluation to further assess the benefits of anticipatory action compared to post-shock response.

8. Validity and future of the framework

The CERF funding for the present framework is pre-arranged for a period of two cyclone seasons (2025/2026 and 2026/2027). If the framework does not activate during this period, it may be extended subject to ERC endorsement. The framework also expires following an activation and may be renewed based on a request by the RC/HC and subject to ERC endorsement. Lessons learned from activations as well as programmatic reviews will inform framework extensions/renewals/revisions in collaboration with the national technical working group on anticipatory action.

9. Annex

Core principles

Each anticipatory action framework is tailored to the local context. OCHA has identified nine core principles that should apply to the framework in Mozambique:


- **Prioritizing a multi-sectoral approach:** Partners should prioritize multi-sectoral, co-targeted interventions, when possible, to maximize synergies and to achieve great impact.
- **Ensuring the Centrality of Protection:** In line with the IASC Centrality of Protection policy, and the principle of “leaving no one behind” (2030 Agenda), all partners implementing anticipatory interventions have the responsibility to ensure that their response will not aggravate the exposure of communities to risks of violence, insecurity, extortion and exploitation. Anticipatory actions must also ensure that they benefit all communities (local communities, displaced communities, returnees, and refugees) based on their needs, with due attention given to obstacles linked to gender, age, disability or social affiliation.
- **Ensuring gender equality is central to inclusive and accountable anticipatory action:** In line with IASC Policy on Gender Equality and the Empowerment of Women and Girls in Humanitarian Action, all partners are responsible and accountable to ensure humanitarian action, including anticipatory action is: rights-based; recognizes gender-based and intersectional needs, as well as potential gender-based discrimination in access to resources and services; facilitate leadership and contribution of crisis-affected women and girls in the planning, implementation, monitoring and evaluation of anticipatory actions and early response, that directly impact their lives and those of their dependents and wider communities.
- **Promoting accountability to affected populations and the Protection from Sexual Exploitation and Abuse (PSEA):** Partners engaged in the implementation of the anticipatory action framework are responsible for the integration of accountability to affected populations approaches in their activities. This includes making all efforts to solicit, hear, and act upon the voices and priorities of affected people (including the most marginalized and at-risk women, men, girls and boys) in a coordinated manner, before, during, and after anticipatory action. It also means ensuring that community feedback leads to corrective action in future anticipatory action.
- **Supporting localization:** All partners involved in the implementation of this framework are expected to honor the HCT’s commitment towards localization. Equitable partnerships with local actors building upon their long-term relationships and trust with communities during anticipatory action are crucial.
- **Engaging in partnerships:** Collaboration across humanitarian actors is key to ensuring that all sectors are engaged, and that assistance is mobilized according to the AA framework.
- **Generating development and climate adaptation co-benefits:** Pilot participants are encouraged to consider how financing for anticipatory action can complement financing for development by reducing suffering and addressing the root causes of problems while supporting adaptation to climate change.
- **Capturing learning:** Monitoring, evaluation and learning activities should be embedded at every phase of the development and implementation of the AA framework.
- **Striving for integration:** The framework seeks to integrate the anticipatory action activities into the existing humanitarian architecture and to foster linkages with long term programming, including resilience and development initiatives.

Evaluation of trigger performance


In order to estimate the performance of the proposed trigger, the historical forecasts have been analyzed in combination with data on past CERF allocations, the available impact data on number of people affected and the national flood exposure up to 10 days after cyclone landfall from FloodScan, as reported in Figure 4. Despite the data limitations reported in the caption of the figure it is possible to see that the combination of these triggers is able to capture almost all the historical cyclones with the highest number of people affected or for which CERF funding was made available. The main outliers are mainly represented by cyclones only reaching the readiness trigger due to the large uncertainty of the forecasts beyond 72 hours. The observational rainfall trigger for which the framework allows for an activation to be “stopped” by the RC/HC or the CERF Secretariat as described in the activation protocol, can be corroborated by the maximum flood exposure from FloodScan data. Notable exceptions, cyclones Dando, Haruna and Kenneth, are explained below.

storm	season	Readiness	Action	Observational Wind Speed	Observational Rainfall	Total Affected	CERF Allocations	Max Flood Exposure
IDAI	2019	True	True	True	True	1,628,167	14,018,121	364,594
FREDDY	2023	True	True	True	True	1,230,691	9,995,213	723,677
DINEO	2017	False	True	True	False	750,102	2,000,095	104,921
GOMBE	2022	False	True	True	True	736,015	4,018,682	390,913
ELOISE	2021	True	True	False	False	481,901		209,013
CHIDO	2025	True	True	True	False	453,971	3,999,970	85,715
KENNETH	2019	False	True	True	True	400,094	9,964,907	99,798
JUDE	2025	True	True	True	True	385,000	6,053,738	369,965
DIKELEDI	2025	False	True	True	True	283,334		286,228
JOKWE	2008	False	False	False	False	220,013	548,913	131,490
ANA	2022	False	False	False	True	185,429		383,178
FAVIO	2007	False	False	False	False	162,770	1,070,014	235,054
FILIPO	2024	False	False	False	False	93,240		112,525
CHALANE	2021	False	False	False	False	73,254		92,530
DANDO	2012	False	False	False	False	40,042		411,064
IZILDA	2009	False	False	False	False	7,103		155,609
IRINA	2012	True	True	False	False	4,958		145,967
HARUNA	2013	False	False	False	False			439,464
DELIWE	2014	False	False	False	False			158,908
GUI TO	2014	False	False	False	False			
HELLEN	2014	False	False	False	False			133,171
CHEDZA	2015	False	False	False	False			
DESMOND	2019	False	False	False	True			223,396
GUAMBE	2021	False	False	False	False			221,936
JASMINE	2022	False	False	False	False			224,217


Figure 4. Historical validation of trigger performance. Main data limitations: No forecast data before 2010 (to evaluate the readiness and action trigger) for Jokwe and Favio, .

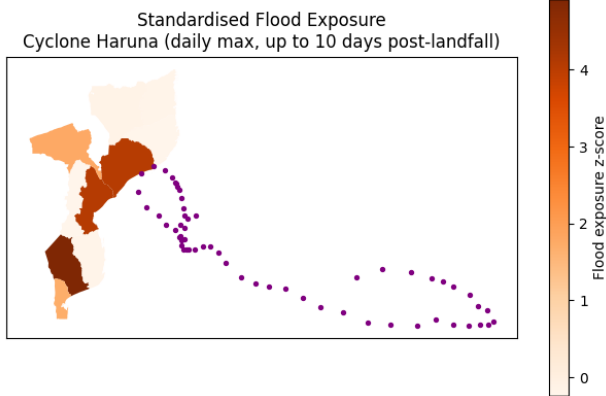

Rainfall associated with Haruna was limited, as the system barely made landfall. The observed flood exposure is therefore likely driven primarily by storm surge rather than rainfall. The cyclone's slow movement within the Mozambique Channel likely contributed to coastal impacts.

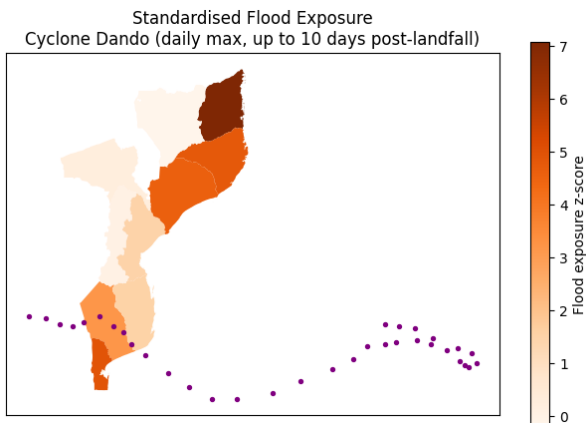

Reported flood exposure during Dando is largely influenced by a separate event further north affecting Zambézia and Sofala. While some flooding did occur in Gaza, national exposure totals appear inflated by impacts outside Dando's core affected area.

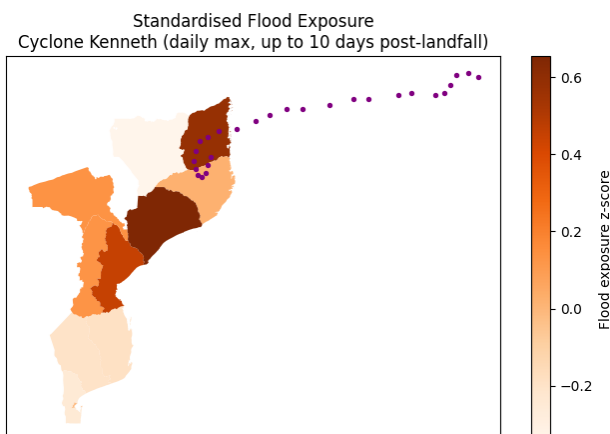

Rainfall from Kenneth was concentrated along the coast and met rainfall trigger thresholds. However, low population density in affected areas resulted in relatively low absolute exposure despite high rainfall. Relative exposure was nonetheless elevated in Cabo Delgado compared to its historical baseline.

The corresponding return periods for the trigger activation are reported below for each window and for the combined observational triggers.

Table 5. Return periods and data limitations

Trigger	Return period (years)	Comment
Readiness	3	Some historical forecasts missing
Action	4.2	Based on historical cyclone tracks
Observational (wind speed)	4.2	Based on historical cyclone tracks
Observational (rainfall)	5.2	Does not include the effect of the 'stop' mechanism
Observational (combined)	4.2	Some data limitations, partial estimation. Also doesn't include the effect of the 'stop' mechanism
Overall	4.2	


Trigger Monitoring Methodology

The exposed area is determined based on the forecast using the cone of uncertainty, accounting for the uncertainty in location, and the wind contours.

- Using the uncertainty cone and the forecasted center of the storm, the exposed area is calculated based on the wind speed at each forecast point and extends inland only as far as the storm's intensity meets the 119km/h threshold. The uncertainty cone is truncated at points where the storm intensity drops below the threshold, with interpolation between forecast points ensuring a smooth representation of wind speeds. Additional buffers are applied around the truncated uncertainty cone based on the maximum wind contour for the threshold at each point.
- For both the action and observational wind speed trigger, one threshold is applied, resulting in one exposed area for tropical cyclones.

An example is included below:

Forecasted Exposed Areas for CHIDO - Issue Time: 2024-12-14T18:00:00Z

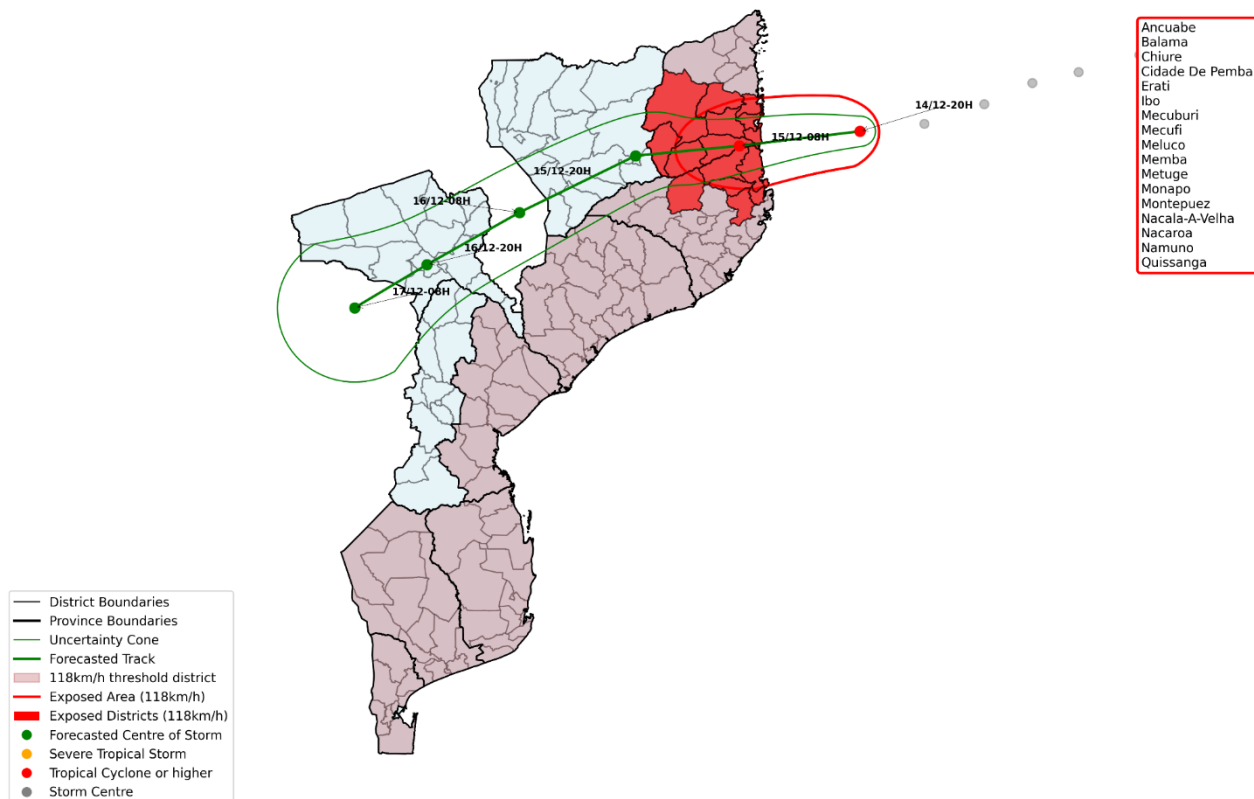

Draft activation messages

READINESS TRIGGER

Subject: Activation of Anticipatory Action framework for Cyclones in Mozambique: Readiness Trigger Threshold Reached

Dear Resident and Humanitarian Coordinator,

Dear Partners,

The readiness trigger threshold for the OCHA-facilitated anticipatory action framework for cyclones in Mozambique has now been reached. According to Météo-France La Reunion forecasts, Cyclone XXX is expected to impact the districts of XXX in XXX province with the intensity of a tropical cyclone.

Partners are requested to immediately commence the planned readiness activities in these districts as outlined in the endorsed framework.

Further updates will be provided as relevant.

If you have any questions regarding the monitoring or evaluation process or require additional support, please reach out to Antonio Rafael at antonio.rafael@un.org or Ioannis Kaffes at ioannis.kaffes@un.org.

For more information, you can refer to the anticipatory action framework here: [link]

Thank you for your continued commitment to anticipatory action.

Best regards,

OCHA Centre for Humanitarian Data

ACTION TRIGGER**BEFORE INGD CONFIRMATION**

Subject: Anticipatory Action framework for Cyclones in Mozambique: Action Trigger Threshold Reached (FRAMEWORK NOT YET ACTIVATED)

Dear Resident and Humanitarian Coordinator,

Dear Partners,

The action trigger threshold for the OCHA-facilitated anticipatory action framework for cyclones in Mozambique has now been reached. According to Météo-France La Reunion forecasts, Cyclone XXX is expected to impact the districts of XXX in XXX province with the intensity of a tropical cyclone.

Please note that the framework is **not yet activated**. The activation protocol requires INGD to convene the Technical Committee on Disaster Management (CTGD) to confirm the activation. A follow-up email will be sent once the framework has been activated.

If you have any questions regarding the monitoring or evaluation process or require additional support, please reach out to Antonio Rafael at antonio.rafael@un.org or Ioannis Kaffes at ioannis.kaffes@un.org.

For more information, you can refer to the anticipatory action framework here: [\[link\]](#)

Thank you for your continued commitment to anticipatory action.

Best regards,

OCHA Centre for Humanitarian Data

AFTER INGD CONFIRMATION

Subject: Activation of Anticipatory Action framework for Cyclones in Mozambique: Action Trigger Threshold Reached (FRAMEWORK ACTIVATED)

Dear Resident and Humanitarian Coordinator,

Dear Partners,

The action trigger threshold for the OCHA-facilitated anticipatory action framework for cyclones in Mozambique has now been reached. According to Météo -France La Reunion forecasts, Cyclone XXX is expected to impact the districts of XXX in XXX province with the intensity of a tropical cyclone. **The Technical Committee on Disaster Management (CTGD) was convened and has confirmed the activation.**

Partners are requested to immediately commence the planned anticipatory activities in these districts as outlined in the endorsed framework.

Further updates will be provided as relevant.

If you have any questions regarding the monitoring or evaluation process or require additional support, please reach out to Antonio Rafael at antonio.rafael@un.org or Ioannis Kaffes at ioannis.kaffes@un.org.

For more information, you can refer to the anticipatory action framework here: [\[link\]](#)

Thank you for your continued commitment to anticipatory action.

Best regards,

OCHA Centre for Humanitarian Data

OBSERVATIONAL TRIGGER

Subject: Activation of Anticipatory Action framework for Cyclones in Mozambique: Observational Trigger Threshold Reached

Dear Resident and Humanitarian Coordinator,

Dear Partners,

The observational trigger threshold for the OCHA-facilitated anticipatory action framework for cyclones in Mozambique has now been reached. According to Météo -France La Reunion forecasts, Cyclone XXX is expected to impact districts XXX in XXX province with intensity of a tropical cyclone OR rainfall in provinces XXX has exceeded the 120mm threshold.

Partners are requested to immediately commence the planned early response activities as outlined in the endorsed framework.

If you have any questions regarding the monitoring or evaluation process or require additional support, please reach out to Antonio Rafael at antonio.rafael@un.org or Ioannis Kaffes at ioannis.kaffes@un.org.

Further updates will be provided as relevant.

For more information, you can refer to the anticipatory action framework here: [link]

Thank you for your continued commitment to anticipatory action.

Best regards,

OCHA Centre for Humanitarian Data

Membership of the national technical working group on anticipatory action

Table 6. Members of the National Technical Working Group on Anticipatory Action in Mozambique

Institution	Institution Type
ADRA	INGO
Banco Mundial	Donor
CEDES	NNGO
COSACA (OxFam)	INGO
CVM	NNGO
Diakonie	INGO
DNAS (Direcção Nacional de Água e Saneamento)	Government
DNGRH	Government
FAO	UN Agency
FORCOM	Civil Society
FSC	Cluster
INAS	Government
ICS	Government

IFRC	INGO
INAM	Government
INGD - CENOE	Government
INGD-DPC	Government
INGD-DPM	Government
INGD-DSSA	Government
INGD - DARIDAS	Government
MAAP (Ministerio de Agricultura, Ambiente e Pescas)	Government
MINEDH (Ministerio de Educacao e Desenvolvimento Humano)	Government
MISAU	Government
OCHA	UN Secretariat
OIM	UN Agency
PMA	UN Agency
Radio Moçambique	government
Save the Children	INGO
SETSAN	Government
UEM-FAEF	Academia
UEM-FC	Academia
UNFPA	UN Agency
UNICEF	UN Agency
WHO	UN Agency
RCO	UN Coordination
Visão Mundial	INGO
